

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 2/13/2024
For Project: **Indian Springs Sewer Phase 2B**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
Contractor: Blankenship Contracting, Inc.
Designer: Alday-Howell Engineering Inspector: Dwayne Josey (850) 258-3386
Notice to Proceed: 8/1/2023 Award Date: 12/13/2022



Substantial Completion: 6/16/2024

Final Completion: 8/15/2024

The report is for the week of: Monday, 2/5/2024 thru Sunday, 2/11/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Installed laterals to right of way at stations 1041+70 and 1044+66 on Appalachee Trl.

Tuesday- Installed manhole 1040 and 42 LF of 8" gravity main from station 1040+40 to 1039+98 on Appalachee Trl.
Performed density testing at manhole 1040.

Wednesday- Installed 126 lf of 8" gravity main from station 1039+98 to 1038+76 on Appalachee Trl.

Thursday- Installed 94 lf of 8" gravity main from station 1038+76 to 1037+72 on Appalachee Trl.

Friday- Performed Low Pressure Air Testing on gravity main between manholes 1050 through 1040.

Saturday- No work at contractor's option.


Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	21%	Time Remaining (%):	42%
Invoiced to Date:	\$1,019,563.24	Weather days to date:	5
Original Contract Amount:	\$6,377,639.99		
Change Order Amount Approved:		Holiday days granted:	15
		Actual Days:	195
Remaining:	\$5,358,076.75	Days used with deduct:	175
Days to Substantial Completion:	300	Remaining to SC:	125
Days to Final Completion:	360	Remaining to FC:	185

A handwritten signature in blue ink, appearing to read "Rob B", is written over a horizontal line.

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)

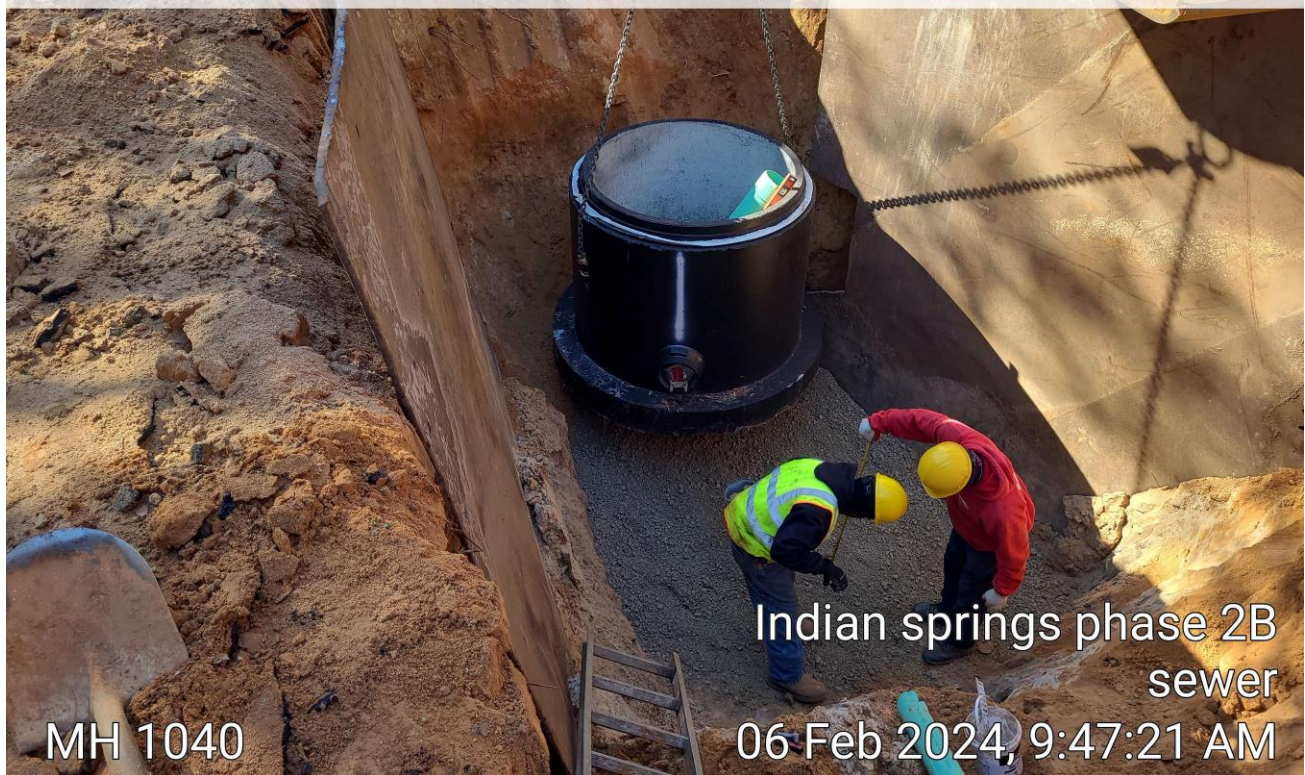



☀ 173° S (T) • 30.773637, -85.167082 ±8 m ▲ 21m



MH 1040

Indian springs phase 2B
sewer

06 Feb 2024, 11:08:48 AM



☀ 135° SE (T) • 30.77506, -85.166495 ±4 m ▲ 19m



Start Air test MH-1050 to
1046

Indian springs phase 2B
sewer
09 Feb 2024, 8:50:14 AM

