

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 2/28/2024
For Project: **Indian Springs Sewer Phase 2B**
NFWMD Const. Grant Agreement No. 20-036 AHE # 20-033
Contractor: Blankenship Contracting, Inc.
Designer: Alday-Howell Engineering Inspector: Dwayne Josey (850) 258-3386
Notice to Proceed: 8/1/2023 Award Date: 12/13/2022



Substantial Completion: 6/17/2024

Final Completion: 8/16/2024

The report is for the week of: Monday, 2/19/2024 thru Sunday, 2/25/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Set wet well for lift station.

Tuesday- Continued installation of lift station wet well. Performed density testing at wet well.

Wednesday- Installed manhole 1072 B, valve vault and 27 lf of 8" gravity main for lift station.

Thursday- Continued backfill and installation of lift station wet well. Performed density testing at wet well.

Friday- Installed grout to manhole benches throughout project. Located existing utilities for next week's construction.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	25%	Time Remaining (%):	37%
Invoiced to Date:	\$1,019,563.24	Weather days to date:	6
Original Contract Amount:	\$6,377,639.99		
Change Order Amount Approved:		Holiday days granted:	15
		Actual Days:	209
Remaining:	\$5,358,076.75	Days used with deduct:	188
Days to Substantial Completion:	300	Remaining to SC:	112
Days to Final Completion:	360	Remaining to FC:	172

A handwritten signature in blue ink, appearing to read "Rob B", is written over a horizontal line.

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)



☼ 340° NW (T) • 30.778583, -85.159476 ±3 m ▲ 15m



Preparing to set wetwell

Indian springs phase 2B
sewer
19 Feb 2024, 2:30:48 PM



☼ 96° E (T) • 30.778551, -85.15944 ±6 m ▲ 18m



Rebar for concrete

Indian springs phase 2B
sewer
19 Feb 2024, 3:53:11 PM



☼ 359° N (T) • 30.778594, -85.159479 ±18 m ▲ 15m



concrete

Indian springs phase 2B
sewer

19 Feb 2024, 4:14:32 PM




☼ 322° NW (T) • 30.778594, -85.159477 ±11 m ▲ 18m



MH. 1072 B

Indian springs phase 2B
sewer

21 Feb 2024, 10:15:52 AM

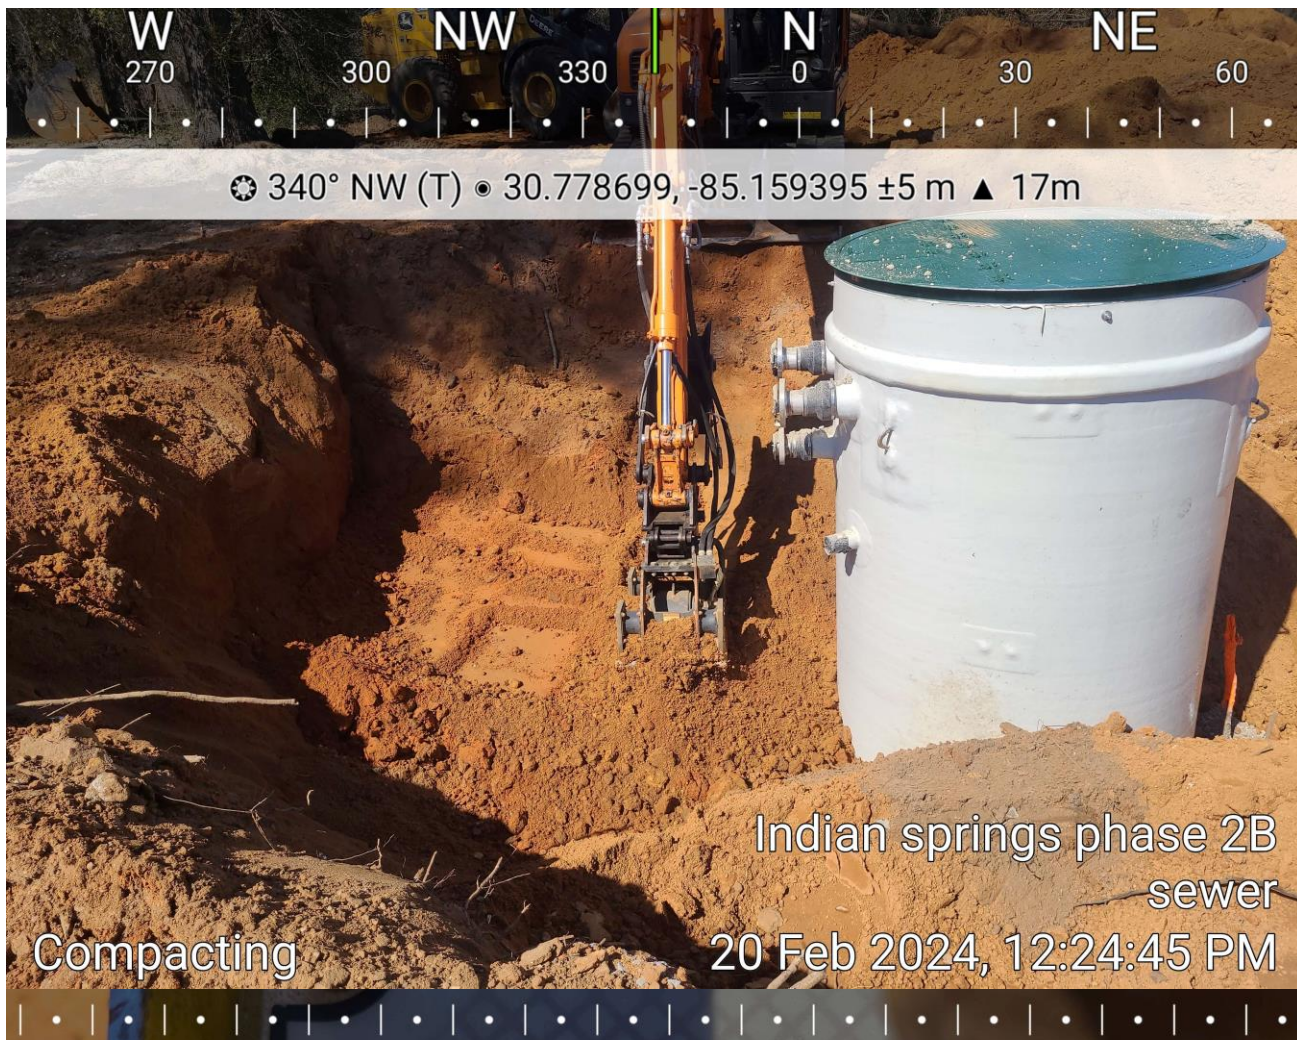



☼ 327° NW (T) • 30.778617, -85.159436 ±5 m ▲ 18m



Valve box

Indian springs phase 2B
sewer
21 Feb 2024, 3:01:00 PM



☼ 338° NW (T) • 30.778642, -85.159556 ±4 m ▲ 10m



Valve box

Indian springs phase 2B
sewer
22 Feb 2024, 10:36:45 AM
