

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 3/9/2023
For Project: **Blue Springs Road Sewer Extensions Phase 1**
NFWFMD Const. Grant Agreement No. 17-061 AHE # 17-062
Contractor: L & K Contracting, Inc.
Designer: Alday-Howell, Engineering Senior Inspector: Keith Prescott (850) 693-2471
Notice to Proceed: 9/27/2022 Award Date: 6/29/2022



Substantial Completion: 8/16/2023 Final Completion: 9/15/2023

The report is for the week of: Monday, 2/27/2023 thru Sunday, 3/5/2023

The contractor performed the following operations this week. Sub work is noted in parenthesis:

- Monday-** Installed 40LF and 80 LF of 10" PVC force main from Sta 201+46 to Sta 201+86 and from Sta 200+30 to Sta 201+00, 1-10" tee, 3-10" valves on Blue Springs Road.
- Tuesday-** Installed temporary erosion control in areas previously disturbed.
- Wednesday-** No work. Contractor's option.
- Thursday-** No work. Contractor's option.
- Friday-** No work. Contractor's option.
- Saturday-** No work. Contractor's option.
- Sunday-** No work. Contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	12%	Time Remaining (%):	54%
Invoiced to Date:	\$899,673.01	Weather days to date:	6
Original Contract Amount:	\$5,347,467.37 *	Holiday days granted:	17
Change Order Amount Approved:		Actual Days:	160
Remaining:	\$4,447,794.36	Days used with deduct:	137
Days to Substantial Completion:	300	Remaining to SC:	163
Days to Final Completion:	330	Remaining to FC:	193


* Budgeted amount is \$3,141,199.00. Contract amount \$5,347,467.37 contingent upon securing additional funding.

Approved:  Eric Worrell, PE, Project Administrator (850-526-2040)

N 0 30 60 90 120 SE
67°NE (T) 30.780777°, -85.191287° ±13ft ▲ 176ft



W 240 270 300 330 N
301°NW (T) 30.780834°, -85.191439° ±36ft ▲ 160ft

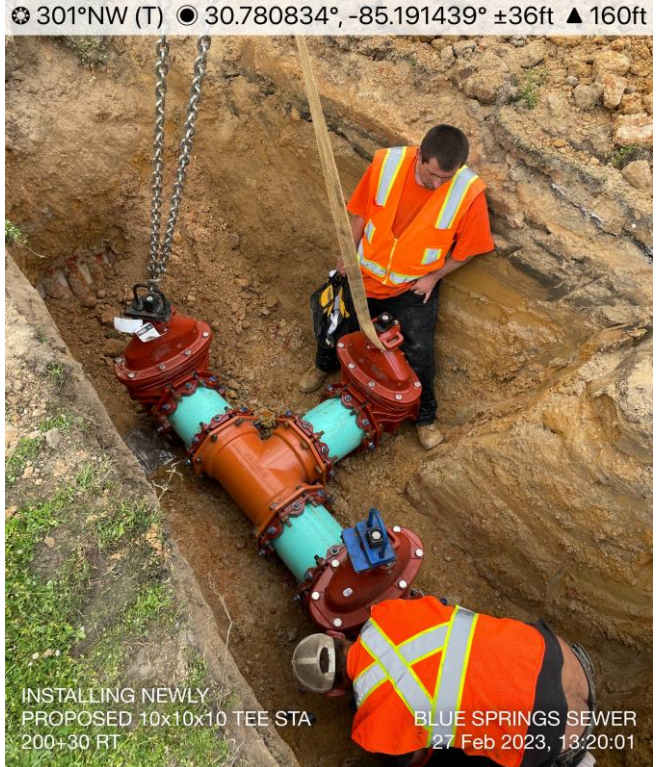

SW 210 240 270 300 330 W NW
267°W (T) 30.780792°, -85.191398° ±13ft ▲ 198ft



SW 210 240 270 300 NW
252°W (T) 30.780993°, -85.191071° ±22ft ▲ 143ft

