

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL

Prepared by: Alday-Howell Engineering, Inc.

Prepared on: 5/17/2023

For Project: **Blue Springs Road Sewer Extensions Phase 1**
NFWFMD Const. Grant Agreement No. 17-061 AHE # 17-062

Contractor: L & K Contracting, Inc.

Designer: Alday-Howell, Engineering Inspector: Jake Edenfield (850) 718-7233

Notice to Proceed: 9/27/2022 Award Date: 6/29/2022



Substantial Completion: 8/17/2023 Final Completion: 9/16/2023

The report is for the week of: Monday, 5/8/2023 thru Sunday, 5/14/2023

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Excavated lift station area.

Tuesday- Installed lift station and manhole 241A. Formed and placed reed bar in preparation for pour of lift station anti-flotation ring.

Wednesday- Formed and placed reed bar in preparation for pour of lift station and MH 241A anti-flotation rings.

Thursday- Poured lift station and MH 241A anti-flotation rings.

Friday- Backfilled compacted and performed density testing at lift station and MH 241A.

Saturday- No work. Contractor's option.

Sunday- No work. Contractor's option.

Engineer's remarks/Pending issues:


Percent Project Complete:	30%	Time Remaining (%):	31%
Invoiced to Date:	\$1,243,185.35	Weather days to date:	7
Original Contract Amount:	\$5,347,467.37 *	Holiday days granted:	17
Change Order Amount Approved:		Actual Days:	230
Remaining:	\$4,104,282.02	Days used with deduct:	206
Days to Substantial Completion:	300	Remaining to SC:	94
Days to Final Completion:	330	Remaining to FC:	124

*Budgeted amount is \$4,617,183.69. Contract amount \$5,347,467.37 contingent upon securing additional funding.

Approved:  Eric Worrell, PE, Project Administrator (850-526-2040)




⊗ 261°W (T) ● 30°46.982'N, 85°10.709'W ±13ft ▲ 0ft ⊗ 263°W (T) ● 30°46.989'N, 85°10.713'W ±95ft ▲ 155ft

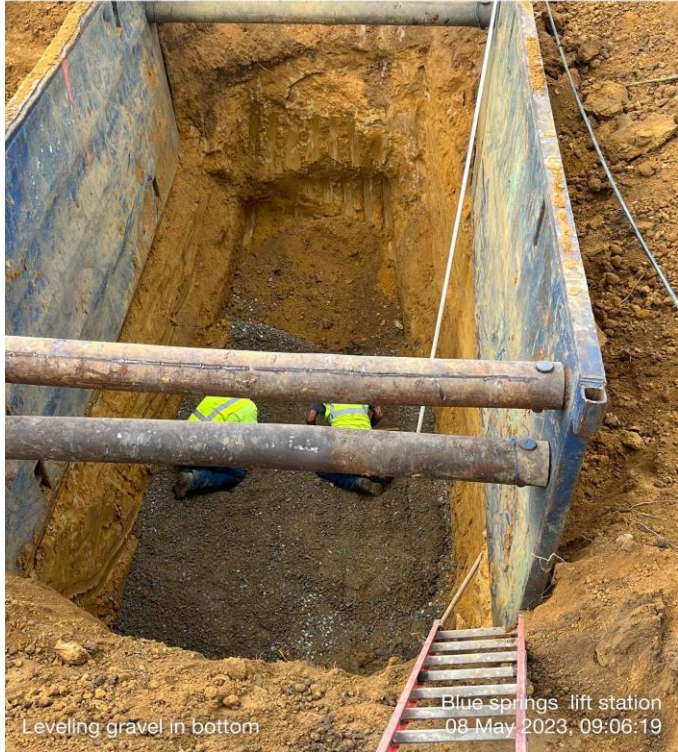

Leveling gravel in bottom
Blue springs lift station
08 May 2023, 09:06:19



Installing wet well
Blue springs lift station
08 May 2023, 09:35:50



⊗ 300°NW (T) ● 30°46.991'N, 85°10.706'W ±16ft ▲ 109ft ⊗ 39°NE (T) ● 30°46.989'N, 85°10.713'W ±9ft ▲ 106ft



Installing wet well rebar
Blue springs lift station
10 May 2023, 13:17:52



Concrete anchor
Blue springs MH241a
11 May 2023, 09:44:26
