

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 6/15/2023



For Project: **Blue Springs Road Sewer Extensions Phase 1**
NFWFMD Const. Grant Agreement No. 17-061 AHE # 17-062
Contractor: L & K Contracting, Inc.
Designer: Alday-Howell, Engineering Inspector: Jake Edenfield (850) 718-7233
Notice to Proceed: 9/27/2022 Award Date: 6/29/2022

Substantial Completion: 8/18/2023

Final Completion: 9/17/2023

The report is for the week of: Monday, 6/5/2023 thru Sunday, 6/11/2023

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Cleaned up construction site.

Tuesday- Installed 60 LF of 18" RCP from Sta 241+10 to 241+70.

Wednesday- Installed 60 LF of 18" RCP from Sta 241+10 to 241+70.(Acme- Closed west bound lane with temporary traffic signals)

Thursday- Installed 42 LF PVC 8" gravity main from Sta 241+10 to 241+52.

Friday- Installed 42 LF PVC 8" gravity main from Sta 240+82 to 241+10.

Saturday- No work. Contractor's option.

Sunday- No work. Contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	31%	Time Remaining (%):	22%
Invoiced to Date:	\$1,243,185.35	Weather days to date:	7
Original Contract Amount:	\$5,347,467.37 *		
Change Order Amount Approved:		Holiday days granted:	18
		Actual Days:	258
Remaining:	\$4,104,282.02	Days used with deduct:	233
Days to Substantial Completion:	300	Remaining to SC:	67
Days to Final Completion:	330	Remaining to FC:	97

* Budgeted amount is \$4,617,183.69. Contract amount \$5,347,467.37 contingent upon securing additional funding.

Approved:  Eric Worrell, PE, Project Administrator (850-526-2040)



NW N NE E
300 330 0 60 90 120
30°NE (T) 30°46.978'N, 85°10.726'W ±13ft ▲ 132ft




S SW W NW
180 210 240 270 300 330
254°W (T) 30°46.979'N, 85°10.727'W ±13ft ▲ 141ft






☼ 250°W (T) ● 30°46.980'N, 85°10.726'W ±9ft ▲ 136ft

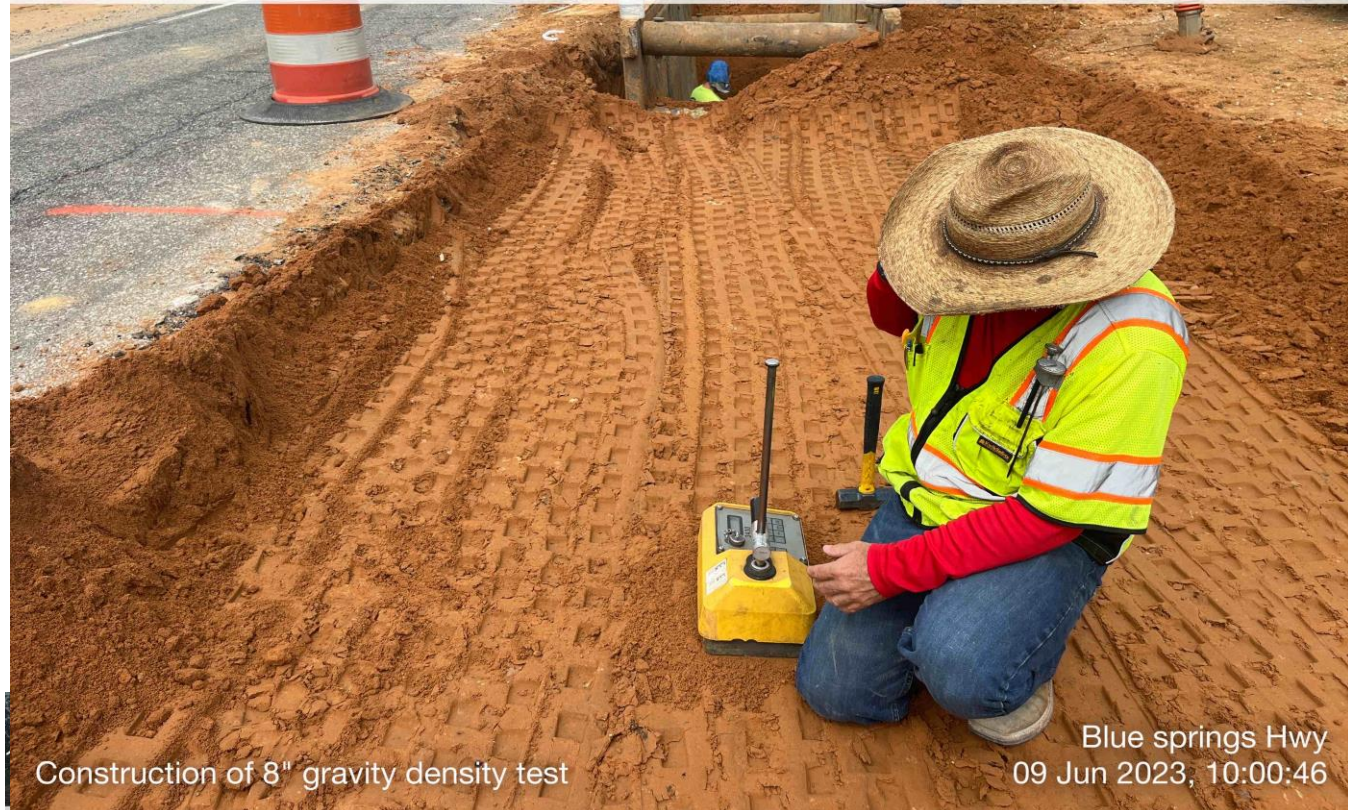

Construction of 8" gravity density test

Blue springs Hwy
09 Jun 2023, 10:00:46

☼ 272°W (T) ● 30°46.980'N, 85°10.729'W ±16ft ▲ 0ft

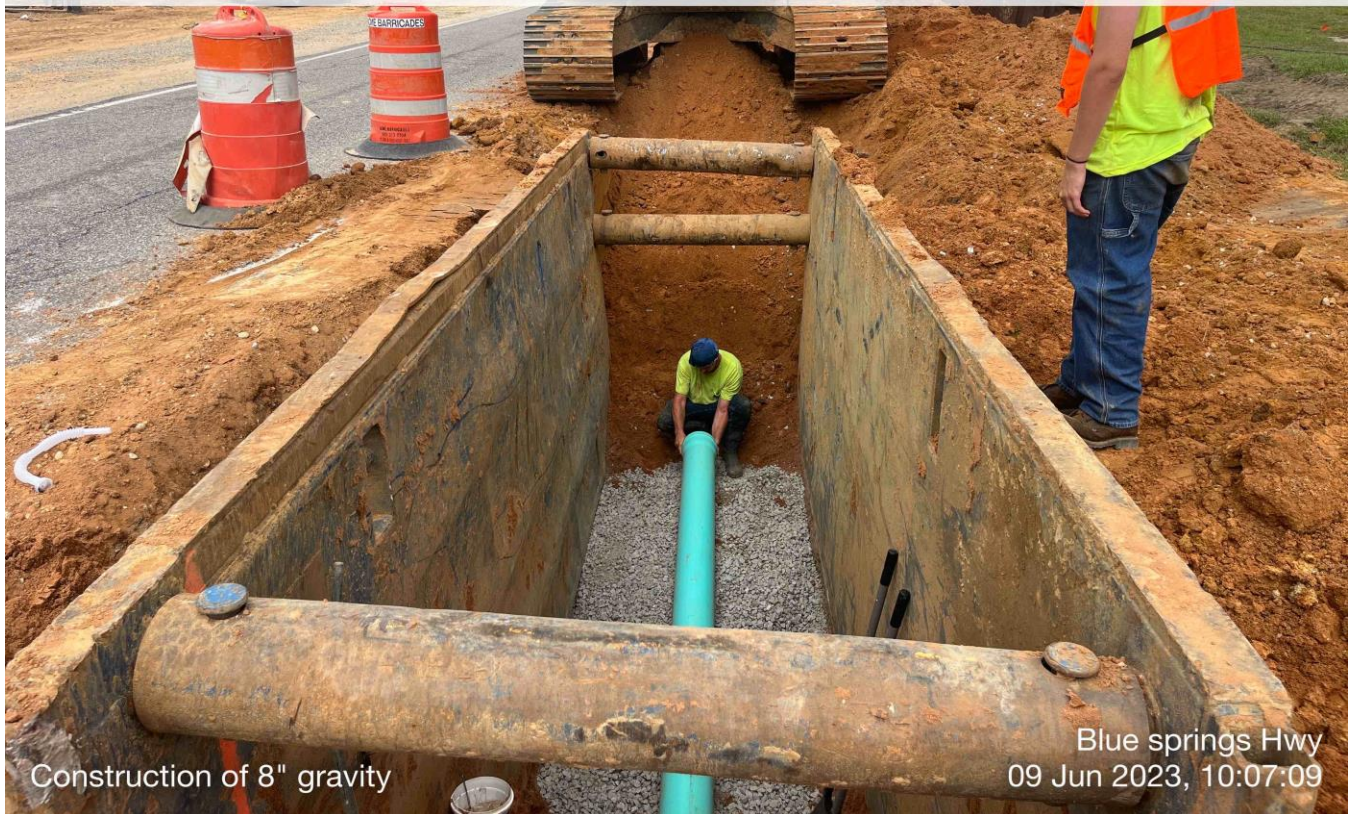

Construction of 8" gravity

Blue springs Hwy
09 Jun 2023, 10:07:09
