

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 7/5/2023
For Project: **Blue Springs Road Sewer Extensions Phase 1**
NFWFMD Const. Grant Agreement No. 17-061 AHE # 17-062
Contractor: L & K Contracting, Inc.
Designer: Alday-Howell, Engineering
Notice to Proceed: 9/27/2022



Inspector: Jake Edenfield (850) 718-7233

Award Date: 6/29/2022

Substantial Completion: 8/20/2023

Final Completion: 9/19/2023

The report is for the week of: Monday, 6/26/2023 thru Sunday, 7/2/2023

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Installed 98 LF PVC 8" gravity main and stubbed out 2-4" lateral from Sta. 234+90 to 235+83.

Tuesday- Installed 70 LF PVC 8" gravity main and stubbed out 1-4" lateral from Sta. 234+90 to 234+20.

Wednesday- Installed 37 LF PVC 8" gravity main and manhole 234 from Sta. 233+83 to 234+20.

Thursday- Removed asphalt prior to open trench pipe installation.

Friday- Installed 28 LF PVC 8" gravity main from Sta. 233+55 to 233+85.

Saturday- No work. Contractor's option.

Sunday- No work. Contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	32%	Time Remaining (%):	16%
Invoiced to Date:	\$1,243,185.35	Weather days to date:	9
Original Contract Amount:	\$5,347,467.37 *	Holiday days granted:	18
Change Order Amount Approved:		Actual Days:	279
Remaining:	\$4,104,282.02	Days used with deduct:	252
Days to Substantial Completion:	300	Remaining to SC:	48
Days to Final Completion:	330	Remaining to FC:	78

* Budgeted amount is \$4,617,183.69. Contract amount \$5,347,467.37 contingent upon securing additional funding.

Approved:  Eric Worrell, PE, Project Administrator (850-526-2040)



☀ 253°W (T) ● 30°46.965'N, 85°10.822'W ±13ft ▲ 149ft



Construction of 8" gravity (compaction)

Blue springs Hwy
26 Jun 2023, 09:39:26



☀ 281°W (T) ● 30°47.008'N, 85°10.532'W ±4333ft ▲ 122ft




Construction of 8" gravity (compaction)

Blue springs Hwy
26 Jun 2023, 09:51:00



☉ 255°W (T) ☉ 30°46.963'N, 85°10.843'W ±13ft ▲ 161ft

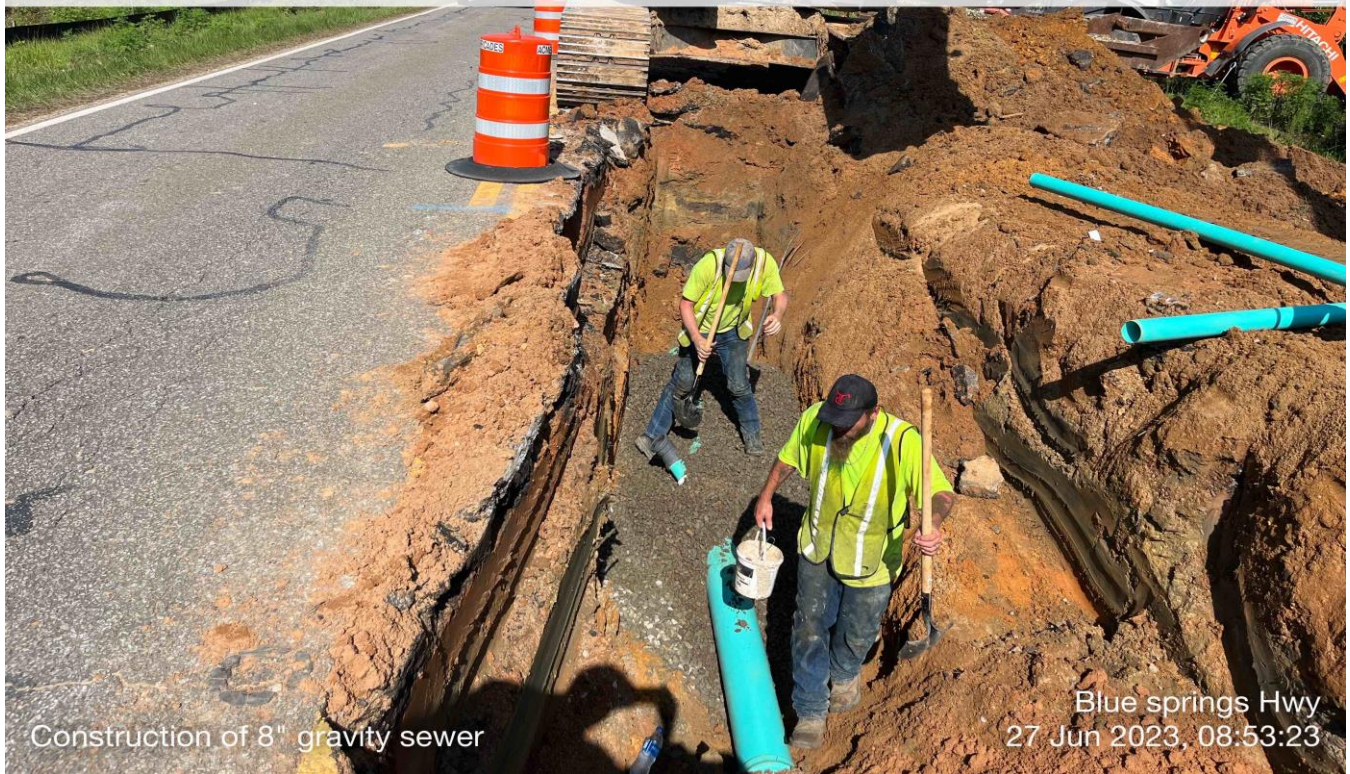

☉ 280°W (T) ☉ 30°46.956'N, 85°10.866'W ±36ft ▲ 149ft





☀ 70°E (T) ● 30°46.957'N, 85°10.862'W ±13ft ▲ 147ft



Construction of 8" gravity sewer (MH 234)

Blue springs Hwy
28 Jun 2023, 10:43:48



☀ 78°E (T) ● 30°46.957'N, 85°10.868'W ±9ft ▲ 162ft



Construction of 8" gravity sewer (MH 234)

Blue springs Hwy
28 Jun 2023, 13:00:28
