

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 7/25/2023
For Project: **Blue Springs Road Sewer Extensions Phase 1**
NFWFMD Const. Grant Agreement No. 17-061 AHE # 17-062
Contractor: L & K Contracting, Inc.
Designer: Alday-Howell, Engineering
Notice to Proceed: 9/27/2022



Award Date: 6/29/2022

Substantial Completion: 8/24/2023

Final Completion: 9/23/2023

The report is for the week of: Monday, 7/17/2023

thru Sunday, 7/23/2023

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Installed 42 LF PVC 8" gravity main.

Tuesday- Installed 28 LF PVC 8" gravity main.

Wednesday- Installed 28 LF PVC 8" gravity main.

Thursday- Installed 25 LF PVC 8" gravity main.

Friday- No work on project. Cleaned up laydown yard and performed service and repair on equipment.

Saturday- No work. Contractor's option.


Sunday- No work. Contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	33%	Time Remaining (%):	10%
Invoiced to Date:	\$1,523,976.94	Weather days to date:	11
Original Contract Amount:	\$5,347,467.37 *	Holiday days granted:	20
Change Order Amount Approved:		Actual Days:	300
Remaining:	\$3,823,490.43	Days used with deduct:	269
Days to Substantial Completion:	300	Remaining to SC:	31
Days to Final Completion:	330	Remaining to FC:	61

* Budgeted amount is \$4,617,183.69. Contract amount \$5,347,467.37 contingent upon securing additional funding.

Approved:  Eric Worrell, PE, Project Administrator (850-526-2040)

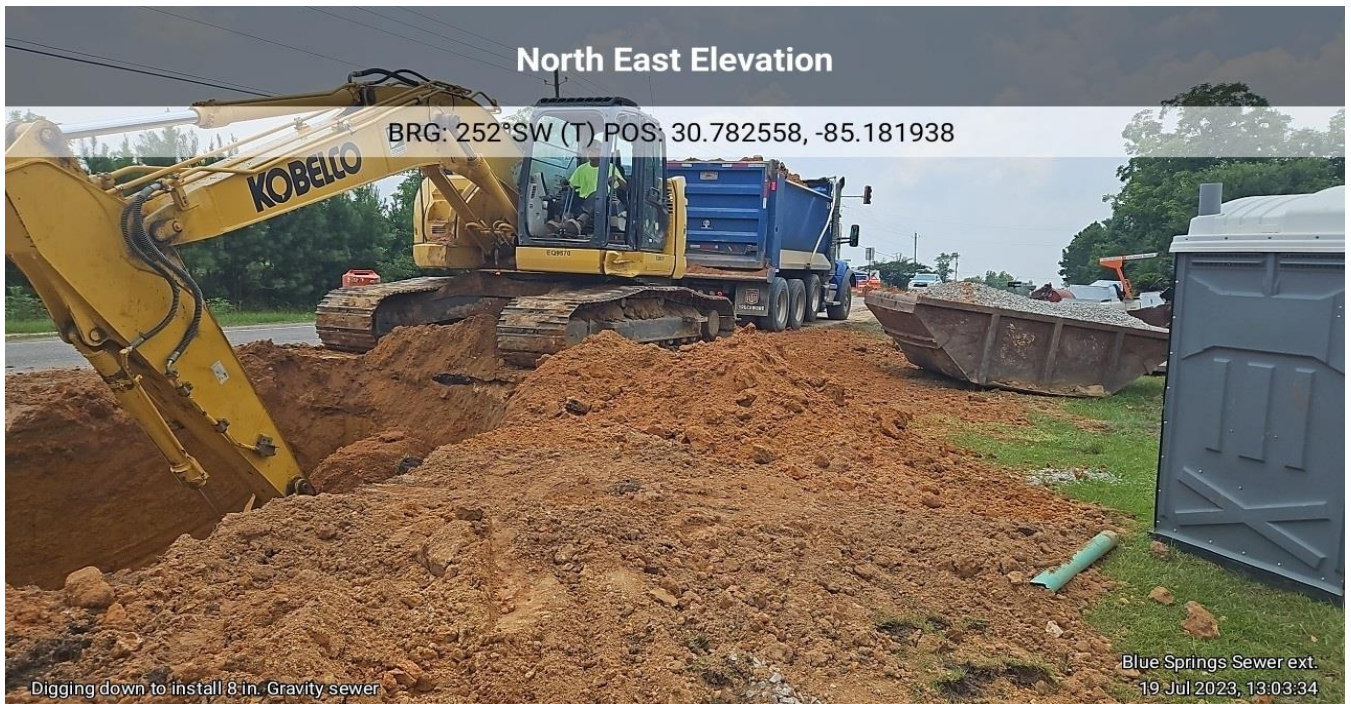

North Elevation

BRG: 200°S (T) POS: 30.782558, -85.181938



Adjusting the trench box

Blue Springs Sewer Extension
19 Jul 2023, 13:03:29
