

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL

Prepared by: Alday-Howell Engineering, Inc.

Prepared on: 10/27/2023

For Project: **Blue Springs Road Sewer Extensions Phase 1**
NFWFMD Const. Grant Agreement No. 17-061 AHE # 17-062

Contractor: L & K Contracting, Inc.

Designer: Alday-Howell Engineering Inspector: Brett Lawrence (850) 718-7233

Notice to Proceed: 9/27/2022 Award Date: 6/29/2022



Substantial Completion: 9/1/2023

Final Completion: 10/1/2023

The report is for the week of: Monday, 10/16/2023 thru Sunday, 10/22/2023

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Installed 60 LF 8" gravity main on Blue Spring Rd. Built up shoulder to allow for safe travel of traveling public.

Tuesday- Installed 84 LF 8" gravity main on Blue Spring Rd. Built up shoulder to allow for safe travel of traveling public.

Wednesday- Installed 70 LF 8" gravity main on Blue Spring Rd.

Thursday- Installed 70 LF 8" gravity main on Blue Spring Rd.

Friday- Installed 42 LF 8" gravity main on Blue Spring Rd.

Saturday- No work. Contractor's option.

Sunday- No work. Contractor's option.


Engineer's remarks/Pending issues:

Percent Project Complete:	37%	Time Remaining (%):	-17%
Invoiced to Date:	\$1,771,637.94	Weather days to date:	18
Original Contract Amount:	\$5,347,467.37 *		
Change Order Amount Approved:		Holiday days granted:	21
		Actual Days:	391
Remaining:	\$3,575,829.43	Days used with deduct:	352
Days to Substantial Completion:	300	Remaining to SC:	-52
Days to Final Completion:	330	Remaining to FC:	-22

* Budgeted amount is \$4,617,183.69. Contract amount \$5,347,467.37 contingent upon securing additional funding.

A handwritten signature in blue ink, appearing to read "Rob B", is written over a horizontal line.

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)

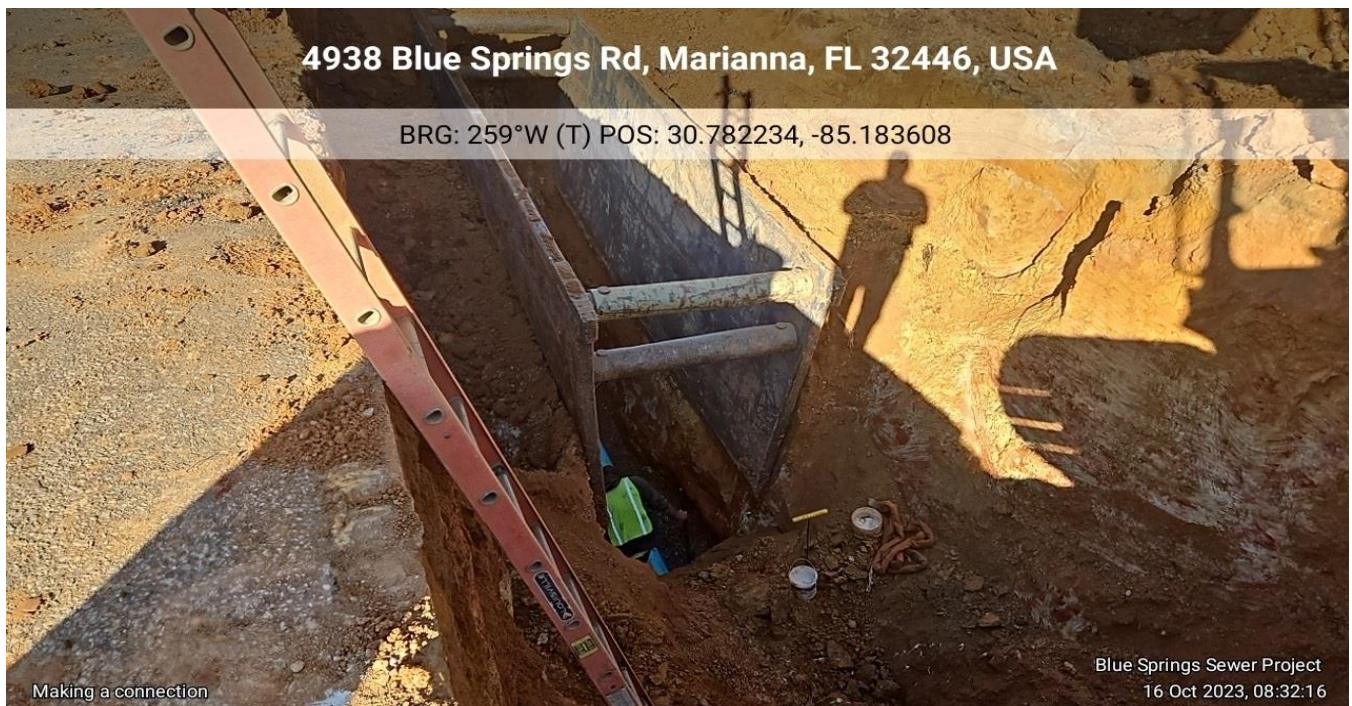



South East Elevation

BRG: 318°NW (T) POS: 30.781995, -85.184037



North East Elevation

BRG: 232°SW (T) POS: 30.78205, -85.184416

