

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL

Prepared by: Alday-Howell Engineering, Inc.

Prepared on: 11/29/2023

For Project: Indian Springs Sewer Phase 2B

NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033

Contractor: Blankenship Contracting, Inc.

Designer: Alday-Howell Engineering

Inspector: Dwayne Josey (850) 258-3386

Notice to Proceed: 8/1/2023

Award Date: 12/13/2022



Substantial Completion: 6/4/2024

Final Completion: 8/3/2024

The report is for the week of: Monday, 11/20/2023

thru Sunday, 11/26/2023

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Installed 70 LF of 8" gravity main on Appalachian Trl.

Tuesday- Cleaned up construction area.

Wednesday- No work due to holiday. Holiday day given.

Thursday- No work due to holiday. Holiday day given.

Friday- No work due to holiday. Holiday day given.

Saturday- No work due to holiday. Holiday day given.

Sunday- No work due to holiday. Holiday day given.

Engineer's remarks/Pending issues:

Percent Project Complete: 13%

Time Remaining (%): 63%

Invoiced to Date: \$493,937.16

Weather days to date: 3

Original Contract Amount: \$6,377,639.99

Change Order Amount Approved:

Holiday days granted: 5

Actual Days: 118

Remaining: \$5,883,702.83

Days used with deduct: 110

Days to Substantial Completion: 300



Remaining to SC: 190



Days to Final Completion: 360


Remaining to FC: 250

A handwritten signature in blue ink, appearing to read "Rob B", is positioned above a horizontal line.

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)

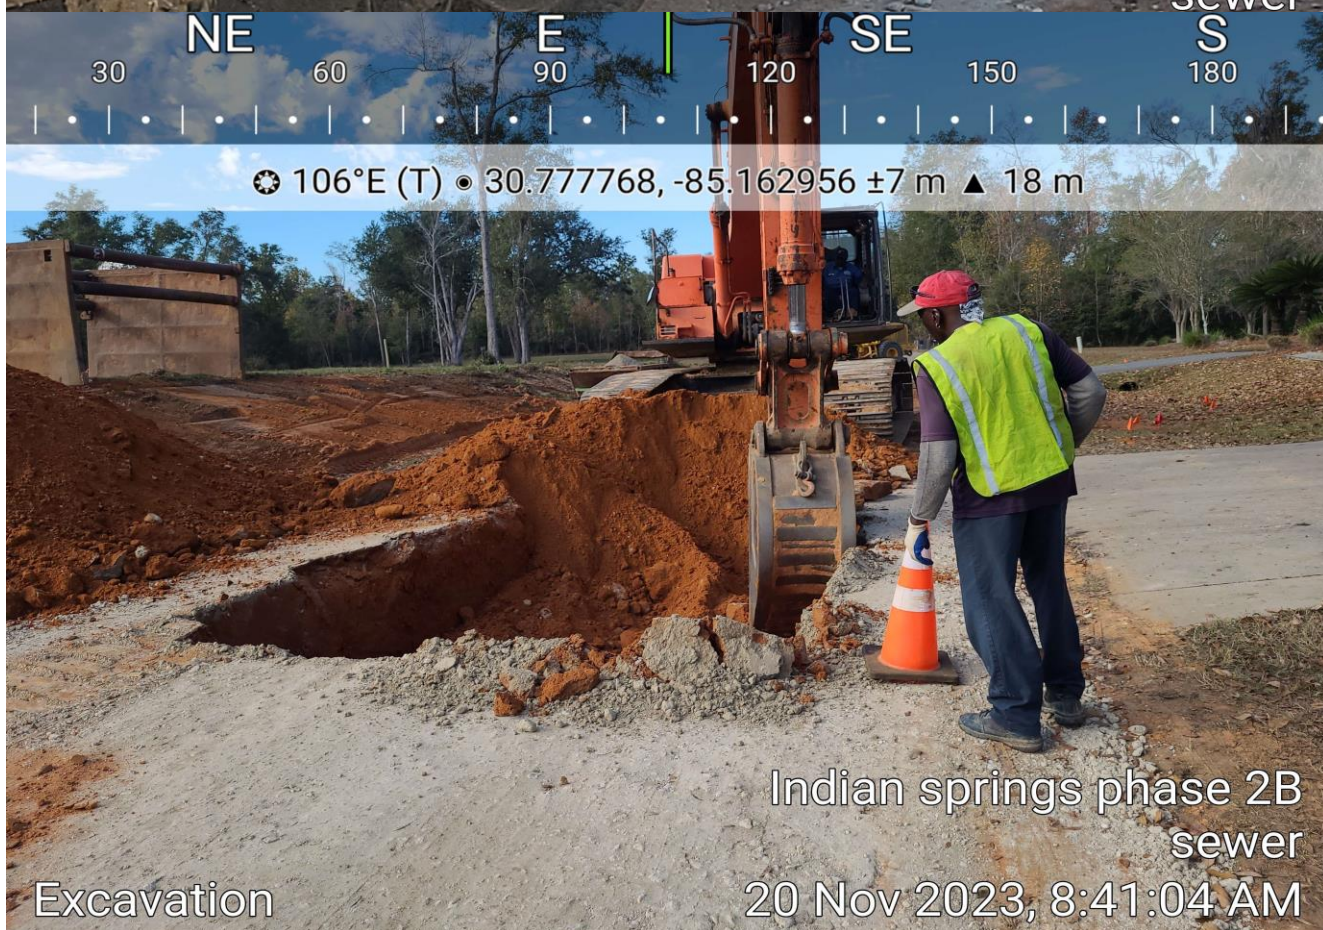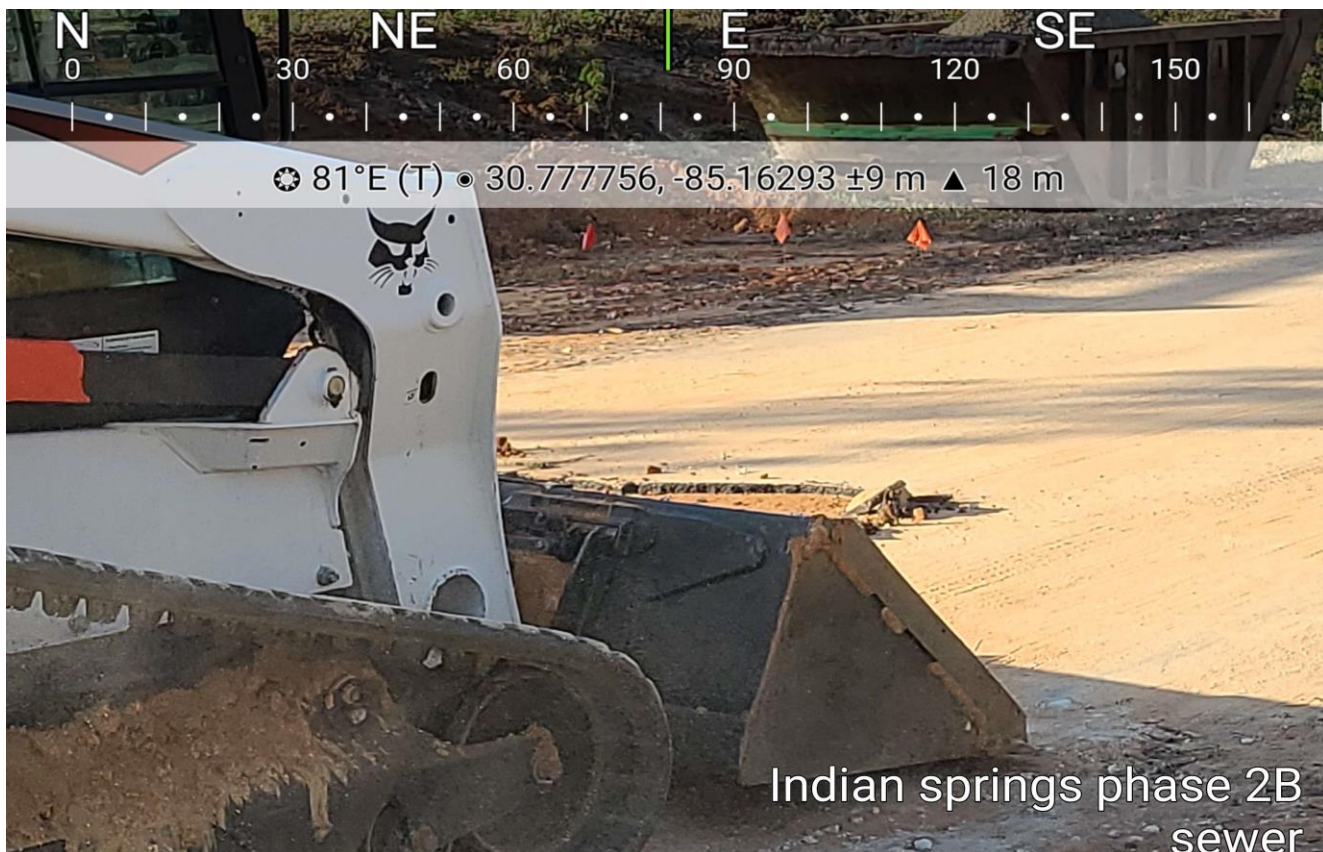

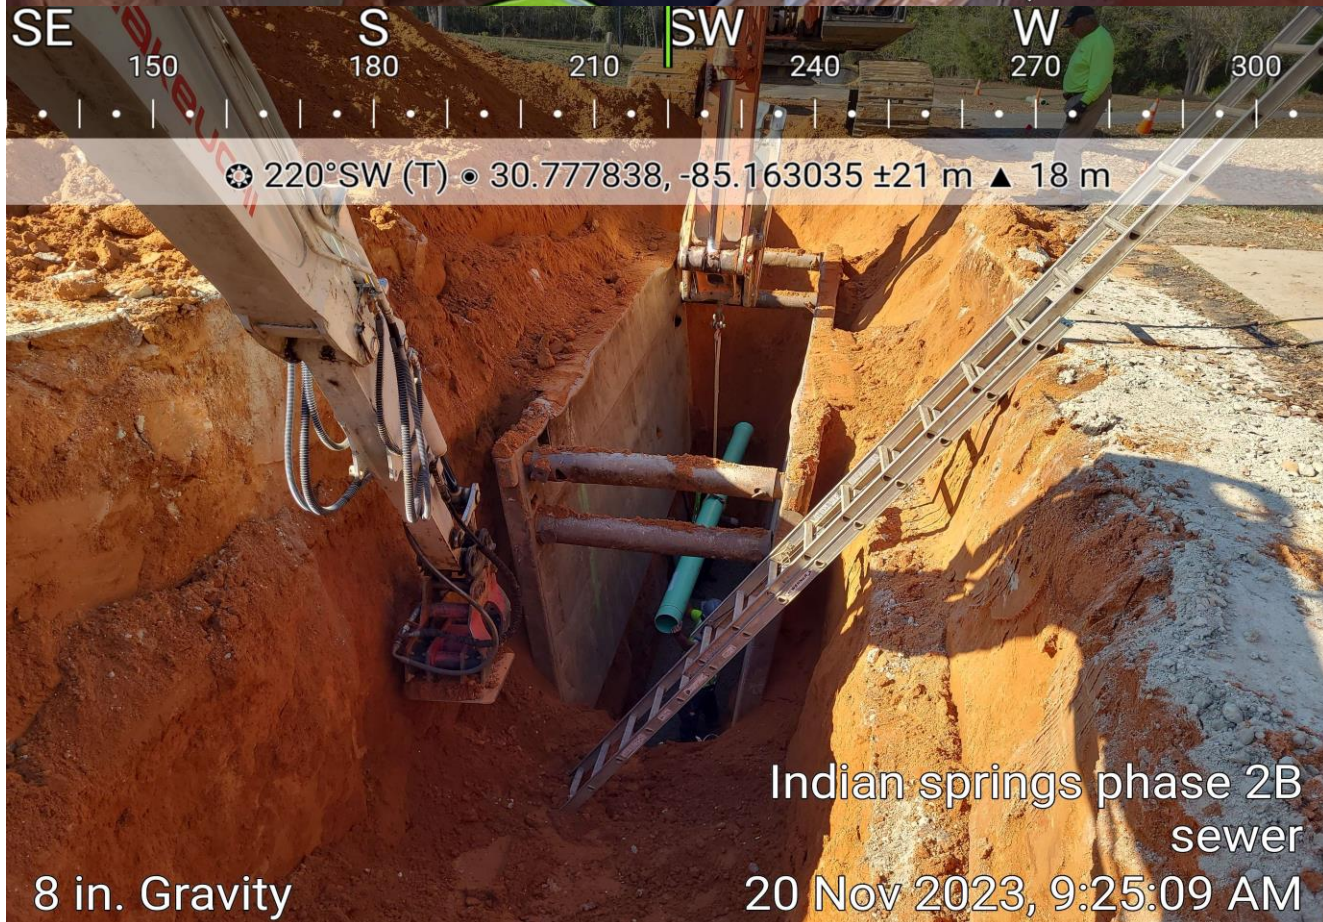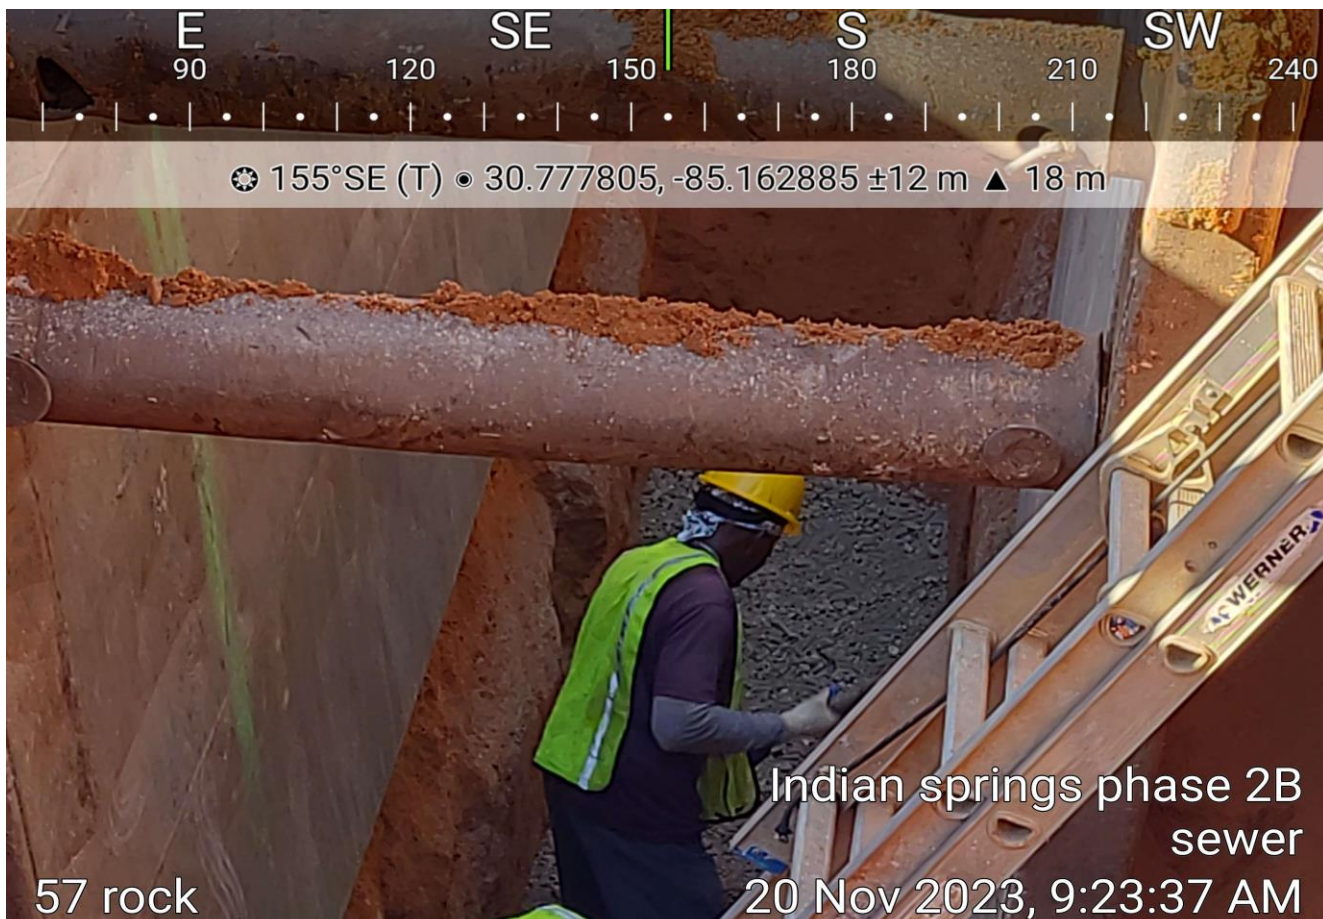

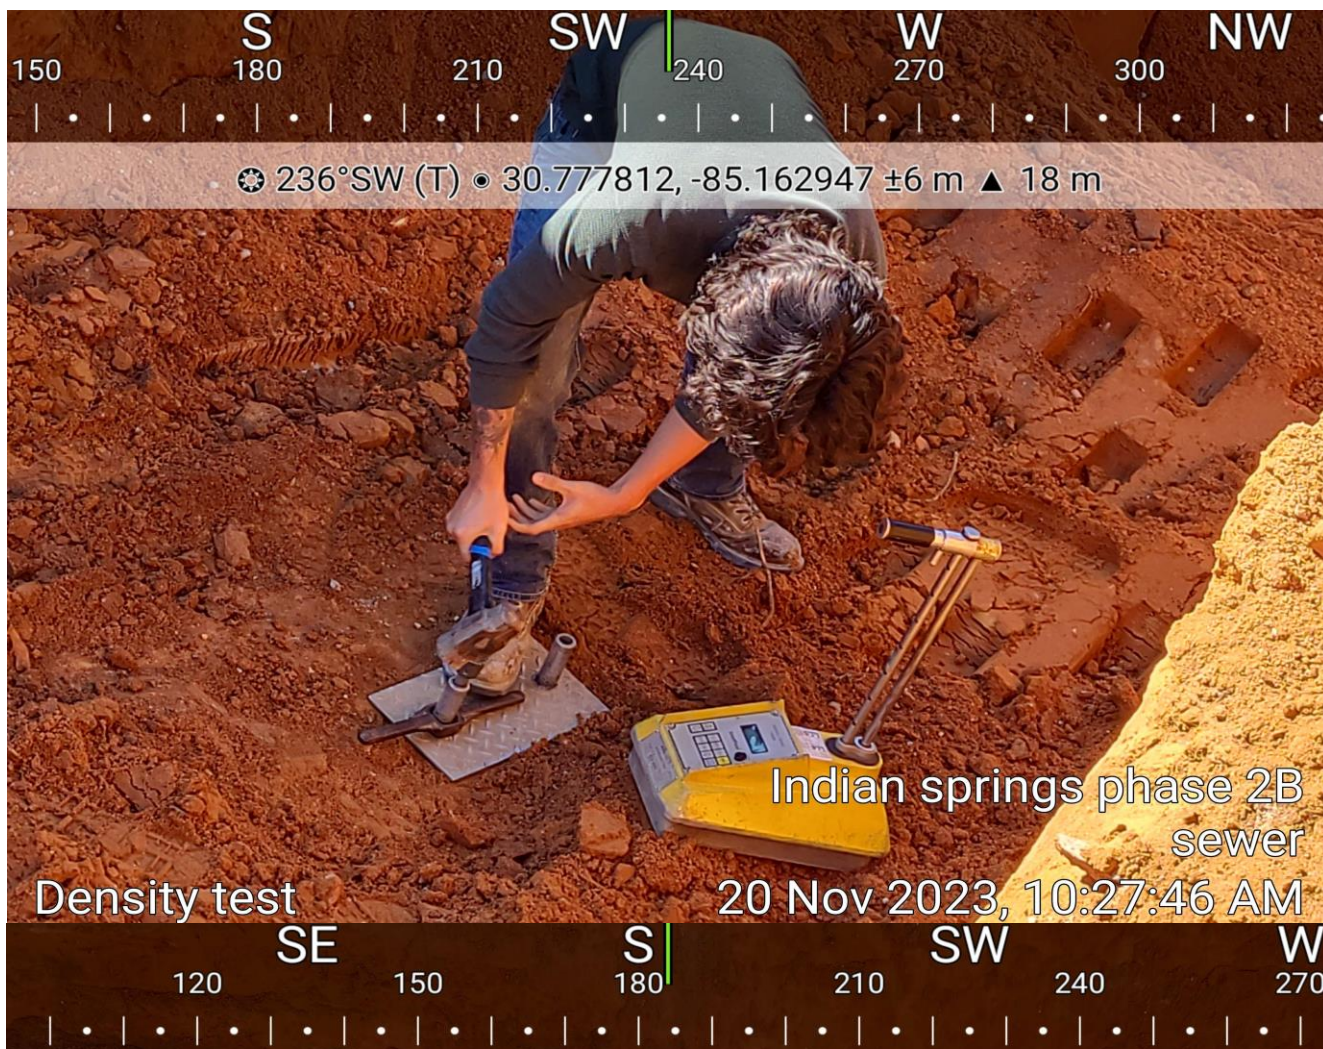

NE 60 90 E SE 120 150 S 180 210

☼ 131°SE (T) • 30.777855, -85.162918 ±7 m ▲ 20 m



NE 60 90 E SE 120 150 S 180 210

☼ 130°SE (T) • 30.777763, -85.16291 ±11 m ▲ 18 m

