

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL

Prepared by: Alday-Howell Engineering, Inc.

Prepared on: 12/5/2023

For Project: **Indian Springs Sewer Phase 2B**

NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033

Contractor: Blankenship Contracting, Inc.

Designer: Alday-Howell Engineering

Inspector: Dwayne Josey (850) 258-3386

Notice to Proceed: 8/1/2023

Award Date: 12/13/2022



Substantial Completion: 6/4/2024

Final Completion: 8/3/2024

The report is for the week of: Monday, 11/27/2023

thru Sunday, 12/3/2023

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Installed 84 LF of 8" gravity main on Appalachee Trl.

Tuesday- Installed 70 LF of 8" gravity main on Appalachee Trl.

Wednesday- Installed 42 LF of 8" gravity main on Appalachee Trl.

Thursday- Installed manhole 1058 & 9 LF of 8" gravity main on Appalachee Trl.

Friday- Cleaned up construction area.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete: 14%

Time Remaining (%): 61%

Invoiced to Date: \$493,937.16

Weather days to date: 3

Original Contract Amount: \$6,377,639.99

Change Order Amount Approved:

Holiday days granted: 5

Remaining: \$5,883,702.83

Actual Days: 125

Days to Substantial Completion: 300

Days used with deduct: 117


Remaining to SC: 183



Days to Final Completion: 360

Remaining to FC: 243

A handwritten signature in blue ink, appearing to read "Rob B", is positioned above a horizontal line.


Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)

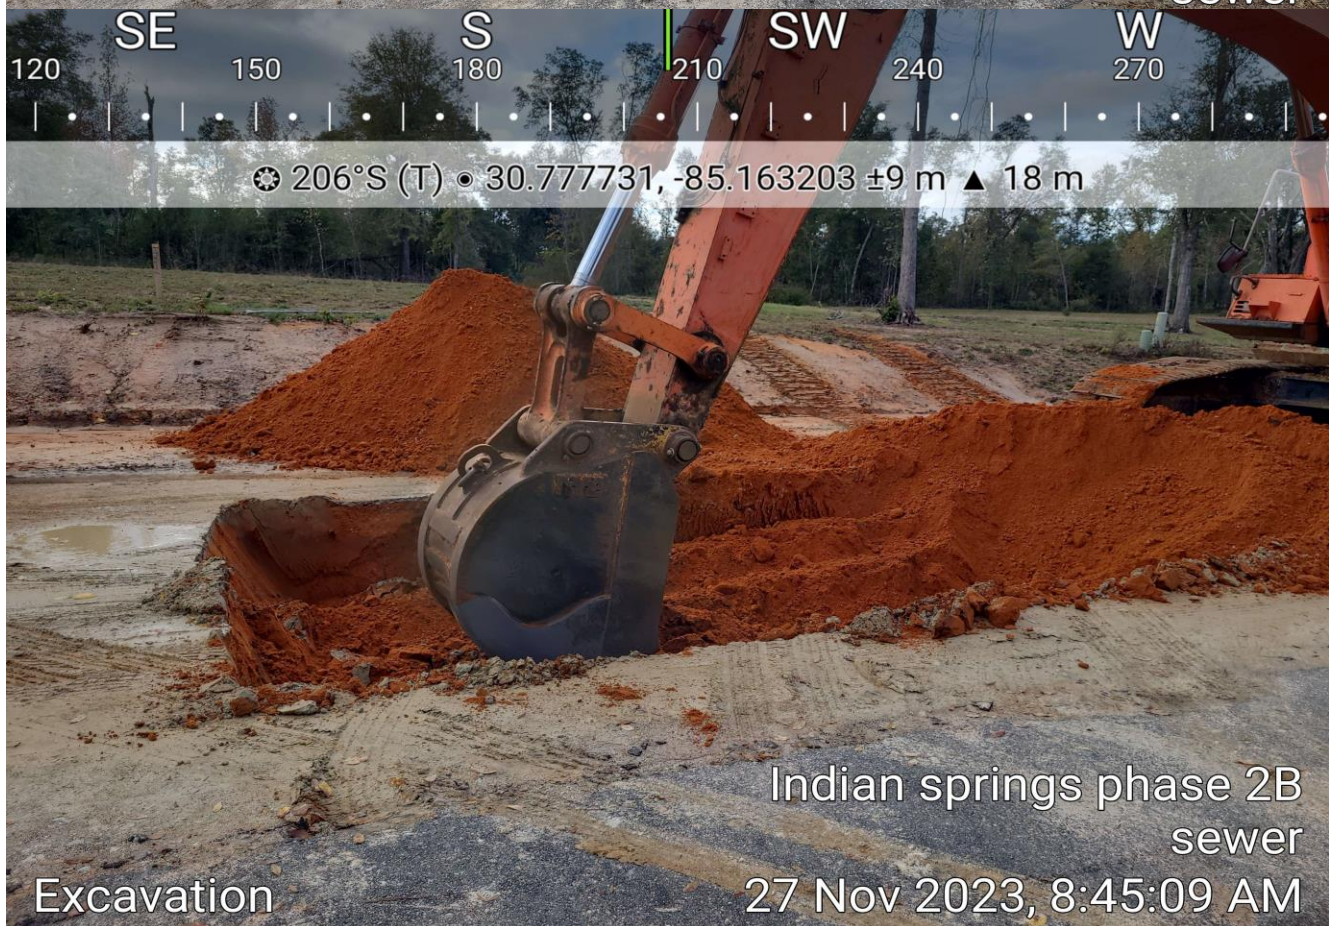

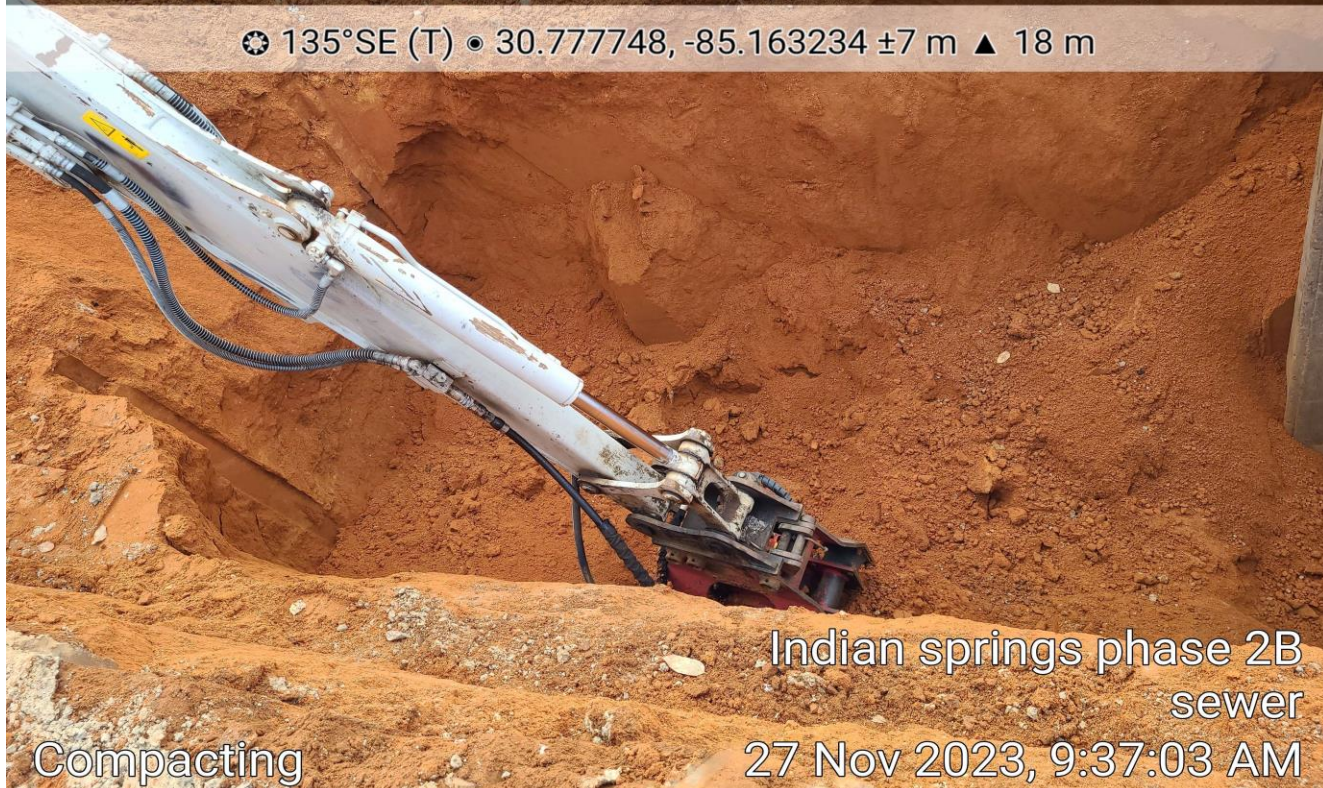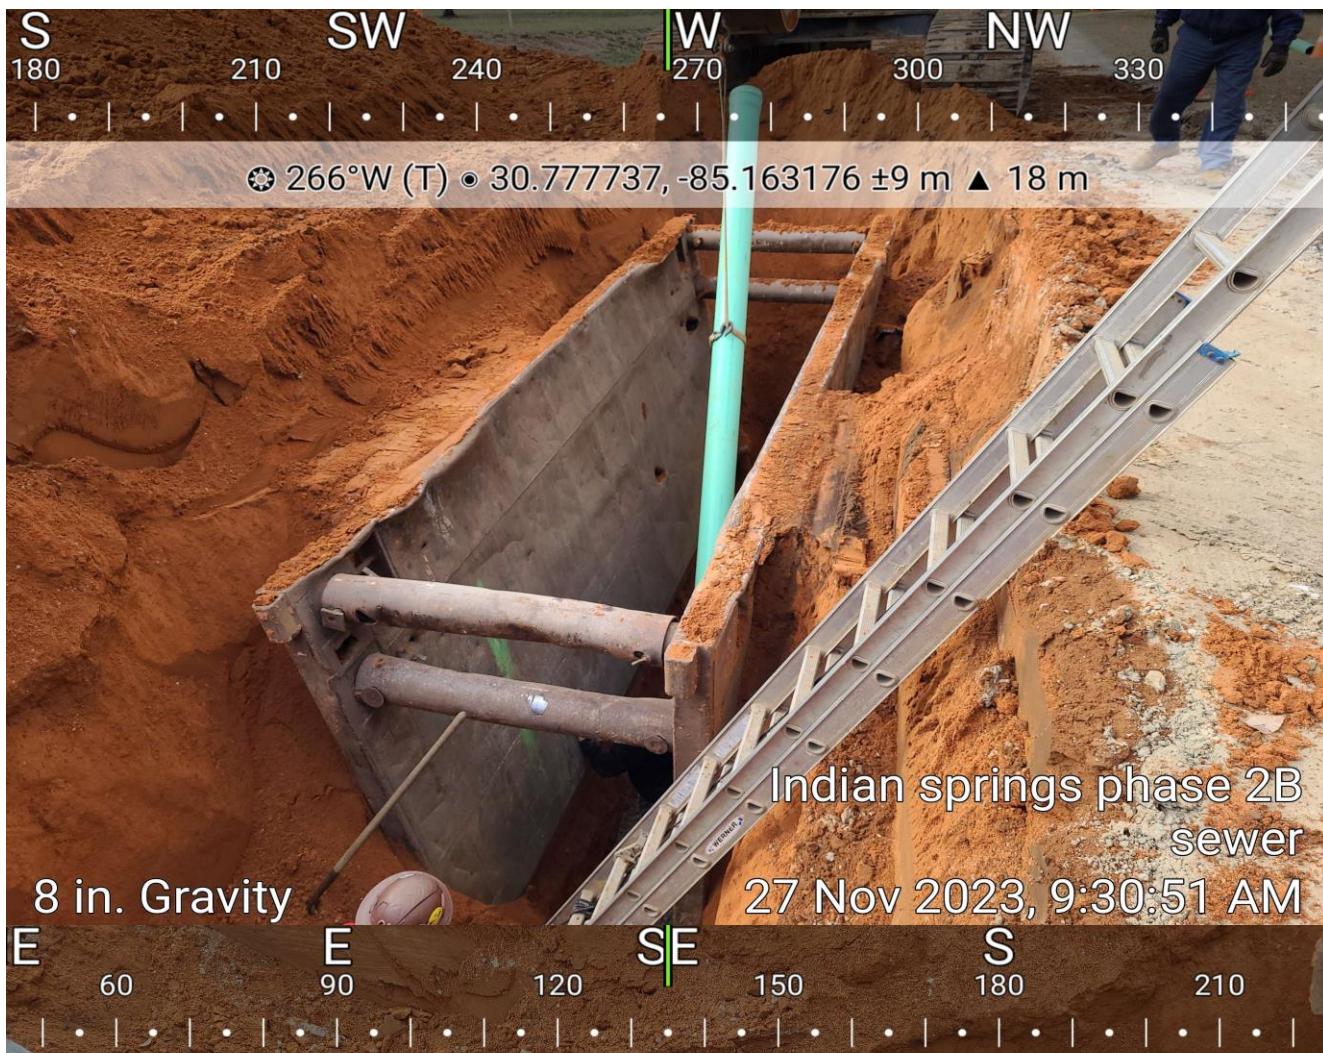



☀ 73°NE (T) • 30.777789, -85.163088 ±87 m ▲ 18 m

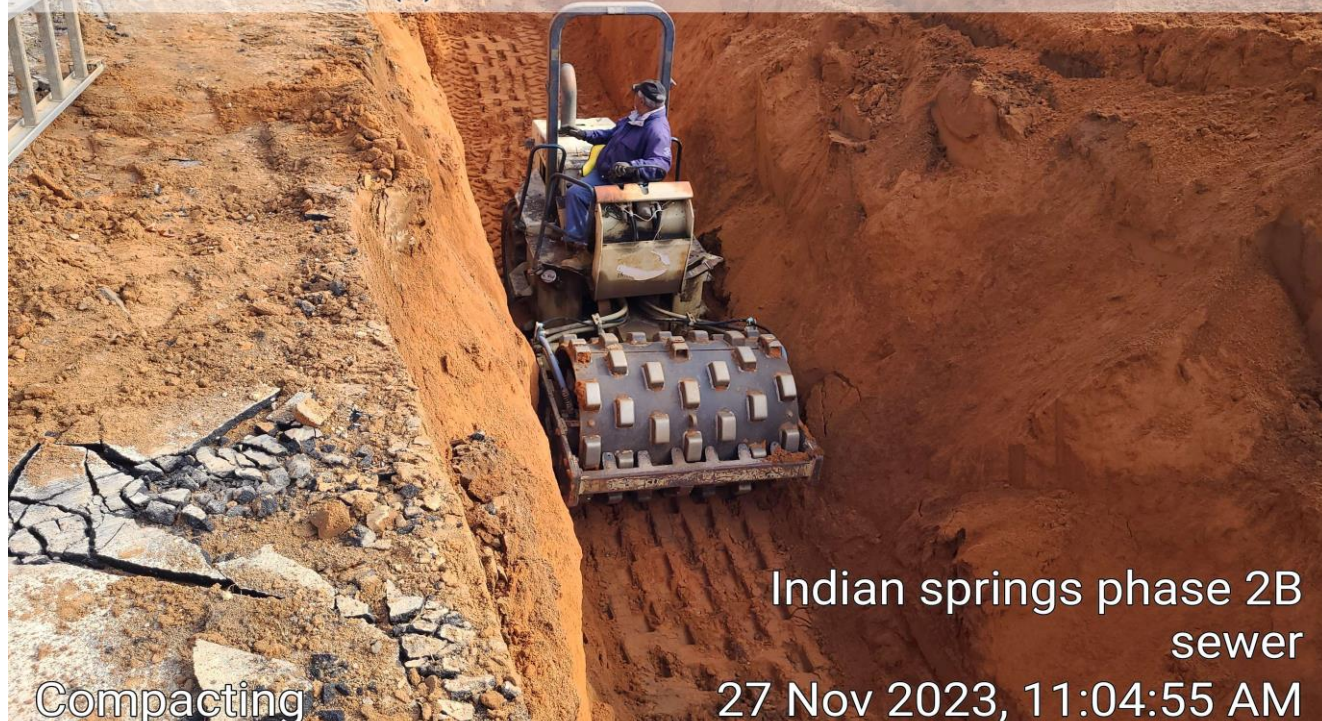

Indian springs phase 2B
sewer

Compacting

27 Nov 2023, 11:04:55 AM



☀ 174°S (T) • 30.777634, -85.163643 ±6 m ▲ 18 m



Indian springs phase 2B
sewer

57 rock

28 Nov 2023, 2:04:08 PM



⊗ 288°W (T) ● 30.777265, -85.163769 ±21 m ▲ -35 m



MH 1058

Indian springs phase 2B
sewer

30 Nov 2023, 2:33:21 PM



⊗ 321°NW (T) ● 30.777789, -85.163078 ±87 m ▲ 18 m



MH 1058

Indian springs phase 2B
sewer

30 Nov 2023, 3:19:07 PM
