

## CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL

Prepared by: Alday-Howell Engineering, Inc.

Prepared on: 12/13/2023

For Project: **Indian Springs Sewer Phase 2B**

**NFWMD Const. Grant Agreement No. 20-036** AHE # 20-033

Contractor: Blankenship Contracting, Inc.

Designer: Alday-Howell Engineering

Inspector: Dwayne Josey (850) 258-3386

Notice to Proceed: 8/1/2023

Award Date: 12/13/2022



Substantial Completion: 6/4/2024

Final Completion: 8/3/2024

The report is for the week of: Monday, 12/4/2023

thru Sunday, 12/10/2023

The contractor performed the following operations this week. Sub work is noted in parenthesis:

**Monday-** Installed 75 LF of 8" gravity main on Appalachee Trl.

**Tuesday-** Installed 163 LF of 8" gravity main on Appalachee Trl.

**Wednesday-** Installed manhole 1056 & 104 LF of 8" gravity main on Appalachee Trl.

**Thursday-** Extended 4- 4" laterals from gravity main to right of way on Appalachee Trl.

**Friday-** Extended 2- 4" laterals from gravity main to right of way on Appalachee Trl. Cleaned up construction area.

**Saturday-** No work at contractor's option.

**Sunday-** No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete: 15%

Time Remaining (%): 59%

Invoiced to Date: \$867,172.46

Weather days to date: 3

Original Contract Amount: \$6,377,639.99

Change Order Amount Approved:

Holiday days granted: 5

Remaining: \$5,510,467.53

Actual Days: 132

Days to Substantial Completion: 300

Days used with deduct: 124

Remaining to SC: 176

Days to Final Completion: 360


Remaining to FC: 236

A handwritten signature in blue ink, appearing to read "Rob B", is positioned above a horizontal line.

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)





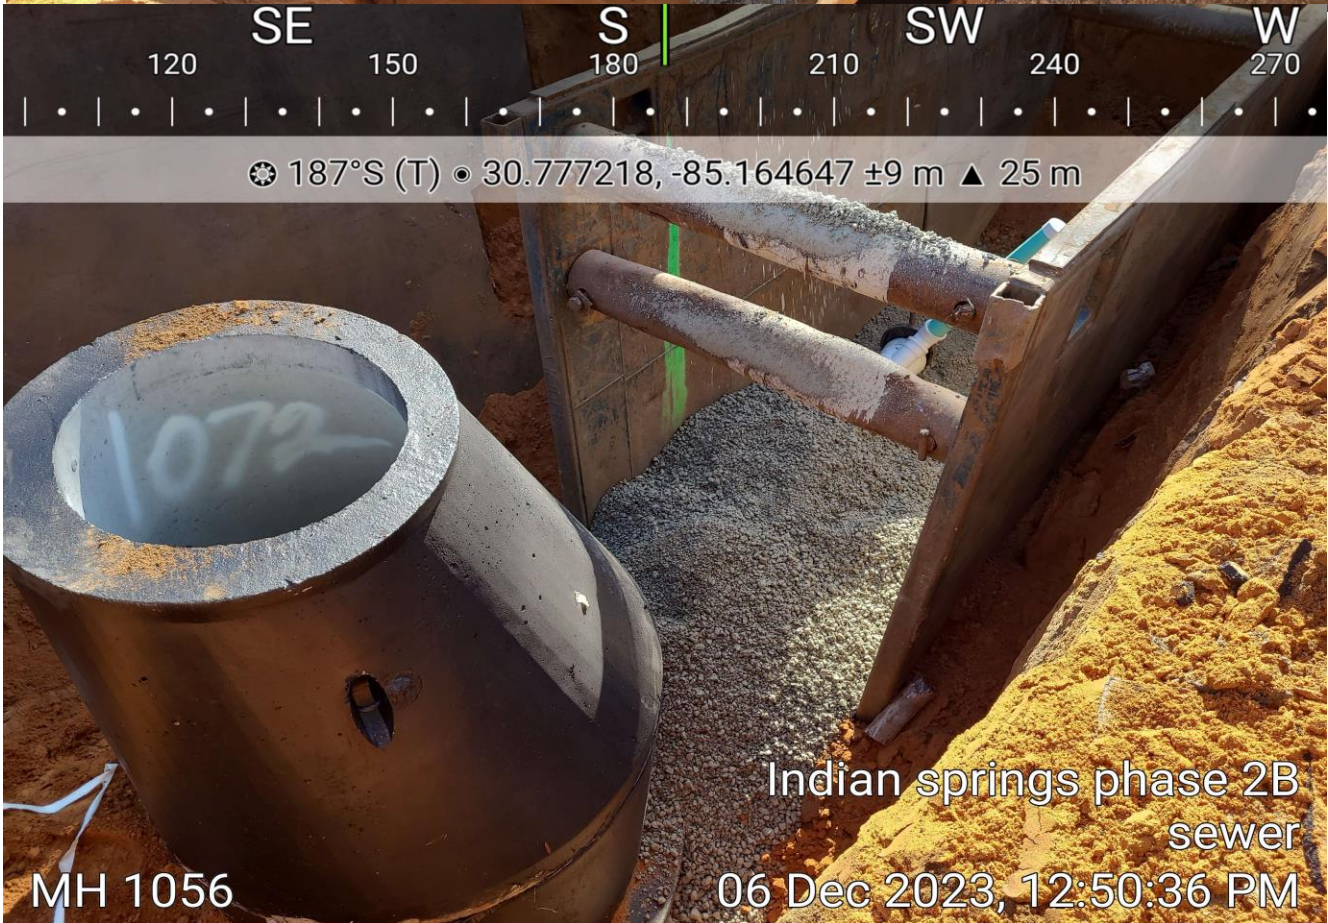




☼ 337°NW (T) • 30.777745, -85.162839 ±8 m ▲ -19 m




Set lateral at station  
1062+15

Indian springs phase 2B  
sewer  
07 Dec 2023, 9:17:35 AM



☼ 344°NW (T) • 30.777619, -85.163761 ±5 m ▲ 15 m

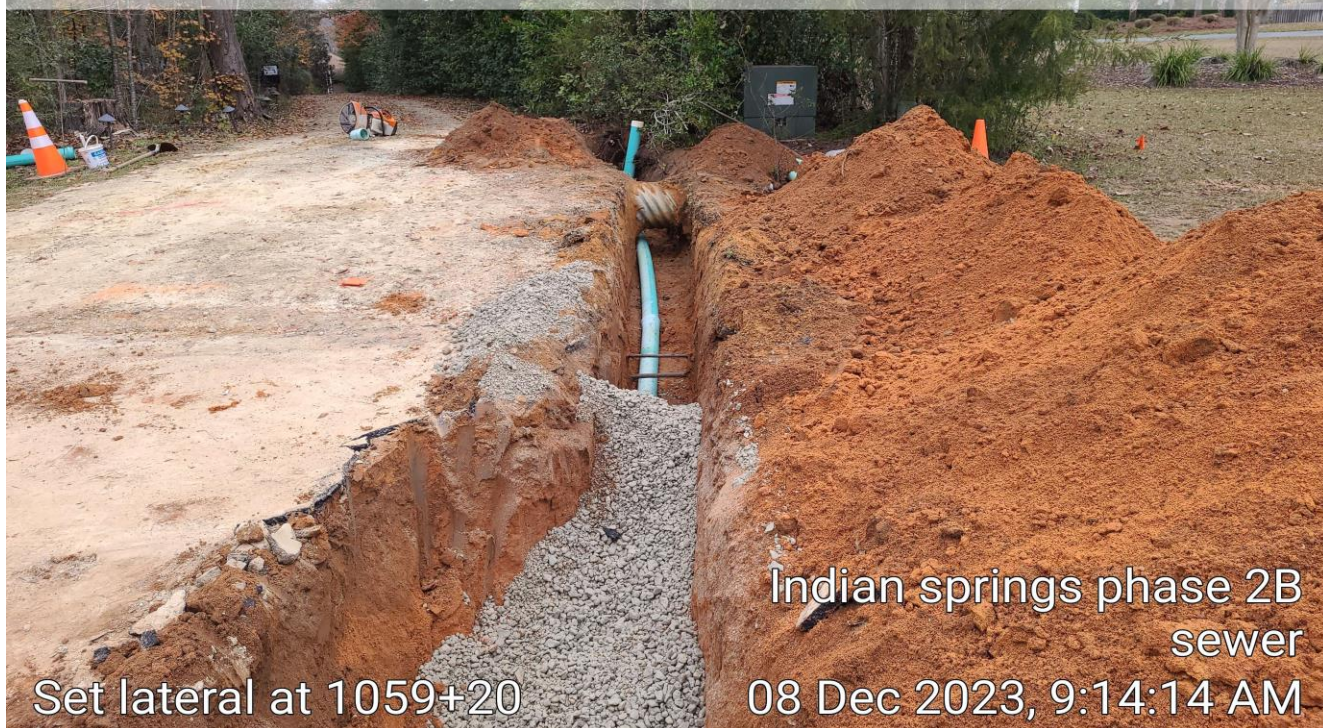

Set lateral at 1059+20

Indian springs phase 2B  
sewer  
08 Dec 2023, 9:14:14 AM
