

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL

Prepared by: Alday-Howell Engineering, Inc.

Prepared on: 1/23/2024

For Project: **Blue Springs Road Sewer Extensions Phase 1**
NFWMD Const. Grant Agreement No. 17-061 AHE # 17-062

Contractor: L & K Contracting, Inc.

Designer: Alday-Howell Engineering Inspector: Brett Lawrence (850) 718-7233

Notice to Proceed: 9/27/2022 Award Date: 6/29/2022



Substantial Completion: 2/12/2024

Final Completion: 3/13/2024

The report is for the week of: Monday, 1/15/2024

thru Sunday, 1/21/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Material too wet to install. Rain recovery day granted.

Tuesday- No work due to weather. Rain day granted.

Wednesday- Installed 14 LF of 8" PVC gravity main on Blue Springs Rd. Material too wet to install. Rain recovery day granted.

Thursday- Material too wet to install. Rain recovery day granted.

Friday- Settling occurred in roadway after rain. Contractor assessed areas.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	52%	Time Remaining (%):	5%
Invoiced to Date:	\$2,442,009.06	Weather days to date:	26
Original Contract Amount:	\$5,347,467.37 *		
Change Order Amount Approved:	\$83,361.30	Holiday days granted:	36
Contract Time Approved:	141	Actual Days:	482
Remaining:	\$2,988,819.61	Days used with deduct:	420
Days to Substantial Completion:	441	Original SC:	300
		Remaining to SC:	21
Days to Final Completion:	471	Original FC:	330
		Remaining to FC:	51

* Budgeted amount is \$4,617,183.69. Contract amount \$5,347,467.37 contingent upon securing additional funding.

A handwritten signature in blue ink, appearing to read 'Rob B', is written over a horizontal line.

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)

West Elevation

BRG: 99°E (T) POS: 30.781565, -85.186786




Preparing to make a connection.

Blue Springs Sewer Project
17 Jan 2024, 9:34:25 AM

South West Elevation

BRG: 47°NE (T) POS: 30.781408, -85.187156

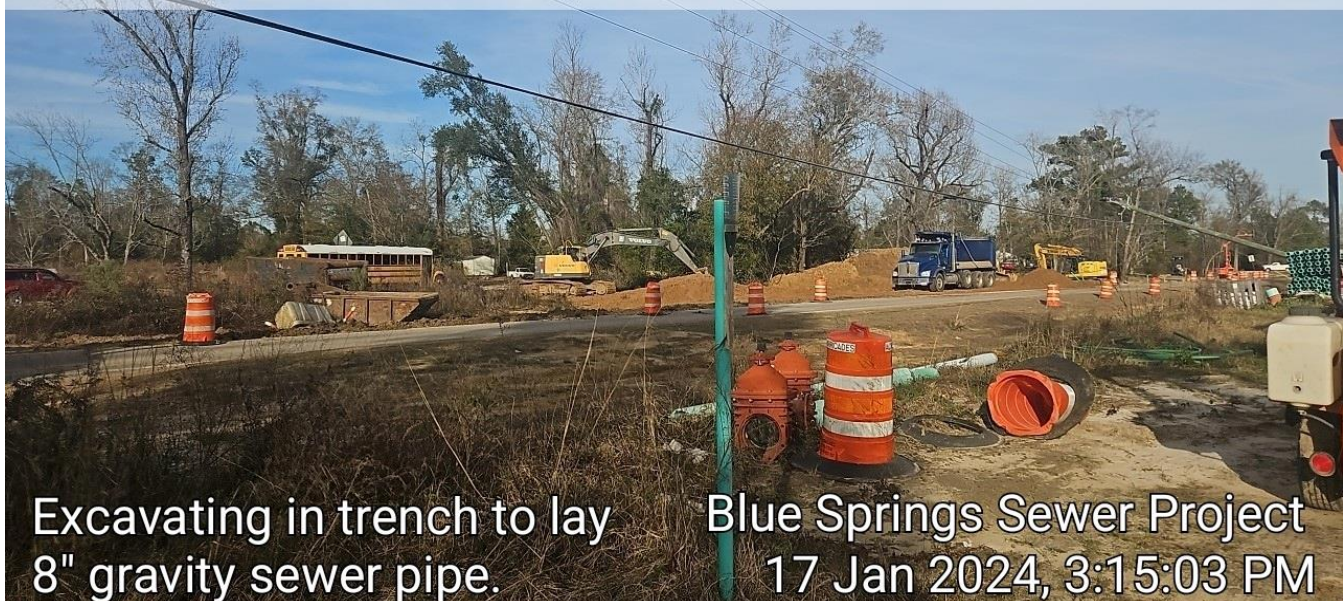

Excavating in trench to lay
8" gravity sewer pipe.

Blue Springs Sewer Project
17 Jan 2024, 3:15:03 PM

