

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL

Prepared by: Alday-Howell Engineering, Inc.

Prepared on: 1/9/2024

For Project: **Indian Springs Sewer Phase 2B**

NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033

Contractor: Blankenship Contracting, Inc.

Designer: Alday-Howell Engineering

Inspector: Dwayne Josey (850) 258-3386

Notice to Proceed: 8/1/2023

Award Date: 12/13/2022



Substantial Completion: 6/15/2024

Final Completion: 8/14/2024

The report is for the week of: Monday, 1/1/2024

thru Sunday, 1/7/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- No work due to holiday. Holiday day granted.

Tuesday- Installed 4" of limerock base above trench preparing for full depth reclamation on Appalachian Trl.

Wednesday- No work due to rain. Rain day granted.

Thursday- Installed 4" of limerock base above trench preparing for full depth reclamation on Appalachian Trl.

Friday- Installed 4" of limerock base above trench preparing for full depth reclamation on Appalachian Trl.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete: 15%

Time Remaining (%): 53%

Invoiced to Date: \$867,172.46

Weather days to date: 4

Original Contract Amount: \$6,377,639.99

Change Order Amount Approved:

Holiday days granted: 15

Actual Days: 160

Remaining: \$5,510,467.53

Days used with deduct: 141

Days to Substantial Completion: 300


Remaining to SC: 159

Days to Final Completion: 360

Remaining to FC: 219

A handwritten signature in blue ink, appearing to read "Rob B", is positioned above the approval line.

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)

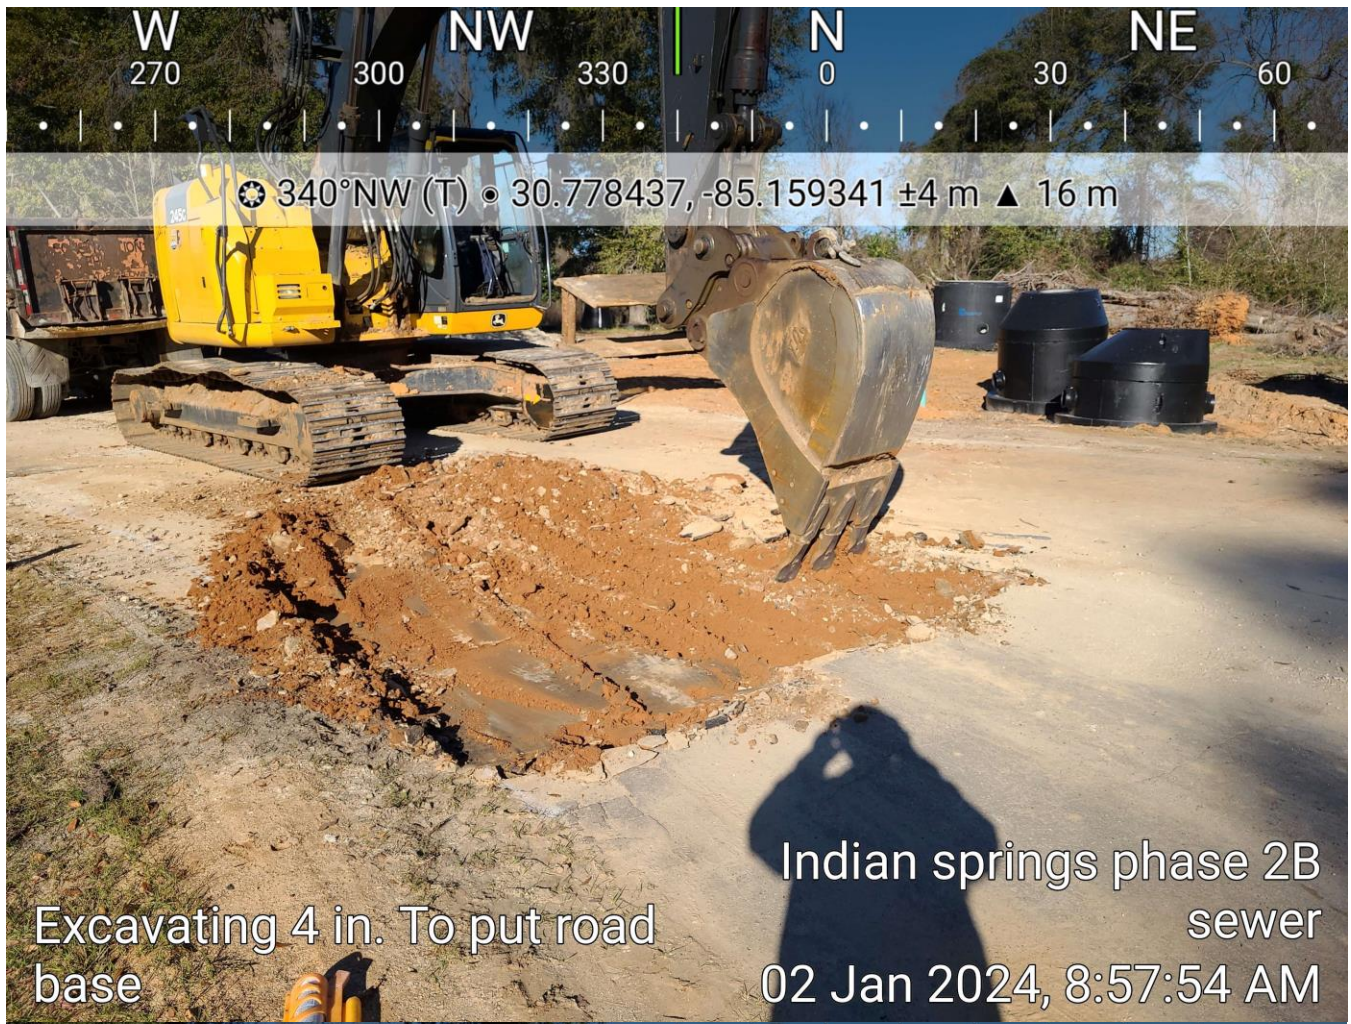




☼ 337°NW (T) • 30.778131, -85.161085 ±6 m ▲ 16 m



Indian springs phase 2B
sewer

Road base

04 Jan 2024, 9:16:43 AM

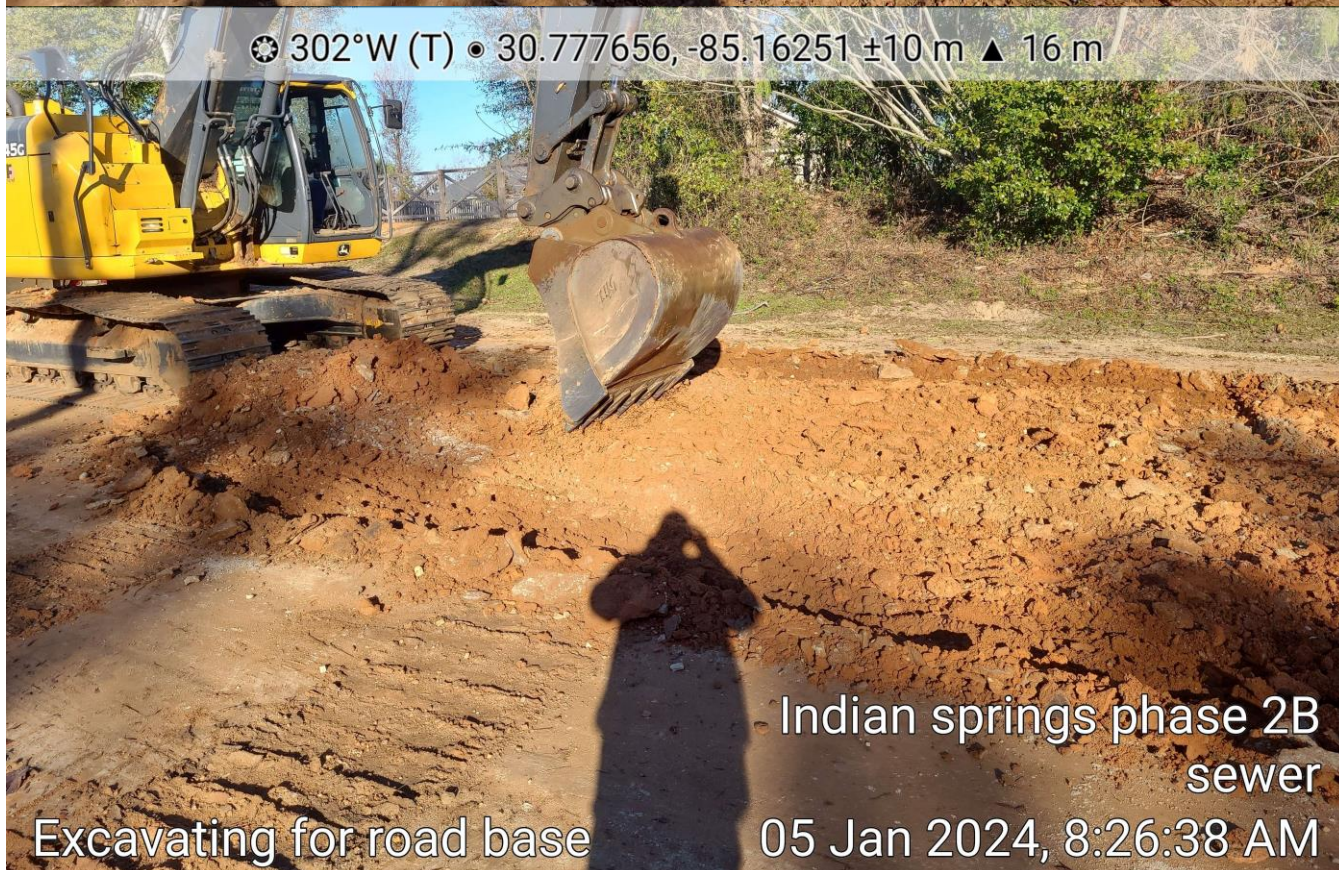

☼ 302°W (T) • 30.777656, -85.16251 ±10 m ▲ 16 m

Indian springs phase 2B
sewer

Excavating for road base

05 Jan 2024, 8:26:38 AM

