

## CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL

Prepared by: Alday-Howell Engineering, Inc.

Prepared on: 2/4/2024

For Project: Indian Springs Sewer Phase 2B

NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033

Contractor: Blankenship Contracting, Inc.

Designer: Alday-Howell Engineering

Inspector: Dwayne Josey (850) 258-3386

Notice to Proceed: 8/1/2023

Award Date: 12/13/2022



Substantial Completion: 6/16/2024

Final Completion: 8/15/2024

The report is for the week of: Monday, 1/22/2024

thru Sunday, 1/28/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

**Monday-** Installed 84 LF of 8" gravity main from station 1046+20 to 1045+36 on Appalachee Trl.

**Tuesday-** Installed 121 LF of 8" gravity main from station 1045+36 to 1044+12 on Appalachee Trl.

**Wednesday-** Installed manhole 1043 and 72 LF of 8" gravity main from station 1044+12 to 1043+40 on Appalachee Trl.

**Thursday-** Installed 4" of limerock to provide weatherproof surface.

**Friday-** Installed 4" of limerock to provide weatherproof surface.

**Saturday-** No work at contractor's option.

**Sunday-** No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete: 18%

Time Remaining (%): 46%

Invoiced to Date: \$1,019,563.24

Weather days to date: 5

Original Contract Amount: \$6,377,639.99

Change Order Amount Approved:

Holiday days granted: 15

Actual Days: 181

Remaining: \$5,358,076.75

Days used with deduct: 161

Days to Substantial Completion: 300

Remaining to SC: 139


Days to Final Completion: 360

Remaining to FC: 199


A handwritten signature in blue ink, appearing to read 'Rob B', is written over a horizontal line.

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)




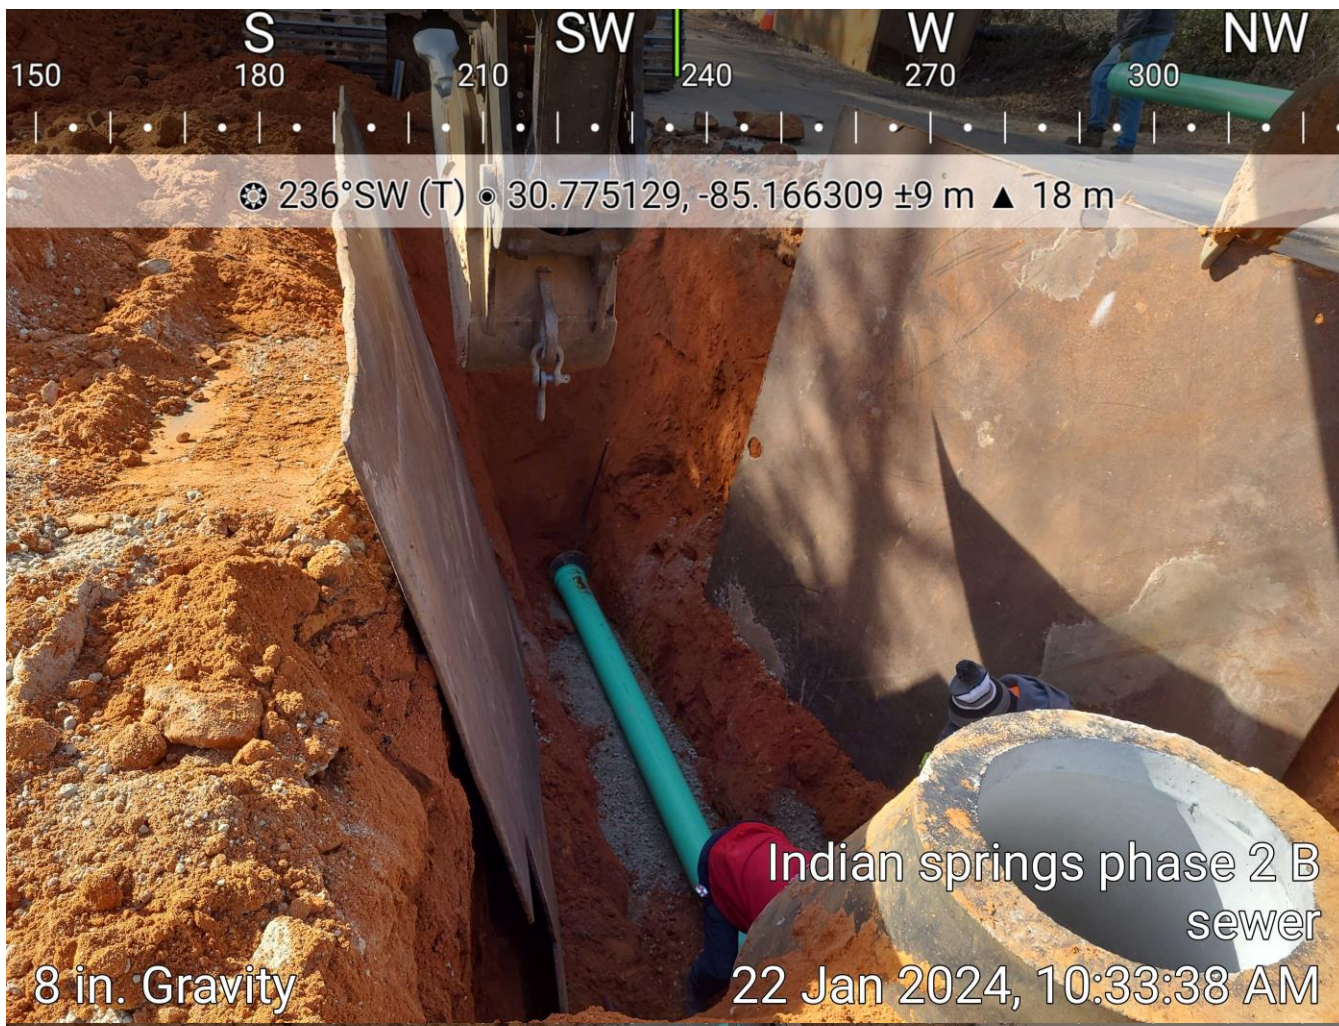



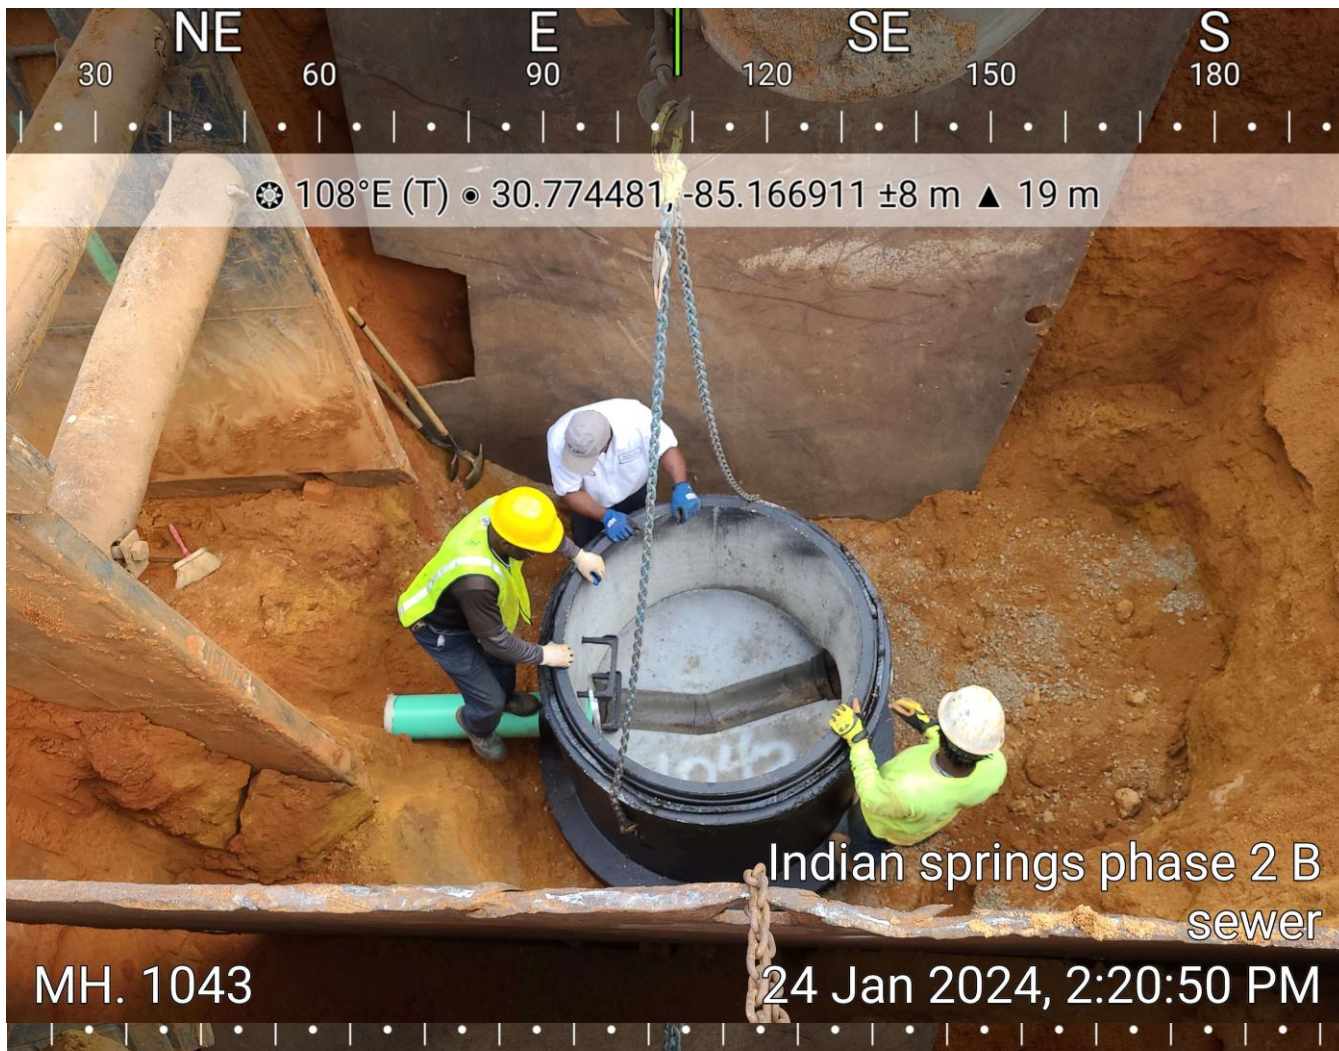





☼ 261°W (T) • 30.77487, -85.167282 ±36 m ▲ 20 m



MH. 1043

Indian springs phase 2 B  
sewer  
24 Jan 2024, 3:27:48 PM

☼ 68° NE (T) • 30.775434, -85.166315 ±7 m ▲ 18m



Fdot road base

Indian springs phase 2 B  
sewer  
26 Jan 2024, 10:03:56 AM
