

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 3/26/2024
For Project: **Indian Springs Sewer Phase 2B**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
Contractor: Blankenship Contracting, Inc.
Designer: Alday-Howell Engineering
Inspector: Dwayne Josey (850) 258-3386
Notice to Proceed: 8/1/2023 Award Date: 12/13/2022



Substantial Completion: 6/20/2024 Final Completion: 8/19/2024

The report is for the week of: Monday, 3/18/2024 thru Sunday, 3/24/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

- Monday-** No work at contractor's option.
- Tuesday-** No work at contractor's option.
- Wednesday-** Performed low pressure air test on manhole 1040 to 1023. Grouted around pipe inside manholes.
- Thursday-** Installed 4" of limerock base above trench. Performed CCTV camera inspection from manhole 1023 to 1043.
- Friday-** Installed 4" of limerock base above trench.
- Saturday-** No work at contractor's option.
- Sunday-** No work at contractor's option.


Engineer's remarks/Pending issues:

Percent Project Complete:	27%	Time Remaining (%):	29%
Invoiced to Date:	\$1,407,308.09	Weather days to date:	9
Original Contract Amount:	\$6,377,639.99	Holiday days granted:	15
Change Order Amount Approved:		Actual Days:	237
Remaining:	\$4,970,331.90	Days used with deduct:	213
Days to Substantial Completion:	300	Remaining to SC:	87
Days to Final Completion:	360	Remaining to FC:	147

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)

210 SW W NW N CH
240 270 300 330 0 230
ir-Loc® Low-Pressure
w


☉ 281° W (T) • 30.772856, -85.167176 ±9 m ▲ 21m

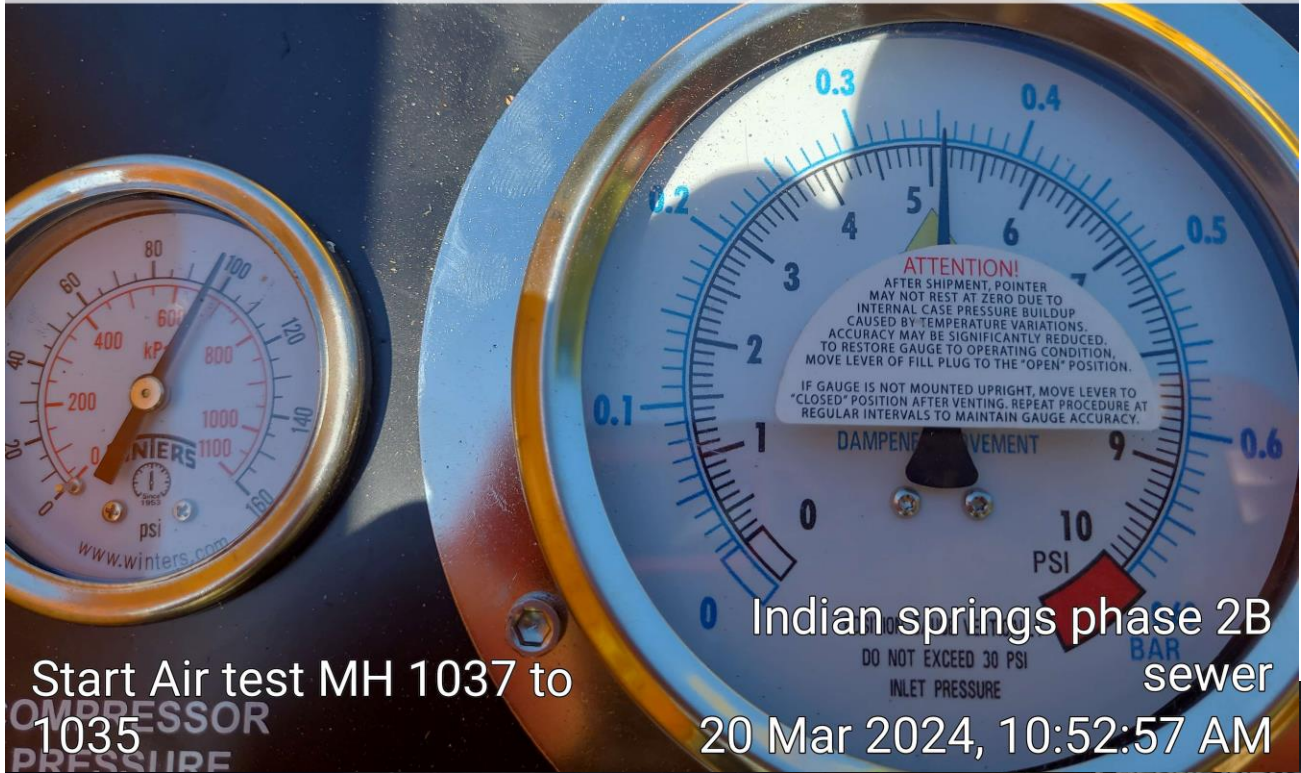

Start Air test MH 1037 to
1035

Indian springs phase 2B
sewer
20 Mar 2024, 10:52:57 AM

280° W (T) • 30.772893, -85.16698 ±4 m ▲ 21m
CHERNE INDUS
2300 VIERLING
SHAKOPEE, M
www.chernein

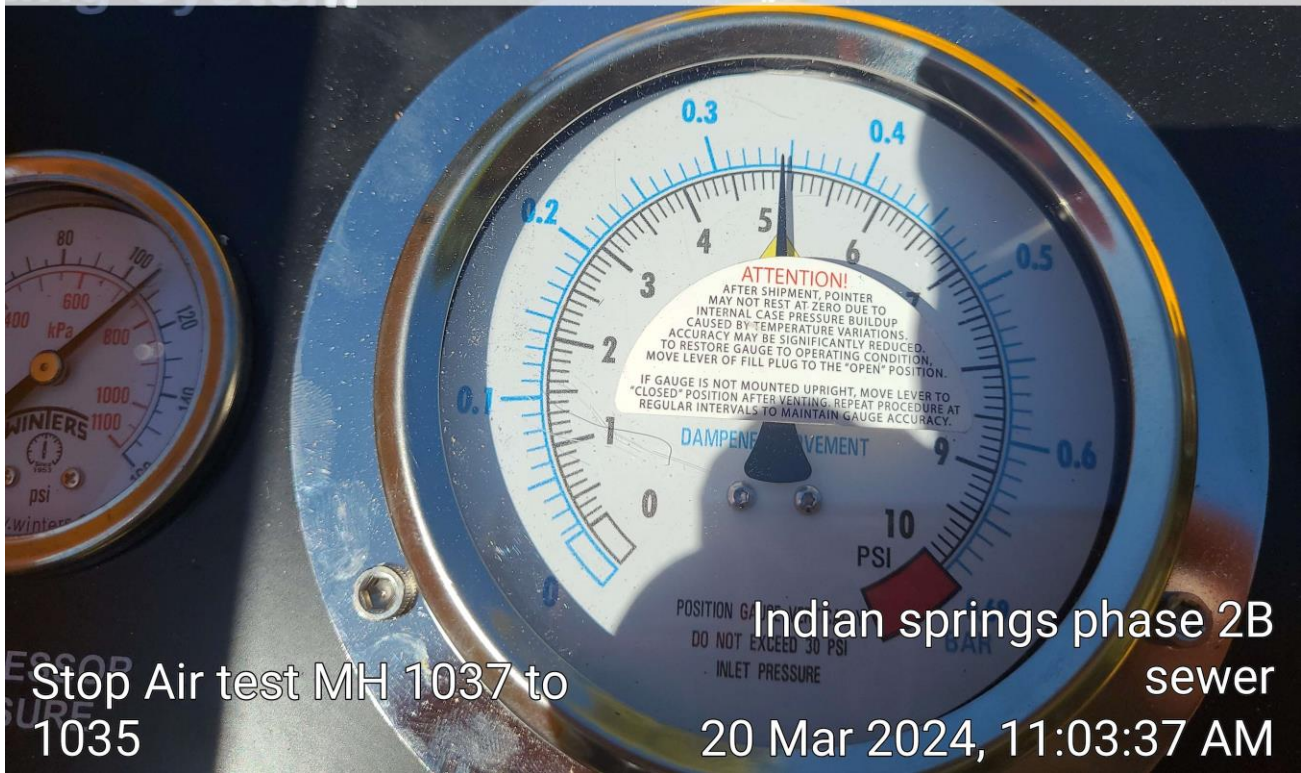

Stop Air test MH 1037 to
1035

Indian springs phase 2B
sewer
20 Mar 2024, 11:03:37 AM



Indian springs phase 2B
sewer

Camera inspection

21 Mar 2024, 9:33:57 AM

133° SE (T) • 30.773046, -85.167011 ±12 m ▲ 21m



Indian springs phase 2B
sewer

22 Mar 2024, 9:15:20 AM

Road base
