

# CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL  
 Prepared by: Alday-Howell Engineering, Inc.  
 Prepared on: 4/16/2024  
 For Project: **Indian Springs Phase 2 Water**  
**FDEP Grant/Loan Agreement DW320381** AHE # 20-034  
 Contractor: L & K Contracting, Inc.  
 Designer: Alday-Howell Engineering Inspector: Tyler Lawrence (850) 718-7233  
 Notice to Proceed: 10/15/2023 Award Date: 9/12/2023



Substantial Completion: 5/16/2025 Final Completion: 7/15/2025

The report is for the week of: Monday, 4/1/2024 thru Sunday, 4/7/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

- Monday-** Installed 150 lf of 6" water main, 104 lf of 8" water main and 200 lf of 10" water main.
- Tuesday-** Installed 1 fire hydrant, 4 services, 80 lf of 6" water main, 55 lf of 8" water main and 340 lf of 10" water main.
- Wednesday-** Installed 1 fire hydrant, 100 lf of 8" water main and 200 lf of 10" water main.
- Thursday-** Installed sod, 3 services, 260 lf of 8" water main and 300 lf of 10" water main.
- Friday-** Installed 3 services and 200 lf of 10" water main.
- Saturday-** No work at contractor's option.
- Sunday-** No work at contractor's option.

Engineer's remarks/Pending issues:


Percent Project Complete:	33%	Time Remaining (%):	72%
Invoiced to Date:	\$1,864,556.12	Weather days to date:	3
Original Contract Amount:	\$4,492,568.00	Holiday days granted:	16
Change Order Amount Approved:	-\$550,499.25	Actual Days:	176
Remaining:	\$2,077,512.63	Days used with deduct:	157
Days to Substantial Completion:	560	Remaining to SC:	403
Days to Final Completion:	620	Remaining to FC:	463

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)



**5188 Oak Dr Marianna FL**

☉ 63°NE (T) ☉ 30°46'19"N, 85°9'48"W ±13ft ▲ 187ft

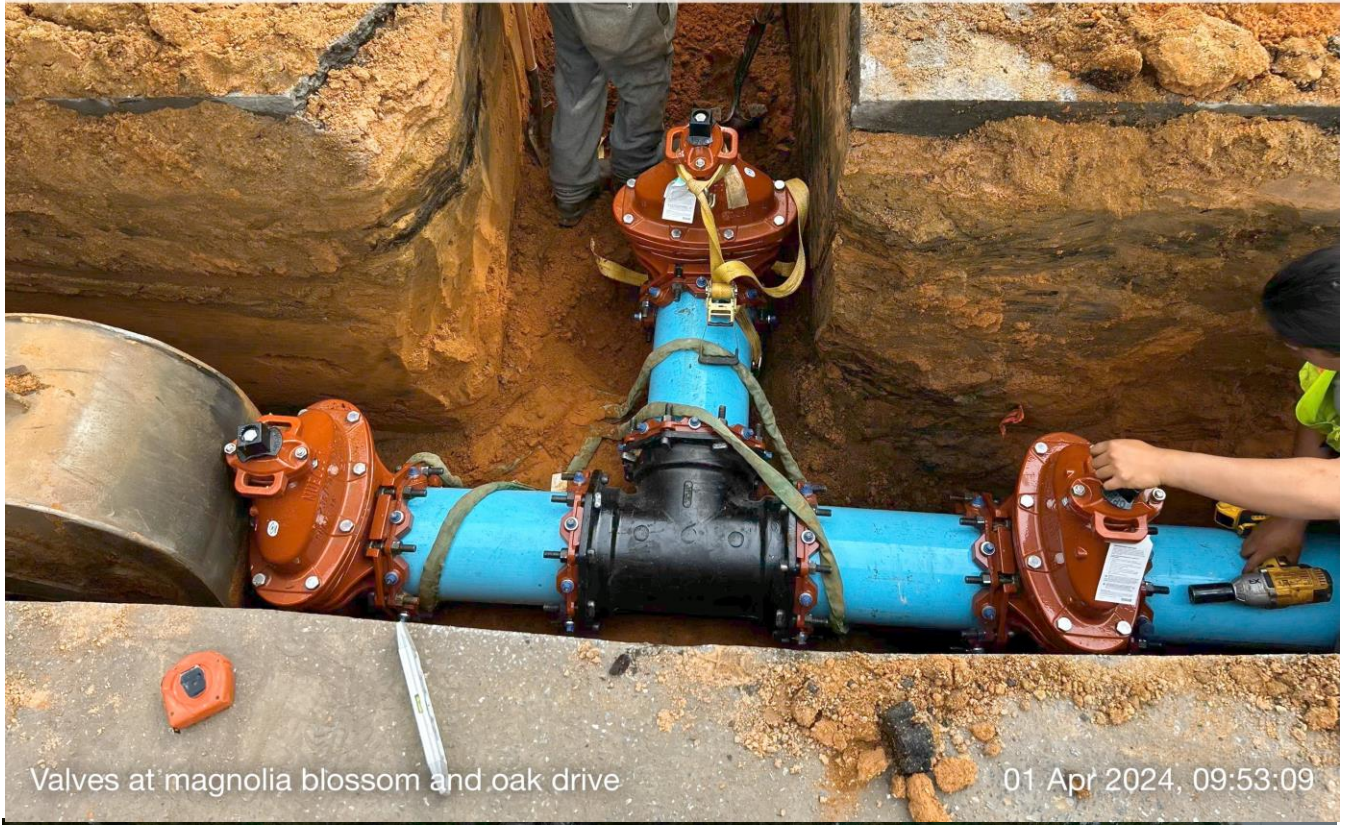

**5248 Clubhouse Dr Marianna FL**

☉ 319°NW (T) ☉ 30°46'3"N, 85°9'29"W ±13ft ▲ 175ft







Installing 6" pvc at the clubhouse

01 Apr 2024, 11:25:06

☉ 145°SE (T) ● 30°46'22"N, 85°9'51"W ±16ft ▲ 178ft



Setting fire hydrant on magnolia blossom

02 Apr 2024, 16:00:10

☉ 314°NW (T) ● 30°46'21"N, 85°9'49"W ±16ft ▲ 133ft



Laying 8 inch pipe on magnolia blossom

04 Apr 2024, 09:42:33
