

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 4/16/2024
For Project: **Indian Springs Phase 2 Water**
FDEP Grant/Loan Agreement DW320381 AHE # 20-034
Contractor: L & K Contracting, Inc.
Designer: Alday-Howell Engineering Inspector: Tyler Lawrence (850) 718-7233
Notice to Proceed: 10/15/2023 Award Date: 9/12/2023



Substantial Completion: 5/16/2025 Final Completion: 7/15/2025

The report is for the week of: Monday, 4/8/2024 thru Sunday, 4/14/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

- Monday-** Installed 1 service, 115 lf of 8" water main and 346 lf of 10" water main.
- Tuesday-** Installed 4 services, 229 lf of 6" water main, 103 lf of 8" water main and 338 lf of 10" water main.
- Wednesday-** Installed 1 fire hydrant, 4 services, 100 lf of 8" water main and 437 lf of 10" water main.
- Thursday-** Installed 1 fire hydrant, 2 services, 255 lf of 6" water main and 338 lf of 10" water main.
- Friday-** Installed 1 fire hydrant and 20 lf of 10" water main.
- Saturday-** No work at contractor's option.
- Sunday-** No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	33%	Time Remaining (%):	71%
Invoiced to Date:	\$1,864,556.12	Weather days to date:	3
Original Contract Amount:	\$4,492,568.00	Holiday days granted:	16
Change Order Amount Approved:	-\$550,499.25	Actual Days:	183
Remaining:	\$2,077,512.63	Days used with deduct:	164
Days to Substantial Completion:	560	Remaining to SC:	396
Days to Final Completion:	620	Remaining to FC:	456

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)

5231 Oak Dr Marianna FL

☀ 17°N (T) ● 30°46'29"N, 85°9'32"W ±29ft ▲ 161ft



Using a sleeve to connect between 2 driveways

09 Apr 2024, 09:54:56

5221 Oak Dr Marianna FL

☀ 196°S (T) ● 30°46'27"N, 85°9'33"W ±141ft ▲ 156ft






10" pipe oak drive

10 Apr 2024, 10:19:43

☀ 56°NE (T) ● 30°46'29"N, 85°9'49"W ±29ft ▲ 148ft

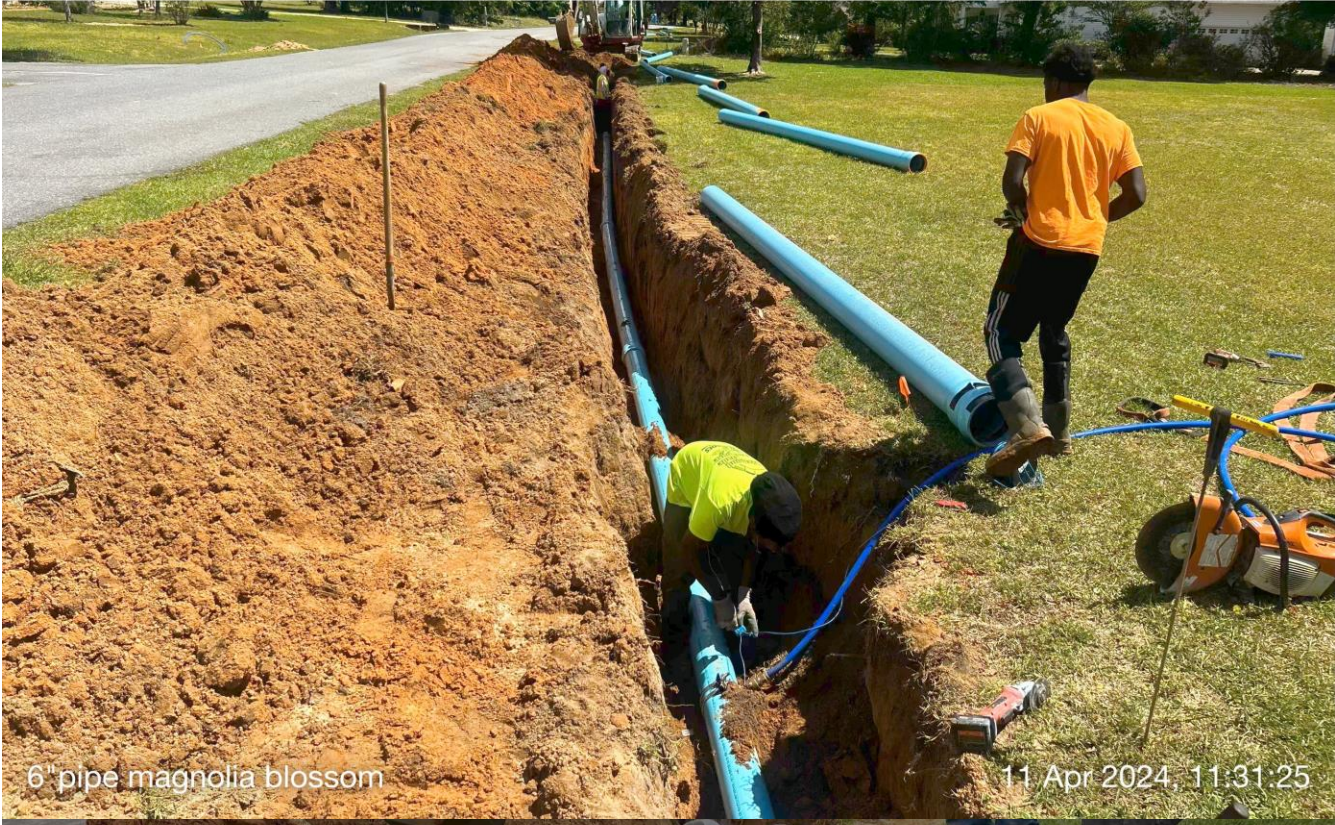

6" pipe magnolia blossom

11 Apr 2024, 11:31:25

☀ 77°E (T) ● 30°46'31"N, 85°9'29"W ±85ft ▲ 145ft



10" oak drive

11 Apr 2024, 15:51:03
