

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 4/24/2024
For Project: **Indian Springs Sewer Phase 2B**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
Contractor: Blankenship Contracting, Inc.
Designer: Alday-Howell Engineering
Inspector: Dwayne Josey (850) 258-3386
Notice to Proceed: 8/1/2023 Award Date: 12/13/2022



Substantial Completion: 6/20/2024 Final Completion: 8/19/2024

The report is for the week of: Monday, 4/15/2024 thru Sunday, 4/21/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Installed 280 lf of 4" force main.

Tuesday- Installed 110 lf of 4" gravity on lot, 29 lf of 4" trenchless and 611 lf of 4" force main.

Wednesday- Installed 400 lf of 4" force main.

Thursday- Installed 240 lf of 4" force main.

Friday- Cleaned construction area.


Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	31%	Time Remaining (%):	20%
Invoiced to Date:	\$1,549,451.80	Weather days to date:	9
Original Contract Amount:	\$6,377,639.99	Holiday days granted:	15
Change Order Amount Approved:		Actual Days:	265
Remaining:	\$4,828,188.19	Days used with deduct:	241
Days to Substantial Completion:	300	Remaining to SC:	59
Days to Final Completion:	360	Remaining to FC:	119

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)



☀ 42° NE (T) • 30.775041, -85.166596 ±5 m ▲ 20m



Indian springs phase 2B
sewer

4 in. FM

15 Apr 2024, 11:12:27 AM




☀ 33° N (T) • 30.774761, -85.166775 ±21 m ▲ 20m



Indian springs phase 2B
sewer


4 in. FM

15 Apr 2024, 2:29:47 PM

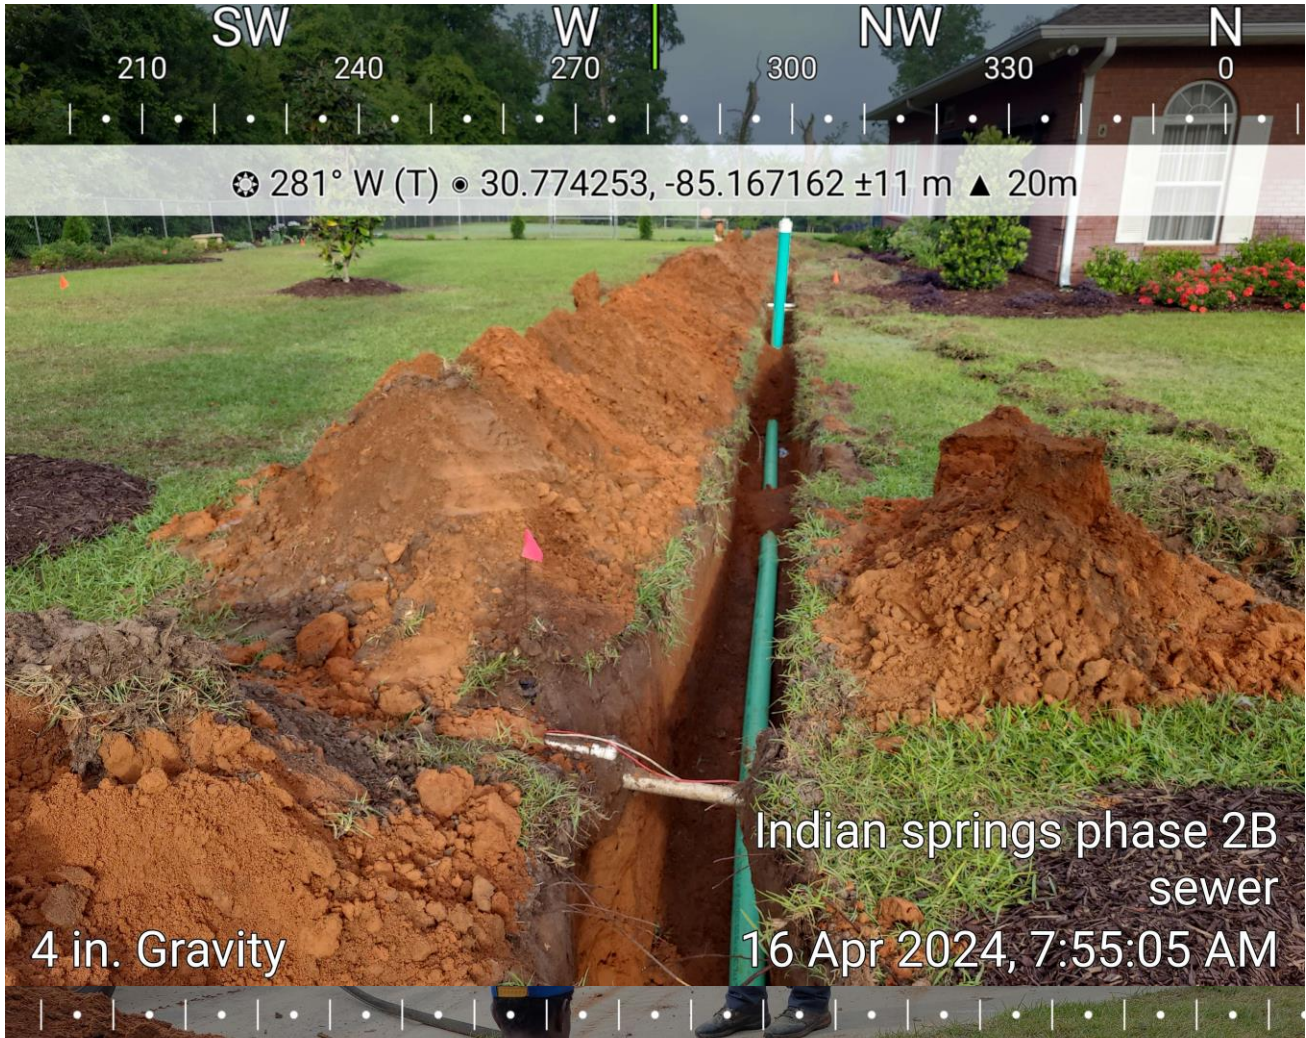

☉ 185° S (T) • 30.774612, -85.166871 ±18 m ▲ 20m





☀ 35° NE (T) • 30.774683, -85.166913 ±8 m ▲ 20m



4 in. FM.

Indian springs phase 2B
sewer
16 Apr 2024, 8:10:25 AM



☀ 174° S (T) • 30.773588, -85.167107 ±5 m ▲ 21m



4 in. FM.

Indian springs phase 2B
sewer
17 Apr 2024, 9:31:53 AM
