

# CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL

Prepared by: Alday-Howell Engineering, Inc.

Prepared on: 4/23/2024

For Project: **Indian Springs Phase 2 Water  
FDEP Grant/Loan Agreement DW320381**

AHE # 20-034

Contractor: L & K Contracting, Inc.

Designer: Alday-Howell Engineering

Inspector: Tyler Lawrence (850) 718-7233

Notice to Proceed: 10/15/2023

Award Date: 9/12/2023

Substantial Completion: 5/16/2025

Final Completion: 7/15/2025

The report is for the week of: Monday, 4/15/2024

thru Sunday, 4/21/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

**Monday-** Installed 244 LF of 3" PVC water main, 135 LF of 6" PVC water main, 90 LF of 10" PVC water main, 1 fire hydrant and 1-1" services.

**Tuesday-** Installed 300 LF of 6" PVC water main, 213 LF of 10" PVC water main and 11-1" services.

**Wednesday-** Installed 185 LF of 3" PVC water main, 213 LF of 10" PVC water main and 7-1" services.

**Thursday-** Installed 7-1" services. Repaired irrigation damaged due to construction.

**Friday-** Installed 7-1" services. Repaired irrigation damaged due to construction.

**Saturday-** No work at contractor's option.

**Sunday-** No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete: 35%

Time Remaining (%): 69%

Invoiced to Date: \$1,864,556.12

Weather days to date: 3

Original Contract Amount: \$4,492,568.00

Change Order Amount Approved: -\$550,499.25

Holiday days granted: 16

Actual Days: 190

Remaining: \$2,077,512.63

Days used with deduct: 171

Days to Substantial Completion: 560

Remaining to SC: 389

Days to Final Completion: 620

Remaining to FC: 449



Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)




**Alday-Howell**  
ENGINEERING, INC.





# 5243 Oak Dr Marianna FL

☉ 76°E (T) ● 30°46'31"N, 85°9'26"W ±16ft ▲ 141ft

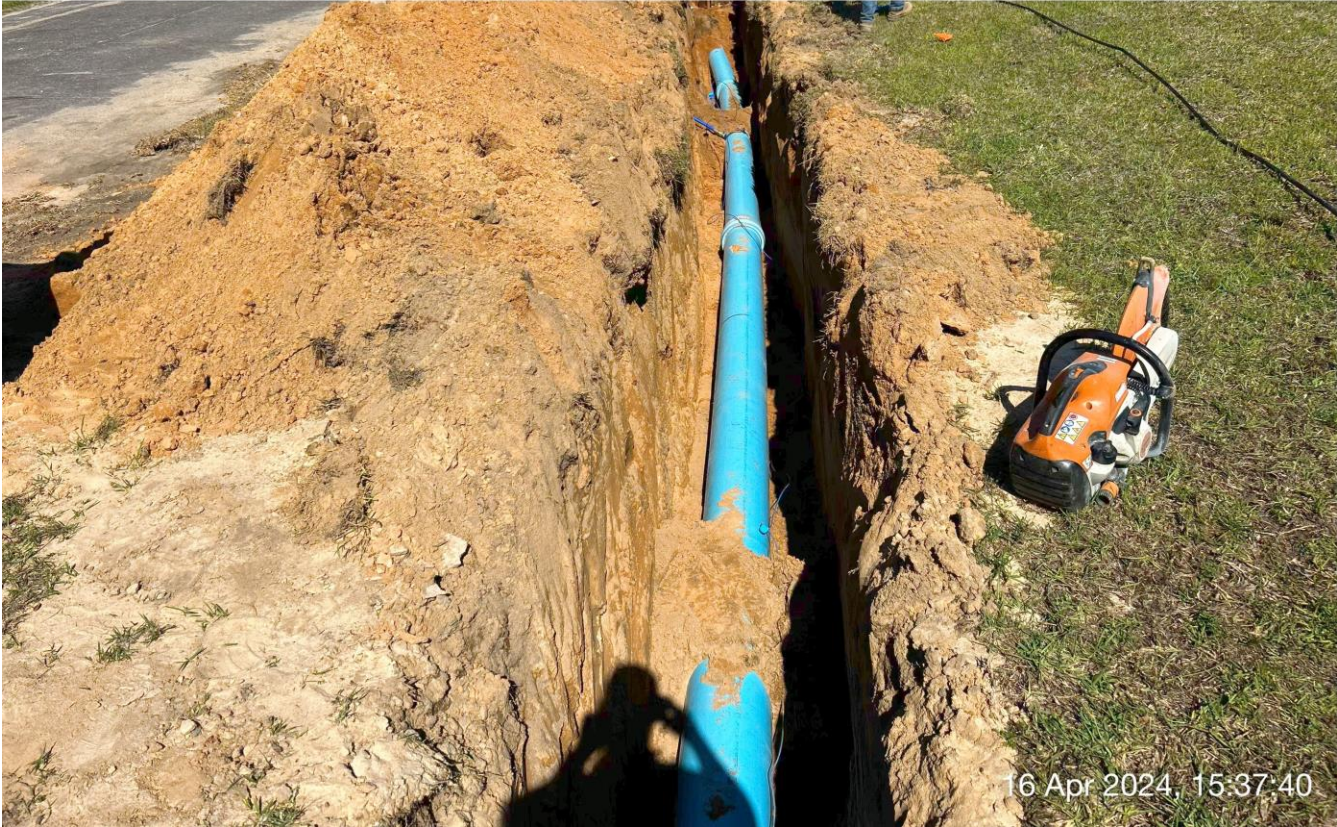

16 Apr 2024, 15:37:40

☉ 51°NE (T) ● 30°46'31"N, 85°9'47"W ±9ft ▲ 128ft



6" pvc

17 Apr 2024, 08:47:09



5243 Oak Dr Marianna FL

☀ 71°E (T) ● 30°46'31"N, 85°9'25"W ±9ft ▲ 158ft



10" pvc

17 Apr 2024, 09:58:58

☀ 237°SW (T) ● 30°46'31"N, 85°9'23"W ±170ft ▲ 158ft



17 Apr 2024, 15:49:24
