

# CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL  
Prepared by: Alday-Howell Engineering, Inc.  
Prepared on: 6/18/2024  
For Project: **Blue Springs Road Sewer Extensions Phase 1**  
**NFWFMD Const. Grant Agreement No. 17-061** AHE # 17-062  
Contractor: L & K Contracting, Inc.  
Designer: Alday-Howell Engineering Inspector: Brett Lawrence (850) 718-7233  
Notice to Proceed: 9/27/2022 Award Date: 6/29/2022



Substantial Completion: 2/25/2024 Final Completion: 3/26/2024

The report is for the week of: Monday, 6/10/2024 thru Sunday, 6/16/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

- Monday-** Installed manhole 245 and 63 LF of 8" gravity sewer pipe.
- Tuesday-** Installed 140 LF of 8" gravity sewer pipe.
- Wednesday-** Installed 70 LF of 8" gravity sewer pipe. Investigated infiltration of gravity system with CCTV.
- Thursday-** Installed 98 LF of 8" gravity sewer pipe. Raised manholes. Investigated infiltration of gravity system with CCTV.
- Friday-** Installed 38 LF of 8" gravity sewer pipe. Raised manholes. Investigated infiltration of gravity system with CCTV.
- Saturday-** No work at contractor's option.
- Sunday-** No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	56%	Time Remaining (%):	-26%		
Invoiced to Date:	\$2,778,986.09	Weather days to date:	36		
Original Contract Amount:	\$5,347,467.37	Holiday days granted:	39		
Change Order Amount Approved:	\$83,361.30	Actual Days:	629		
Contract Time Approved:	141	Days used with deduct:	554		
Remaining:	\$2,651,842.58				
Days to Substantial Completion:	441	Original SC:	300	Remaining to SC:	-113
Days to Final Completion:	471	Original FC:	330	Remaining to FC:	-83

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)





☉ 147° SE (T) ● 30.78328, -85.177492 ±44 m ▲ 7m



AHE/bhl

10 Jun 2024, 9:03:18 AM


☉ 264° W (T) ● 30.783237, -85.177424 ±9 m ▲ 7m



Roller packing the pipe trench  
AHE/bhl

Blue Springs Sewer Project  
10 Jun 2024, 9:03:25 AM





☀ 301° W (T) • 30.783267, -85.177246 ±5 m ▲ 12m



Installation of MH 245  
AHE/bhl

Blue Springs Sewer Project  
11 Jun 2024, 7:49:43 AM


☀ 231° SW (T) • 30.783244, -85.177527 ±5 m ▲ 11m




Contractors working in the pipe  
trench  
AHE/bhl

Blue Springs Sewer Project  
07 Jun 2024, 8:19:32 AM






☉ 243° SW (T) ● 30.783402, -85.176399 ±3 m ▲ 13m

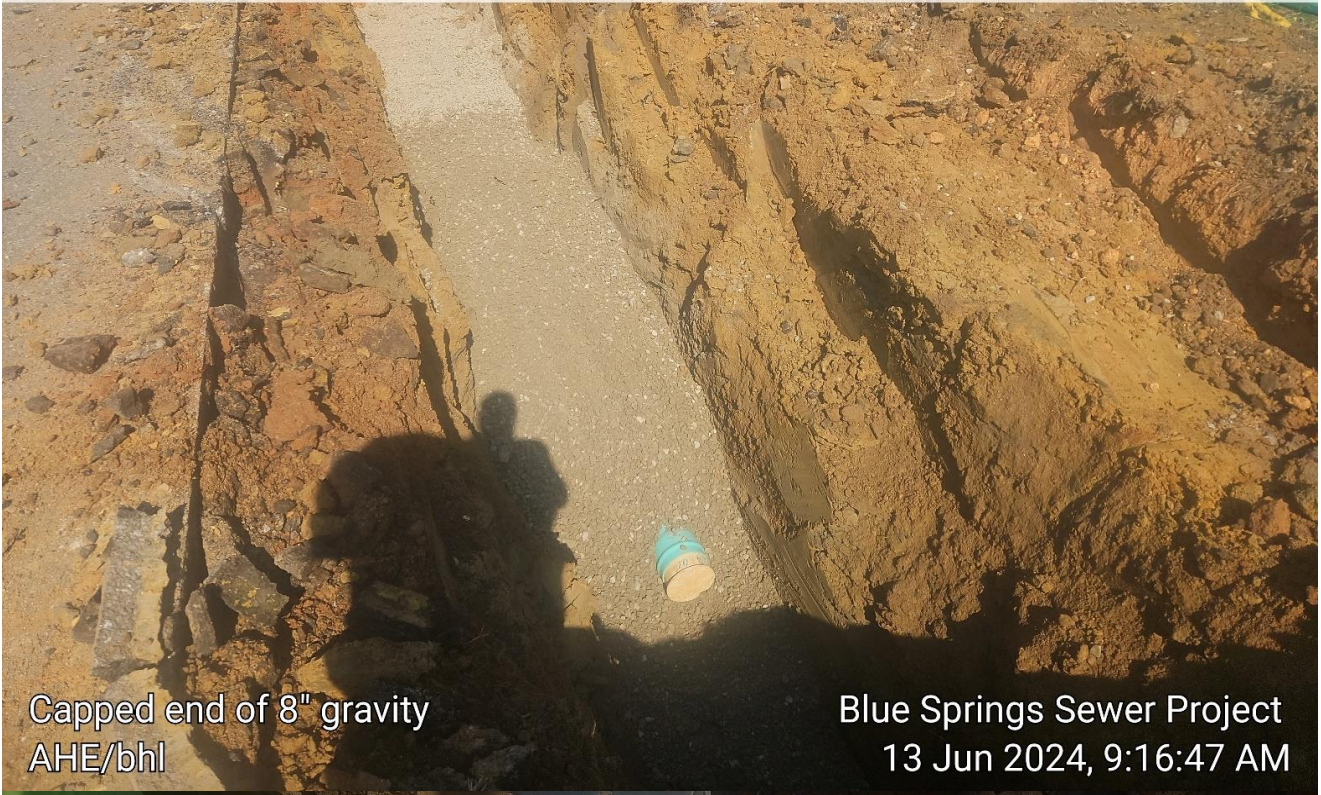

Capped end of 8" gravity  
AHE/bhl

Blue Springs Sewer Project  
13 Jun 2024, 9:16:47 AM



☉ 18° N (T) ● 30.783456, -85.17619 ±3 m ▲ 15m



Installation of MH249  
AHE/bhl

Blue Springs Sewer Project  
14 Jun 2024, 10:01:07 AM
