

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 6/27/2024
For Project: **Indian Springs Sewer Phase 2B**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
Contractor: Blankenship Contracting, Inc.
Designer: Alday-Howell Engineering
Inspector: Dwayne Josey (850) 258-3386
Notice to Proceed: 8/1/2023 Award Date: 12/13/2022



Substantial Completion: 6/23/2024 Final Completion: 8/22/2024

The report is for the week of: Monday, 6/17/2024 thru Sunday, 6/23/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Directional bored under roadway installing services to right of way.

Tuesday- Paved turnout at Clubhouse Dr. Installed services to right of way.

Wednesday- Installed 200 LF of 2" low pressure force main. Completed paving structural lift.

Thursday- Installed 160 LF of 2" low pressure force main.

Friday- Installed services to right of way.


Saturday- No work at contractor's option.


Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	34%	Time Remaining (%):	0%
Invoiced to Date:	\$1,857,047.85	Weather days to date:	11
Original Contract Amount:	\$6,377,639.99	Holiday days granted:	16
Change Order Amount Approved:		Actual Days:	328
Remaining:	\$4,520,592.14	Days used with deduct:	301
Days to Substantial Completion:	300	Remaining to SC:	-1
Days to Final Completion:	360	Remaining to FC:	59

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)

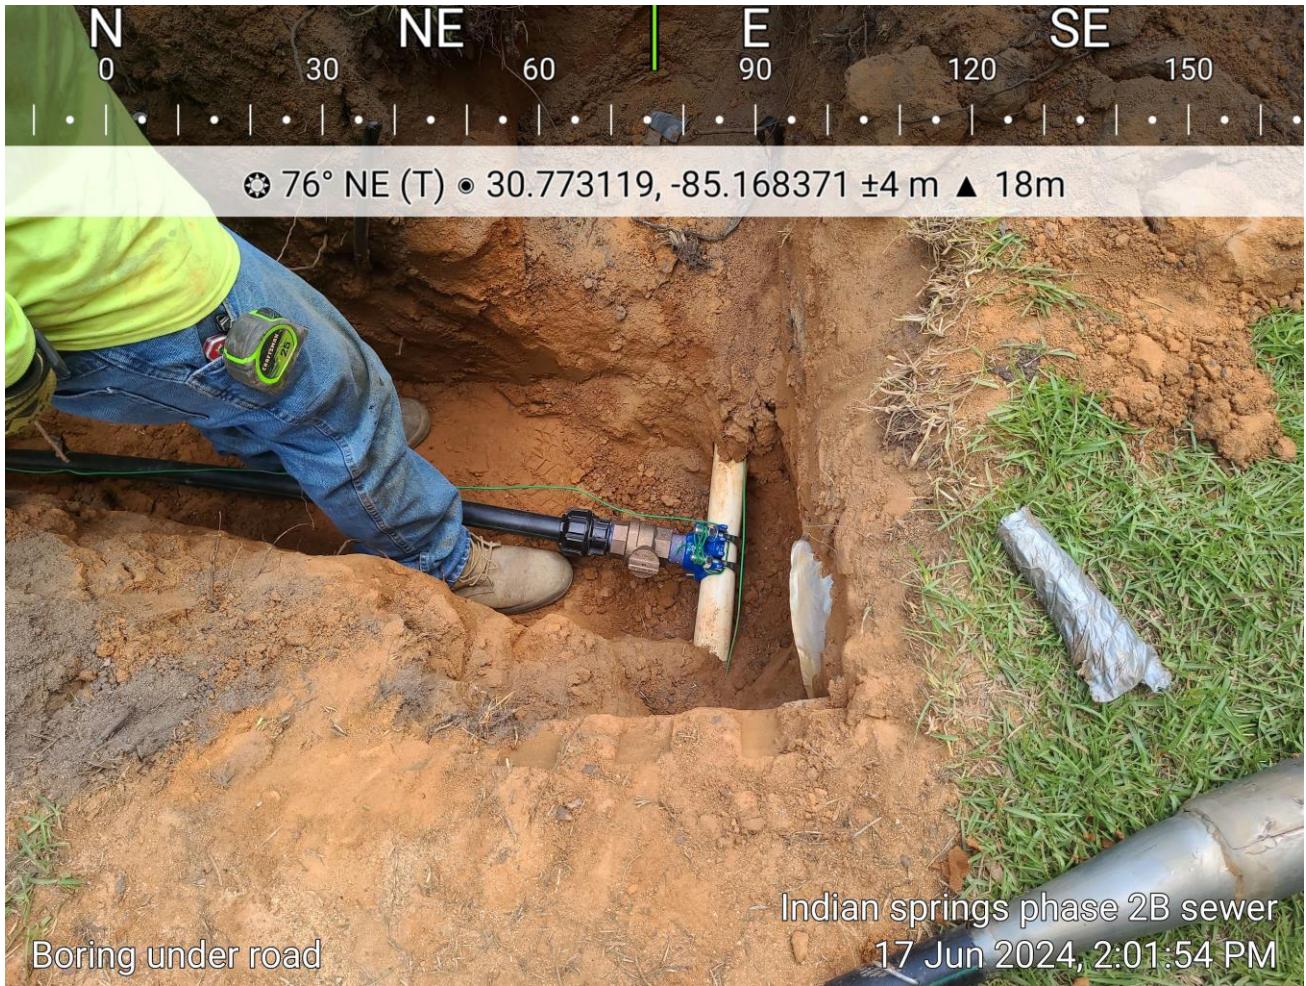



☉ 319° NW (T) ● 30.768743, -85.165143 ±3 m ▲ 21m



Spread asphalt

Indian springs phase 2B sewer
18 Jun 2024, 7:27:47 AM




☉ 220° SW (T) ● 30.778077, -85.15957 ±18 m ▲ 23m



Start joint

Indian springs phase 2B sewer
19 Jun 2024, 7:01:53 AM



☼ 193° S (T) ● 30.773042, -85.169024 ±6 m ▲ 17m



2 in FM

Indian springs phase 2B sewer
20 Jun 2024, 10:23:25 AM



☼ 260° W (T) ● 30.773109, -85.168695 ±7 m ▲ 17m



2 in FM service

Indian springs phase 2B sewer
21 Jun 2024, 10:00:23 AM
