

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
 Prepared by: Alday-Howell Engineering, Inc.
 Prepared on: 6/25/2024
 For Project: **Blue Springs Road Sewer Extensions Phase 1**
NFWFMD Const. Grant Agreement No. 17-061 AHE # 17-062
 Contractor: L & K Contracting, Inc.
 Designer: Alday-Howell Engineering Inspector: Brett Lawrence (850) 718-7233
 Notice to Proceed: 9/27/2022 Award Date: 6/29/2022



Substantial Completion: 2/25/2024 Final Completion: 3/26/2024

The report is for the week of: Monday, 6/17/2024 thru Sunday, 6/23/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

- Monday-** Installed 1 lateral and 98 LF of 8" gravity sewer pipe. Installed 24 lf of 24" RCP.
- Tuesday-** Installed 1 lateral and 112 LF of 8" gravity sewer pipe. Installed 24 lf of 24" RCP. Poured lift station pad.
- Wednesday-** Installed 70 LF of 8" gravity sewer pipe.
- Thursday-** Installed 70 LF of 8" gravity sewer pipe.
- Friday-** Cleaned up lay down yard.
- Saturday-** No work at contractor's option.
- Sunday-** No work at contractor's option.


Engineer's remarks/Pending issues:

Percent Project Complete:	56%	Time Remaining (%):	-27%
Invoiced to Date:	\$2,778,986.09	Weather days to date:	36
Original Contract Amount:	\$5,347,467.37	Holiday days granted:	39
Change Order Amount Approved:	\$83,361.30	Actual Days:	636
Contract Time Approved:	141	Days used with deduct:	561
Remaining:	\$2,651,842.58		
Days to Substantial Completion:	441	Original SC:	300
		Remaining to SC:	-120
Days to Final Completion:	471	Original FC:	330
		Remaining to FC:	-90

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)



☉ 134° SE (T) • 30.781881, -85.185423 ±4 m ▲ 25m

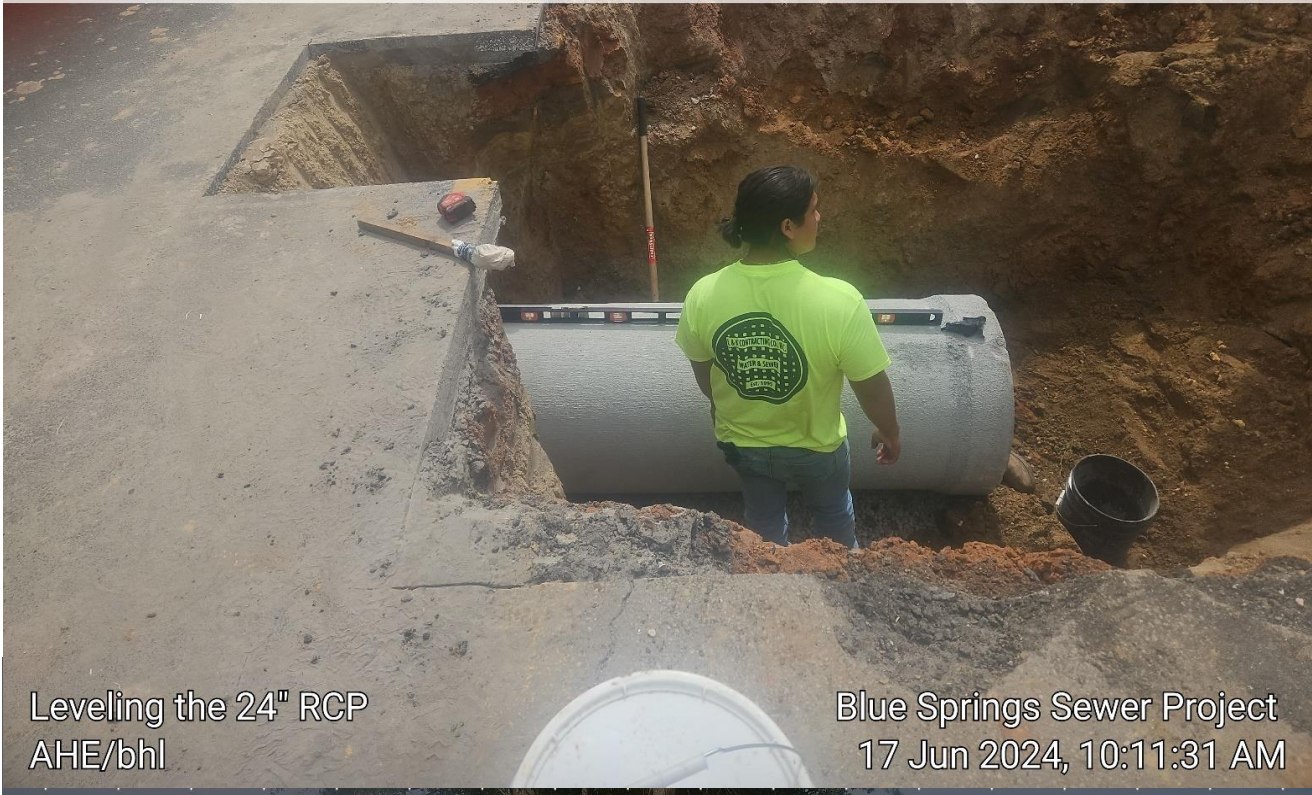

Leveling the 24" RCP
AHE/bhl

Blue Springs Sewer Project
17 Jun 2024, 10:11:31 AM

☉ 84° E (T) • 30.783172, -85.178654 ±3 m ▲ 22m




Preparing the lift station for cement
AHE/bhl

Blue Springs Sewer Project
17 Jun 2024, 4:50:48 PM

North Elevation

☉ 193° S (T) ● 30.783304, -85.177228 ±3 m ▲ 10m

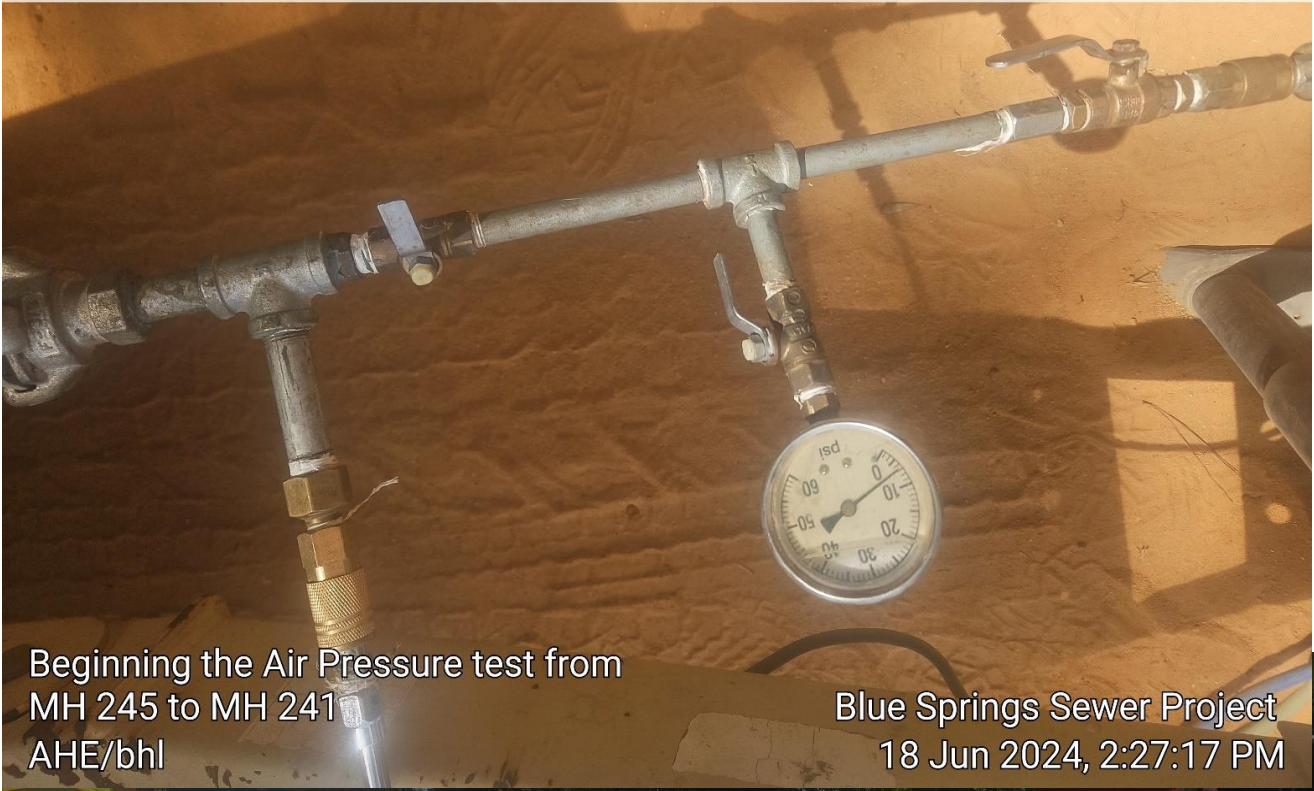

Beginning the Air Pressure test from
MH 245 to MH 241
AHE/bhl

Blue Springs Sewer Project
18 Jun 2024, 2:27:17 PM

☉ 18° N (T) ● 30.781838, -85.185423 ±4 m ▲ 24m



Installation of 24" RCP at 219+90
(BSR)
AHE/bhl

Blue Springs Sewer Project
17 Jun 2024, 12:07:02 PM
