

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
 Prepared by: Alday-Howell Engineering, Inc.
 Prepared on: 7/23/2024
 For Project: **Blue Springs Road Sewer Extensions Phase 1**
NFWFMD Const. Grant Agreement No. 17-061 AHE # 17-062
 Contractor: L & K Contracting, Inc.
 Designer: Alday-Howell Engineering Inspector: Brett Lawrence (850) 718-7233
 Notice to Proceed: 9/27/2022 Award Date: 6/29/2022



Substantial Completion: 3/7/2024 Final Completion: 4/6/2024

The report is for the week of: Monday, 7/15/2024 thru Sunday, 7/21/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

- Monday-** Installed 64 LF of 24" RCP.
- Tuesday-** Installed 46 LF of 4" gravity force main.
- Wednesday-** Installed mitered end.
- Thursday-** Added lime rock base.
- Friday-** Cleaned up construction area. Rain affected more than 50% of the day. Rain day granted.
- Saturday-** Rain affected more than 50% of the day. Rain day granted.
- Sunday-** Rain affected more than 50% of the day. Rain day granted.

Engineer's remarks/Pending issues:

Percent Project Complete:	61%	Time Remaining (%):	-31%
Invoiced to Date:	\$2,959,986.89	Weather days to date:	42
Original Contract Amount:	\$5,347,467.37	Holiday days granted:	44
Change Order Amount Approved:	\$83,361.30	Actual Days:	664
Contract Time Approved:	141	Days used with deduct:	578
Remaining:	\$2,470,841.78		
Days to Substantial Completion:	441	Original SC:	300
		Remaining to SC:	-137
Days to Final Completion:	471	Original FC:	330
		Remaining to FC:	-107

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)

5013 Co Rd 164, Marianna, FL 32446, USA


☉ 227° SW (T) • 30.783138, -85.177219 ±3 m ▲ 13m



Working on road at cross drain
(245+90)
AHE/bhl

Blue Springs Sewer Project
17 Jul 2024, 9:43:00 AM

☉ 279° W (T) • 30.783137, -85.177222 ±3 m ▲ 13m

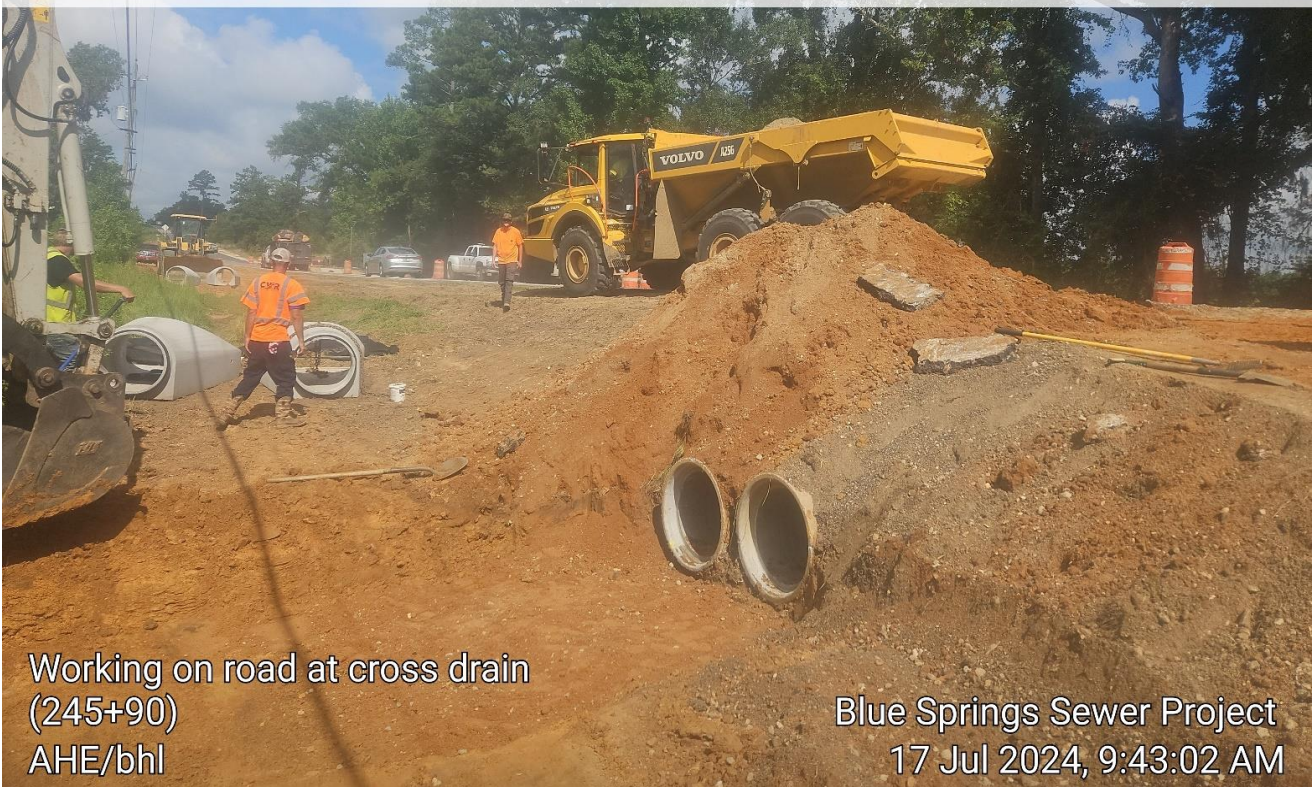

Working on road at cross drain
(245+90)
AHE/bhl

Blue Springs Sewer Project
17 Jul 2024, 9:43:02 AM

4922 Pope Chapel Cir, Marianna, FL 32446, USA

☉ 169° S (T) • 30.782049, -85.185431 ±3 m ▲ 24m



Mitered end section at 219+90
AHE/bhl

Blue Springs Sewer Project
18 Jul 2024, 2:18:30 PM

☉ 233° SW (T) • 30.782017, -85.185402 ±6 m ▲ 24m



Mitered end section at 219+90
AHE/bhl

Blue Springs Sewer Project
18 Jul 2024, 2:21:19 PM
