

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
 Prepared by: Alday-Howell Engineering, Inc.
 Prepared on: 8/12/2024
 For Project: **Blue Springs Road Sewer Extensions Phase 1**
NFWFMD Const. Grant Agreement No. 17-061 AHE # 17-062
 Contractor: L & K Contracting, Inc.
 Designer: Alday-Howell Engineering Inspector: Brett Lawrence (850) 718-7233
 Notice to Proceed: 9/27/2022 Award Date: 6/29/2022



Substantial Completion: 3/11/2024 Final Completion: 4/10/2024

The report is for the week of: Monday, 8/5/2024 thru Sunday, 8/11/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Installed 50 LF of 8" force main. Paved section of structural asphalt.

Tuesday- Moved automated traffic signal. Removed asphalt in preparation to install gravity sewer main.

Wednesday- Removed asphalt in preparation to install gravity sewer main.

Thursday- Installed 56 LF of 8" gravity main.

Friday- Temporarily repaired asphalt deficiencies.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	61%	Time Remaining (%):	-35%
Invoiced to Date:	\$2,959,986.89	Weather days to date:	46
Original Contract Amount:	\$5,347,467.37	Holiday days granted:	44
Change Order Amount Approved:	\$83,361.30	Actual Days:	685
Contract Time Approved:	141	Days used with deduct:	595
Remaining:	\$2,470,841.78		
Days to Substantial Completion:	441	Original SC:	300
		Remaining to SC:	-154
Days to Final Completion:	471	Original FC:	330
		Remaining to FC:	-124

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)

5021 Co Rd 164, Marianna, FL 32446, USA

☉ 54° NE (T) • 30.783389, -85.176551 ±3 m ▲ 12m



A/C paving section of BSR from station 241+76 to Station 253+20
AHE/bhl

Blue Springs Sewer Project
05 Aug 2024, 10:16:53 AM

☉ 300° W (T) • 30.78339, -85.17655 ±3 m ▲ 10m



A/C paving section of BSR from station 241+76 to Station 253+20
AHE/bhl

Blue Springs Sewer Project
05 Aug 2024, 10:17:06 AM

5055 Co Rd 164, Marianna, FL 32446, USA

☉ 153° SE (T) ● 30.784014, -85.173671 ±4 m ▲ 15m



Beginning of hydrostatic Pressure Testing 256+80 to 257+30
AHE/bhl

Blue Springs Sewer Project
05 Aug 2024, 1:09:43 PM

☉ 195° S (T) ● 30.783994, -85.173684 ±4 m ▲ 21m



Ending hydrostatic Pressure test (256+80 to 257+30)
AHE/bhl

Blue Springs Sewer Project
05 Aug 2024, 3:02:12 PM

2994 Chase Way, Marianna, FL 32446, USA

☉ 284° W (T) ● 30.782805, -85.174971 ±62 m ▲ 19m



Beginning to install 8" gravity pipe at station 253+20
AHE/bhl

Blue Springs Sewer Project
07 Aug 2024, 11:08:15 AM

☉ 283° W (T) ● 30.783743, -85.174756 ±3 m ▲ 17m



Beginning to install 8" gravity pipe at station 253+20
AHE/bhl

Blue Springs Sewer Project
07 Aug 2024, 11:08:27 AM

3004 Chase Way, Marianna, FL 32446, USA


☉ 187° S (T) • 30.783765, -85.174704 ±3 m ▲ 17m



Excavating around underground wire crossing Blue Springs Road
AHE/bhl

Blue Springs Sewer Project
08 Aug 2024, 9:53:43 AM

☉ 166° SE (T) • 30.783766, -85.174694 ±3 m ▲ 17m

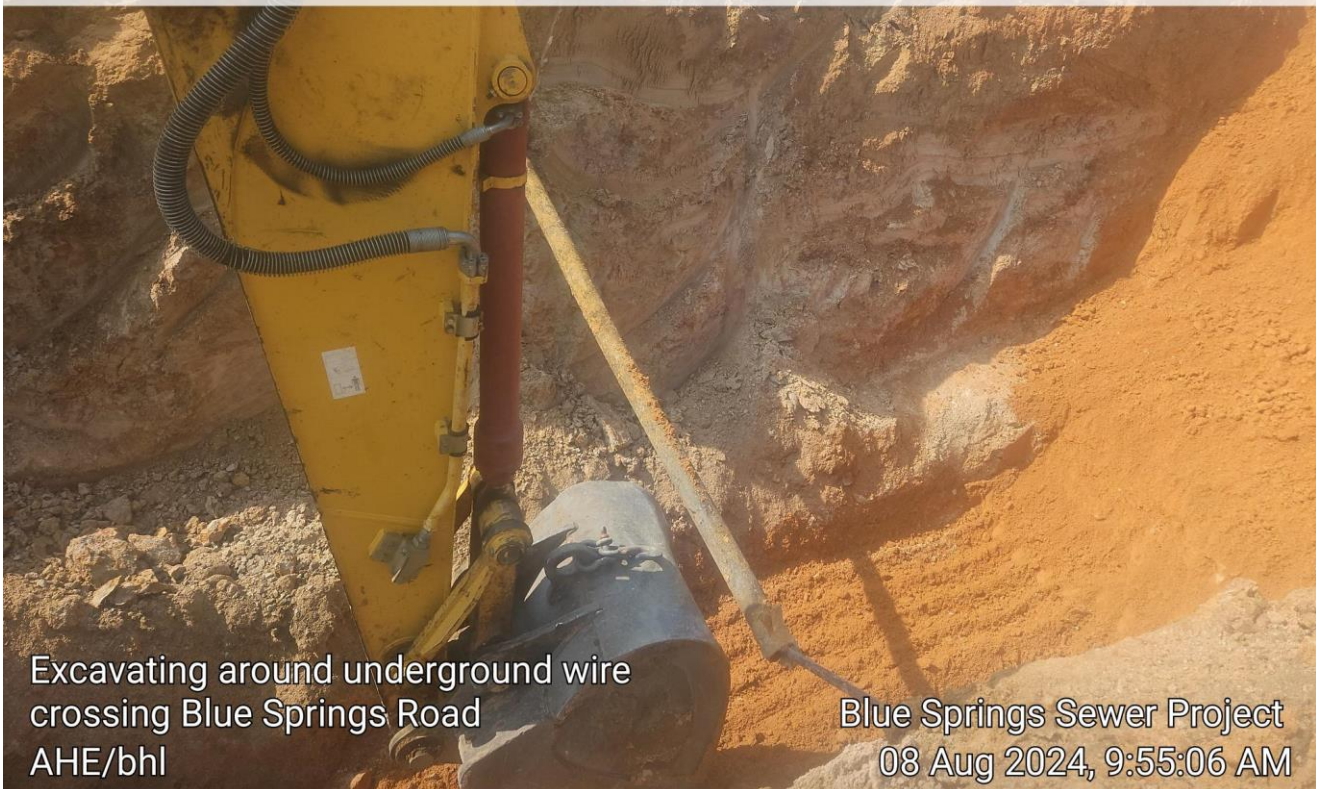

Excavating around underground wire crossing Blue Springs Road
AHE/bhl

Blue Springs Sewer Project
08 Aug 2024, 9:55:06 AM
