

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 8/20/2024
For Project: **Indian Springs Sewer Phase 2B**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
Contractor: Blankenship Contracting, Inc.
Designer: Alday-Howell Engineering
Notice to Proceed: 8/1/2023



Inspector: Dwayne Josey (850) 258-3386

Award Date: 12/13/2022

Substantial Completion: 6/30/2024

Final Completion: 8/29/2024

The report is for the week of: Monday, 8/12/2024

thru Sunday, 8/18/2024


The contractor performed the following operations this week. Sub work is noted in parenthesis:

- Monday-** Corrected leaks found in hydrostatic testing.
- Tuesday-** Poured valve pads.
- Wednesday-** Corrected leaks found in hydrostatic testing. Poured valve pads.
- Thursday-** Corrected leaks found in hydrostatic testing.
- Friday-** Corrected leaks found in hydrostatic testing.
- Saturday-** No work at contractor's option.
- Sunday-** No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	44%	Time Remaining (%):	-17%
Invoiced to Date:	\$2,533,904.35	Weather days to date:	13
Original Contract Amount:	\$6,377,639.99	Holiday days granted:	21
Change Order Amount Approved:		Actual Days:	384
Remaining:	\$3,843,735.64	Days used with deduct:	350
Days to Substantial Completion:	300	Remaining to SC:	-50
Days to Final Completion:	360	Remaining to FC:	10

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)



☼ 301° W (T) ● 30.777917, -85.159732 ±5 m ▲ 17m



Clean out pad

Indian springs phase 2B sewer
13 Aug 2024, 12:32:15 PM




☼ 35° NE (T) ● 30.770269, -85.165863 ±25 m ▲ 20m




Clean out pad

Indian springs phase 2B sewer
13 Aug 2024, 2:59:00 PM



☼ 11° N (T) ● 30.775883, -85.16799 ±3 m ▲ 20m

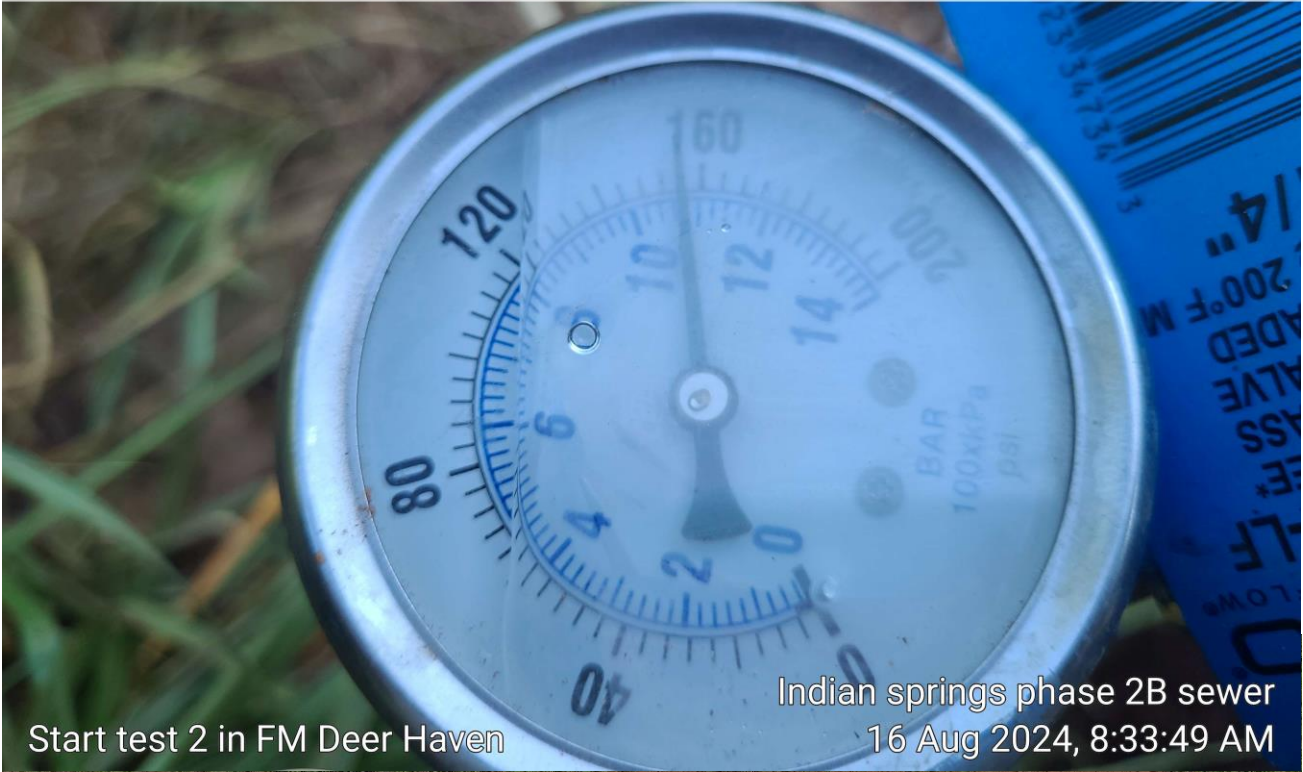

Start test 2 in FM Deer Haven

Indian springs phase 2B sewer
16 Aug 2024, 8:33:49 AM
