

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL

Prepared by: Alday-Howell Engineering, Inc.

Prepared on: 9/3/2024

For Project: **Blue Springs Road Sewer Extensions Phase 1**
NFWFMD Const. Grant Agreement No. 17-061 AHE # 17-062

Contractor: L & K Contracting, Inc.

Designer: Alday-Howell Engineering Inspector: Brett Lawrence (850) 718-7233

Notice to Proceed: 9/27/2022 Award Date: 6/29/2022



Substantial Completion: 3/14/2024

Final Completion: 4/13/2024

The report is for the week of: Monday, 8/26/2024

thru Sunday, 9/1/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Performed CCTV on gravity main.

Tuesday- Performed CCTV on gravity main.

Wednesday- Aligned manhole steps. Cleaned construction area.

Thursday- Aligned manhole steps. Cleaned construction area. Began installing sewer meter.

Friday- No work due to holiday. Holiday day granted.

Saturday- No work due to holiday. Holiday day granted.

Sunday- No work due to holiday. Holiday day granted.

Engineer's remarks/Pending issues:

Percent Project Complete:	61%	Time Remaining (%):	-39%		
Invoiced to Date:	\$3,004,234.28	Weather days to date:	46		
Original Contract Amount:	\$5,347,467.37	Holiday days granted:	47		
Change Order Amount Approved:	\$83,361.30	Actual Days:	706		
Contract Time Approved:	141	Days used with deduct:	613		
Remaining:	\$2,426,594.39				
Days to Substantial Completion:	441	Original SC:	300	Remaining to SC:	-172
Days to Final Completion:	471	Original FC:	330	Remaining to FC:	-142

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)

3003 Chase Way, Marianna, FL 32446, USA


☉ 194° S (T) • 30.783687, -85.174913 ±19ft ▲ 55ft



L and K contractors setting up to flush and vac 8" gravity pipe from MH 253 to MH 257
AHE/bhl

Blue Springs Sewer Project
26 Aug 2024, 8:21:00 AM

☉ 86° E (T) • 30.783688, -85.174909 ±13ft ▲ 55ft

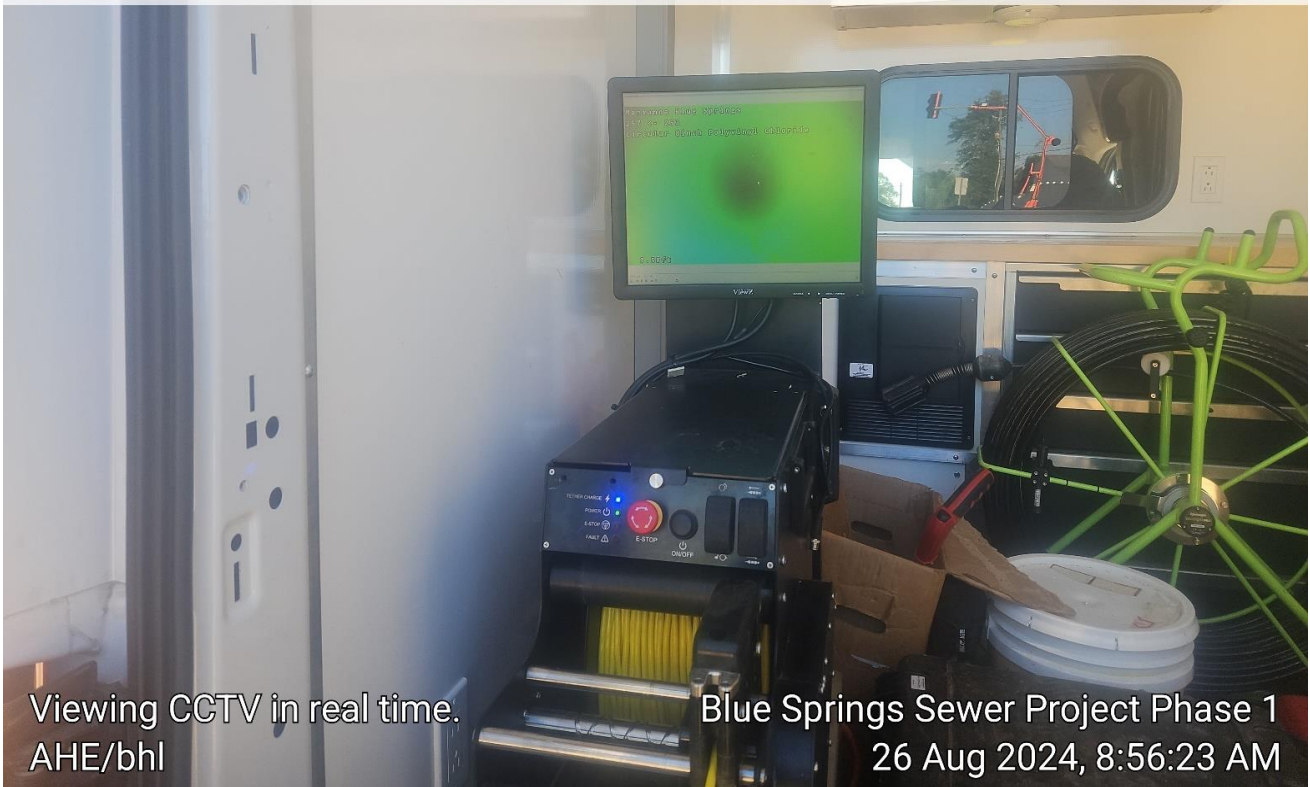

Viewing CCTV in real time.
AHE/bhl

Blue Springs Sewer Project Phase 1
26 Aug 2024, 8:56:23 AM

2829 Greenwood Hwy, Marianna, FL 32446, USA

☉ 93° E (T) ● 30.770215, -85.202374 ±9ft ▲ 26ft



Sewer Meter assembly with vault @
Hwy 71
AHE/bhl

Blue Springs Sewer Project
28 Aug 2024, 2:42:07 PM

☉ 297° W (T) ● 30.770156, -85.202372 ±23ft ▲ 26ft



Sewer Meter assembly with vault @
Hwy 71
AHE/bhl

Blue Springs Sewer Project
28 Aug 2024, 2:42:51 PM

2941 Co Rd 164, Marianna, FL 32446, USA

☉ 302° W (T) ● 30.779385, -85.193279 ±39ft ▲ 75ft



Removing brass ARV valves and replacing them with stainless steel per contract plans.
AHE/bhl

Blue Springs Sewer Project
29 Aug 2024, 11:55:49 AM
