

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
 Prepared by: Alday-Howell Engineering, Inc.
 Prepared on: 9/18/2024
 For Project: **Blue Springs Road Sewer Extensions Phase 1**
NFWFMD Const. Grant Agreement No. 17-061 AHE # 17-062
 Contractor: L & K Contracting, Inc.
 Designer: Alday-Howell Engineering Inspector: Brett Lawrence (850) 718-7233
 Notice to Proceed: 9/27/2022 Award Date: 6/29/2022



Substantial Completion: 3/16/2024 Final Completion: 4/15/2024

The report is for the week of: Monday, 9/9/2024 thru Sunday, 9/15/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Repaired damaged laterals to correct infiltration.

Tuesday- Repaired damaged laterals to correct infiltration.

Wednesday- Repaired main to correct infiltration.

Thursday- No work due to rain. Ran day granted.

Friday- Lowered manholes.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	61%	Time Remaining (%):	-42%
Invoiced to Date:	\$3,004,234.28	Weather days to date:	48
Original Contract Amount:	\$5,347,467.37	Holiday days granted:	47
Change Order Amount Approved:	\$83,361.30	Actual Days:	720
Contract Time Approved:	141	Days used with deduct:	625
Remaining:	\$2,426,594.39		
Days to Substantial Completion:	441	Original SC:	300
		Remaining to SC:	-184
Days to Final Completion:	471	Original FC:	330
		Remaining to FC:	-154

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)

4922 Pope Chapel Cir, Marianna, FL 32446, USA

📍 186° S (T) • 30.781912, -85.185591 ±9ft ▲ 78ft



AHE/bhl

16 Sep 2024, 10:26:11 AM

📍 99° E (T) • 30.78237, -85.182849 ±9ft ▲ 78ft




L and Construction making repairs on lateral at station 228+18
AHE/bhl

Blue Springs Sewer Project Phase 1
09 Sep 2024, 2:55:16 PM

4934 Pope Chapel Cir, Marianna, FL 32446, USA

☼ 204° S (T) • 30.782135, -85.184246 ±9ft ▲ 78ft

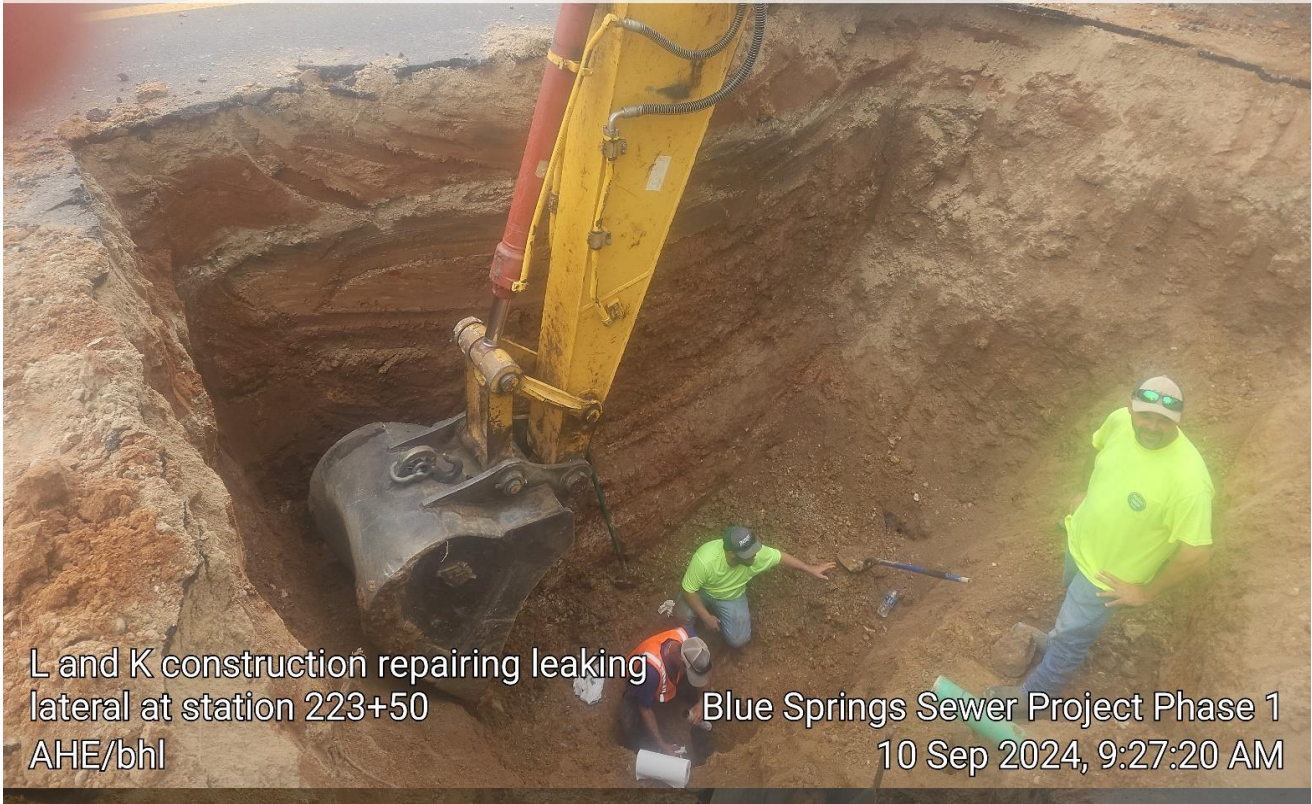

L and K construction repairing leaking lateral at station 223+50
AHE/bhl

Blue Springs Sewer Project Phase 1
10 Sep 2024, 9:27:20 AM

☼ 84° E (T) • 30.782362, -85.182808 ±9ft ▲ 78ft



L and Construction making repairs on lateral at station 228+18
AHE/bhl

Blue Springs Sewer Project Phase 1
09 Sep 2024, 1:28:40 PM
