

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 10/14/2024
For Project: **Blue Springs Road Sewer Extensions Phase 2**
NFWFMD Const. Grant Agreement No. 17-061 AHE # 23-013
Contractor: Gulf Coast Underground Contracting LLC.
Designer: Alday-Howell Engineering Inspector: Brett Lawrence (850) 718-7233
Notice to Proceed: 8/12/2024 Award Date: 12/12/2023



Substantial Completion: 5/16/2025 Final Completion: 7/15/2025

The report is for the week of: Monday, 10/7/2024 thru Sunday, 10/13/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Installed 380 LF of 2" low pressure PVC force main.

Tuesday- Installed 3 cleanouts, 2 valves, 600 LF of 2" low pressure PVC force main.

Wednesday- Installed 4 low pressure services.

Thursday- Installed 700 LF of 2" low pressure PVC force main.

Friday- Cleaned construction area.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	18%	Time Remaining (%):	79%
Invoiced to Date:	\$469,102.46	Weather days to date:	3
Original Contract Amount:	\$2,975,353.25	Holiday days granted:	4
Change Order Amount Approved:	\$0.00	Actual Days:	63
Contract Time Approved:		Days used with deduct:	56
Remaining:	\$2,506,250.79	Remaining to SC:	214
Days to Substantial Completion:	270	Remaining to FC:	274
Days to Final Completion:	330		

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)




5° N (T) • 30.779678, -85.182552 ±5 m ▲ 24m



2 in FM

Blue springs
07 Oct 2024, 9:43:12 AM

76° NE (T) • 30.780714, -85.182603 ±4 m ▲ 18m

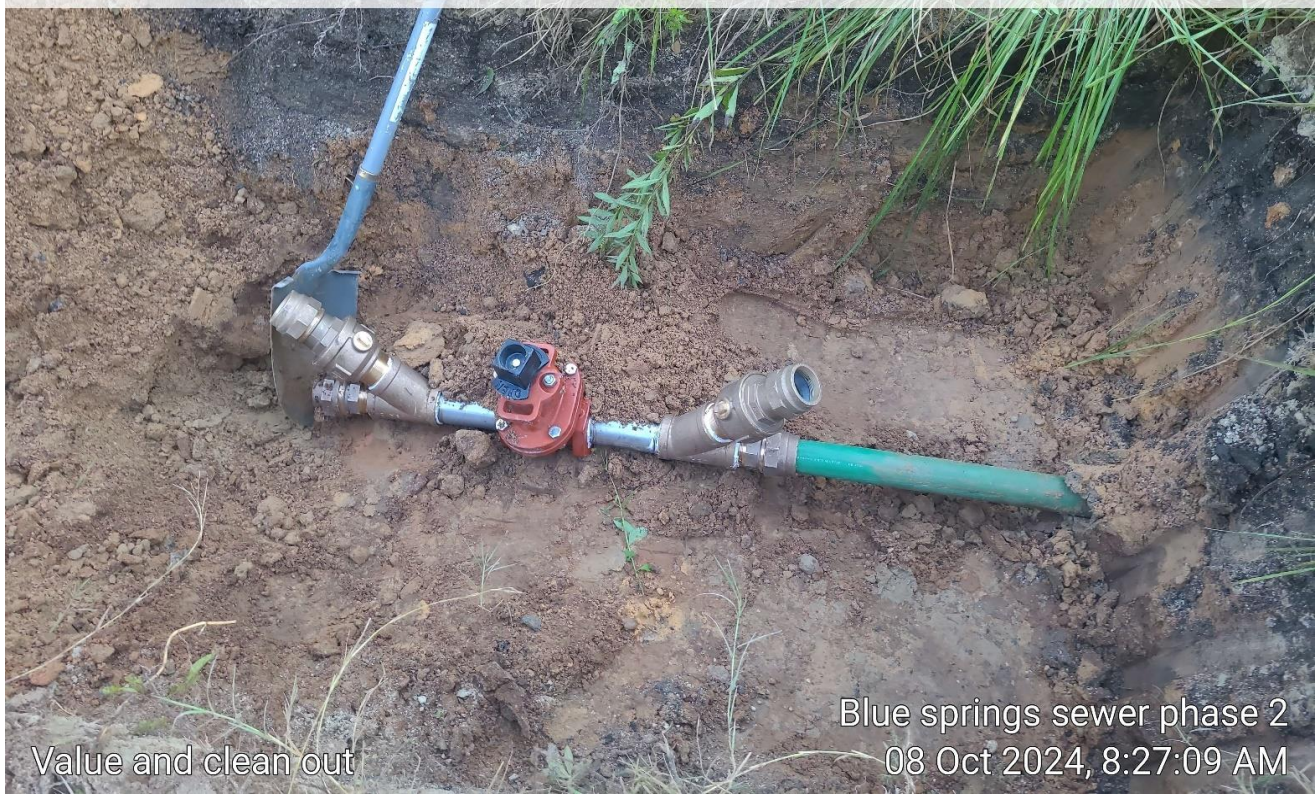

Value and clean out

Blue springs sewer phase 2
08 Oct 2024, 8:27:09 AM



☉ 117° E (T) • 30.779691, -85.18256 ±11 m ▲ 23m



2 in FM

Blue springs
07 Oct 2024, 9:42:47 AM

☉ 353° N (T) • 30.780634, -85.182545 ±3 m ▲ 22m



2in FM

Blue springs sewer
08 Oct 2024, 9:38:54 AM
