

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 10/22/2024
For Project: **Blue Springs Road Sewer Extensions Phase 2**
NFWFMD Const. Grant Agreement No. 17-061 AHE # 23-013
Contractor: Gulf Coast Underground Contracting LLC.
Designer: Alday-Howell Engineering Inspector: Brett Lawrence (850) 718-7233
Notice to Proceed: 8/12/2024 Award Date: 12/12/2023



Substantial Completion: 5/16/2025 Final Completion: 7/15/2025

The report is for the week of: Monday, 10/14/2024 thru Sunday, 10/20/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- No work at contractor's option.

Tuesday- Installed 1 gravity service.

Wednesday- Installed 1 gravity service.

Thursday- Performed hydrostatic pressure testing.

Friday- Performed hydrostatic pressure testing.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	18%	Time Remaining (%):	77%
Invoiced to Date:	\$469,102.46	Weather days to date:	3
Original Contract Amount:	\$2,975,353.25	Holiday days granted:	4
Change Order Amount Approved:	\$0.00	Actual Days:	70
Contract Time Approved:		Days used with deduct:	63
Remaining:	\$2,506,250.79	Remaining to SC:	207
Days to Substantial Completion:	270	Remaining to FC:	267
Days to Final Completion:	330		

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)

4901 Firstclass Ave, Marianna, FL 32446, USA


☉ 185°S (T) • 30.779436, -85.18727 ±9ft ▲ 88ft



Preparing for hydrostatic Pressure test
AHE/bhl

Blue Springs Sewer Project Phase 2
17 Oct 2024, 10:11:29 AM

☉ 77°NE (T) • 30.780636, -85.182586 ±9ft ▲ 55ft

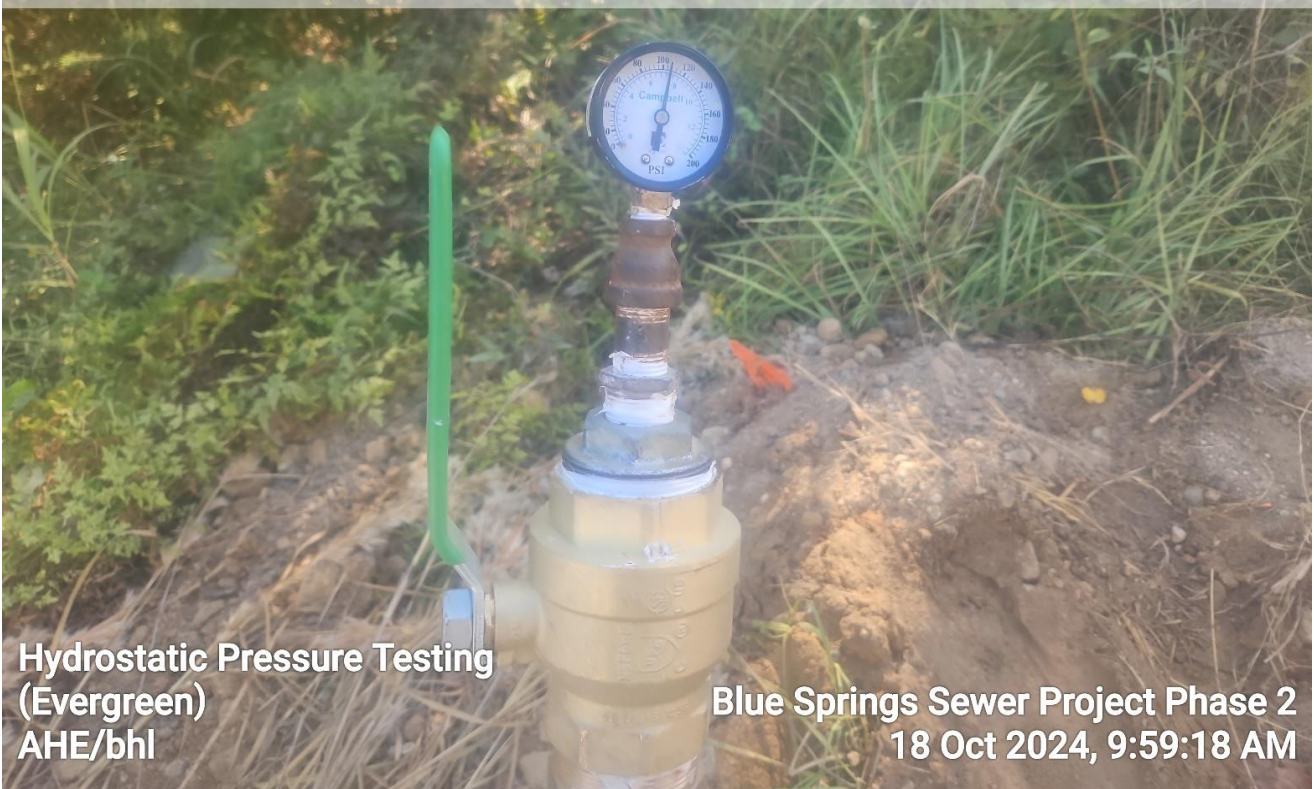

Hydrostatic Pressure Testing (Evergreen)
AHE/bhl

Blue Springs Sewer Project Phase 2
18 Oct 2024, 9:59:18 AM

2974 Evergreen Ln, Marianna, FL 32446, USA

☉ 56°NE (T) • 30.780637, -85.182571 ±9ft ▲ 55ft



AHE/bhl

**Blue Springs Sewer Project Phase 2
18 Oct 2024, 10:59:36 AM**

☉ 66°NE (T) • 30.780615, -85.182554 ±39ft ▲ 75ft



**Hydrostatic Pressure Testing. Final
reading. (EVERGREEN RD)
AHE/bhl**

**Blue Springs Sewer Project Phase 2
18 Oct 2024, 12:06:34 PM**
