

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL

Prepared by: Alday-Howell Engineering, Inc.

Prepared on: 11/18/2024

For Project: **Blue Springs Road Sewer Extensions Phase 2**

NFWFMD Const. Grant Agreement No. 17-061 AHE # 23-013

Contractor: Gulf Coast Underground Contracting LLC.

Designer: Alday-Howell Engineering

Inspector: Brett Lawrence (850) 718-7233

Notice to Proceed: 8/12/2024

Award Date: 12/12/2023



Substantial Completion: 5/17/2025

Final Completion: 7/16/2025

The report is for the week of: Monday, 11/11/2024

thru Sunday, 11/17/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- No work due to holiday. Holiday day granted.

Tuesday- No work at contractor's option.

Wednesday- Installed 98 LF of 8" PVC gravity main.

Thursday- Installed manhole 261 and 42 LF of 8" PVC gravity main.

Friday- Installed 56 LF of 8" PVC gravity main.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete: 29%

Time Remaining (%): 67%

Invoiced to Date: \$787,389.33

Weather days to date: 3

Original Contract Amount: \$2,975,353.25

Change Order Amount Approved: \$0.00

Holiday days granted: 5

Contract Time Approved:

Actual Days: 98

Remaining: \$2,187,963.92

Days used with deduct: 90

Days to Substantial Completion: 270

Remaining to SC: 180

Days to Final Completion: 330


Remaining to FC: 240

A handwritten signature in blue ink, appearing to read 'Rob B', is written over a horizontal line.

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)

5054 Blue Springs Rd, Marianna, FL 32446, USA

⊙ 69°NE (T) ⊙ 30.784181, -85.173442 ±16ft ▲ 49ft

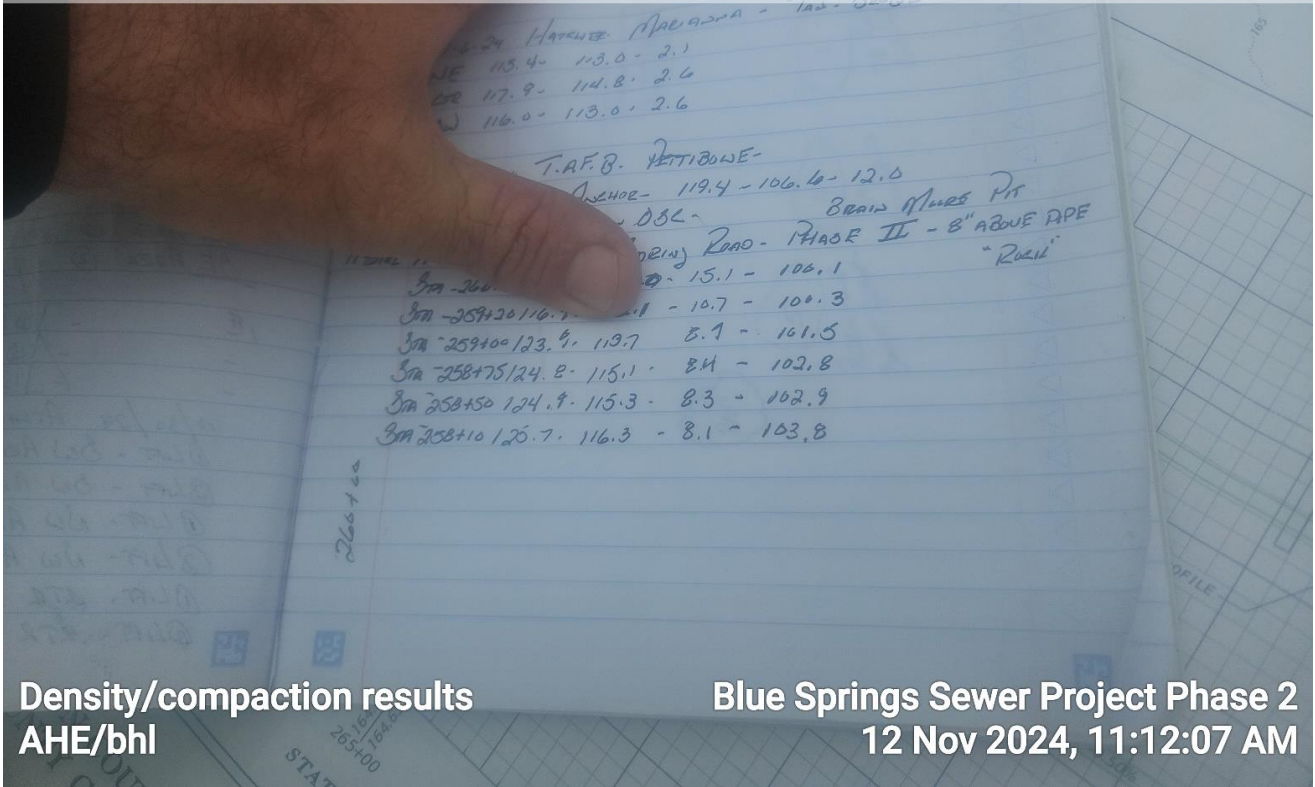

Density/compaction results
AHE/bhl

Blue Springs Sewer Project Phase 2
12 Nov 2024, 11:12:07 AM

⊙ 49°NE (T) ⊙ 30.784305, -85.173047 ±9ft ▲ 62ft



8" gravity pipe
AHE/bhl

Blue Springs Sewer Project Phase 2
13 Nov 2024, 7:43:53 AM

5071 Blue Springs Rd, Marianna, FL 32446, USA

☉ 225°SW (T) • 30.784437, -85.172652 ±9ft ▲ 59ft



Setting MH261
AHE/bhl

Blue Springs Sewer Project Phase 2
14 Nov 2024, 11:08:23 AM

☉ 160°SE (T) • 30.784487, -85.172666 ±13ft ▲ 59ft



J&M testing lab on-site to conduct
density testing
AHE/bhl

Blue Springs Sewer Project Phase 2
15 Nov 2024, 12:16:30 PM
