

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL

Prepared by: Alday-Howell Engineering, Inc.

Prepared on: 11/11/2024

For Project: **Indian Springs Sewer Phase 2C**

NFWMD Const. Grant Agreement No. 20-036 AHE # 20-033

Contractor: Blankenship Contracting, Inc.

Designer: Alday-Howell, Engineering

Inspector: Jake Edenfield (850) 718-7233

Notice to Proceed: 11/4/2024

Award Date: 12/13/2022

Substantial Completion: 8/31/2025

Final Completion: 10/30/2025

The report is for the week of: Monday, 11/4/2024

thru Sunday, 11/10/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Notice to proceed. Delivered manholes. Attended pre-construction meeting.

Tuesday- Surveyed project.

Wednesday- Surveyed project.

Thursday- Installed manhole 1641 on Oak Dr.

Friday- Cleaned construction area.

Saturday- No work. Contractor's option.

Sunday- No work. Contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete: 0%

Time Remaining (%): 98%

Invoiced to Date: \$0.00

Weather days to date:

Original Contract Amount: \$6,168,668.47

Change Order Amount Approved:

Holiday days granted:

Actual Days: 7

Remaining: \$6,168,668.47

Days used with deduct: 7

Days to Substantial Completion: 300

Remaining to SC: 293

Days to Final Completion: 360

Remaining to FC: 353



Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)






305°NW (T) • 30.780009, -85.155246 ±9m ▲ 16m



Manhole

Indian springs sewer 2C
04 Nov 2024, 9:35:42 AM

301°W (T) • 30.779284, -85.155348 ±5m ▲ 16m

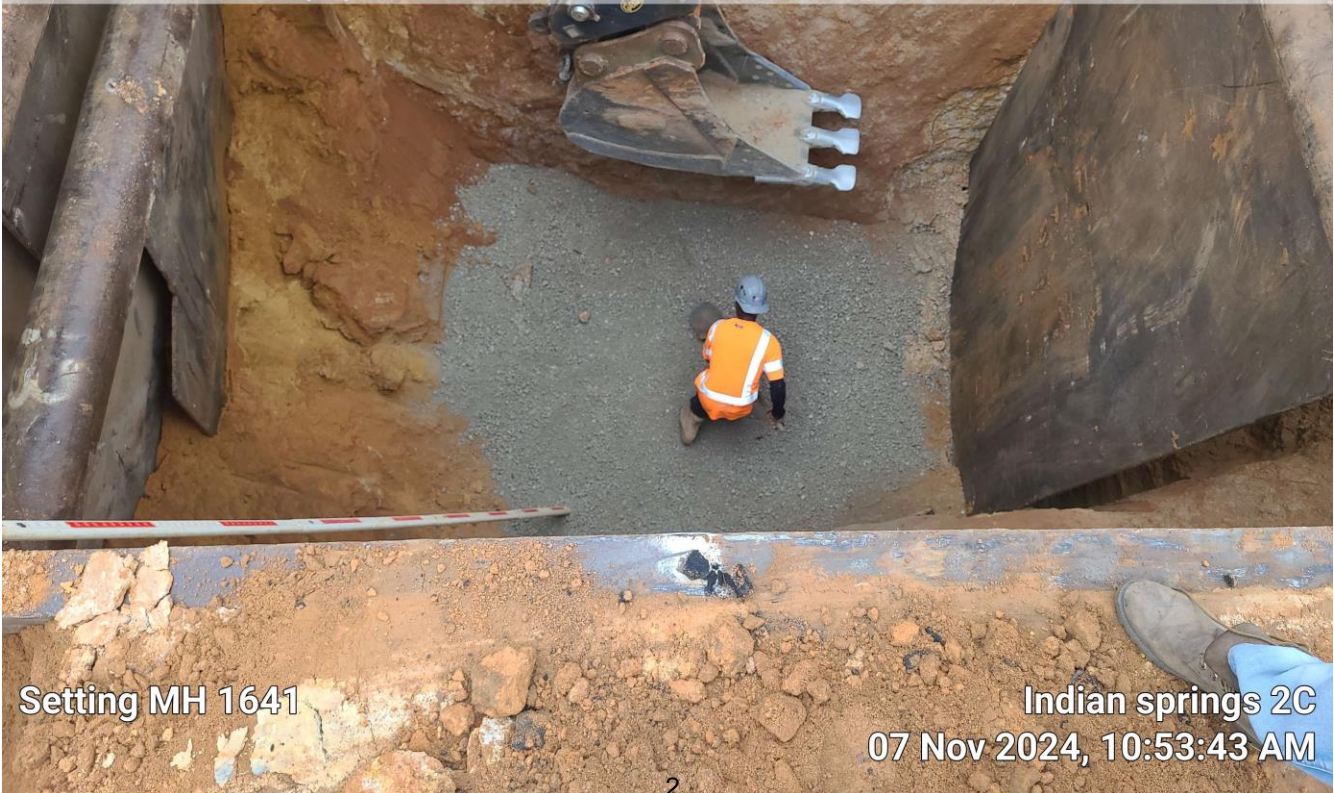

Setting MH 1641

Indian springs 2C
07 Nov 2024, 10:53:43 AM



312°NW (T) • 30.779357, -85.155381 ±6m ▲ 16m

Setting MH 1641

Indian springs 2C
07 Nov 2024, 11:24:54 AM
