

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 1/9/2025
For Project: **Blue Springs Road Sewer Extensions Phase 2**
NFWMD Const. Grant Agreement No. 17-061 AHE # 23-013
Contractor: Gulf Coast Utility Contractors
Designer: Alday-Howell Engineering
Notice to Proceed: 8/12/2024 Award Date: 12/12/2023



Substantial Completion: 5/25/2025 Final Completion: 7/24/2025

The report is for the week of: Monday, 12/15/2024 thru Sunday, 12/22/2024

The contractor performed the following operations this week. Sub work is noted in parenthesis:

- Monday-** Installed 56' LF of 8" gravity sewer pipe.
- Tuesday-** Installed manhole 268 and 28 LF of 8" gravity pipe
- Wednesday-** Air pressure tested From manhole 268 - 261. Prepared road for paving.
- Thursday-** Performed CCTV on 8" gravity pipe. Prepared road for paving.
- Friday-** Paved Blue Springs road. Guittler striped new pavement markings. Removed temporary stop lights.
- Saturday-** No work at contractor's option.
- Sunday-** No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	38%	Time Remaining (%):	62%
Invoiced to Date:	\$1,015,456.50	Weather days to date:	6
Original Contract Amount:	\$2,975,353.25	Holiday days granted:	10
Change Order Amount Approved:	\$0.00	Actual Days:	112
Contract Time Approved:		Days used with deduct:	102
Remaining:	\$1,959,896.75	Remaining to SC:	168
Days to Substantial Completion:	270	Remaining to FC:	228
Days to Final Completion:	330		

Robin G. Besczeczynski, Utility Project Manager (850-526-2040)






AHE/bhl

Blue Springs Sewer Project (Phase 2)
03 Dec 2024, 7:31:21 AM

5083 Blue Springs Rd, Marianna, F

293°W (T) • 30.784859, -85.17190

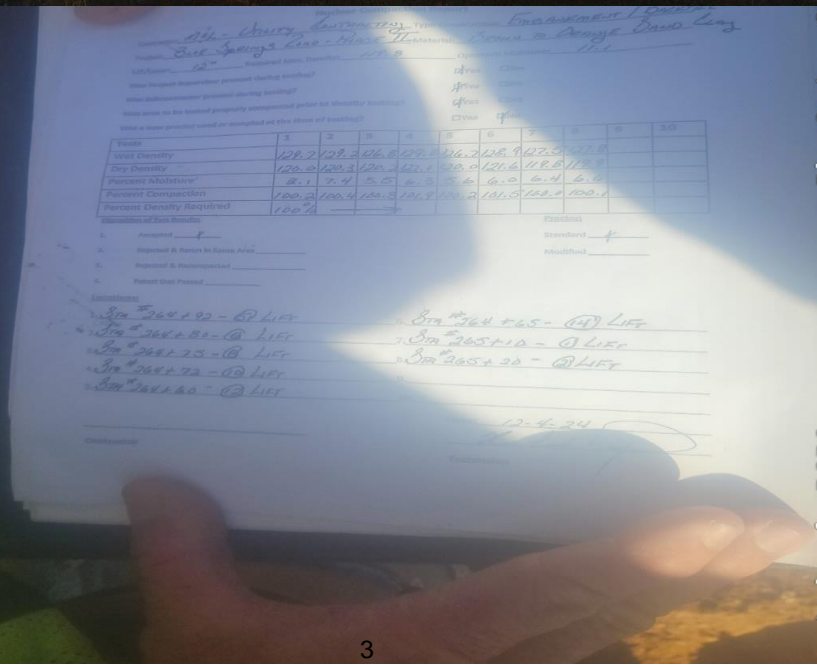

Blue Springs S 04

density log for BSR2
HE/bhl

