

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
 Prepared by: Alday-Howell Engineering, Inc.
 Prepared on: 1/5/2025
 For Project: **Indian Springs Sewer Phase 2C**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
 Contractor: Blankenship Contracting, Inc.
 Designer: Alday-Howell, Engineering Inspector: Dwayne Josey (850) 258-3386
 Notice to Proceed: 11/4/2024 Award Date: 12/13/2022



Substantial Completion: 9/16/2025 Final Completion: 11/15/2025

The report is for the week of: Monday, 12/30/2024 thru Sunday, 1/5/2025

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- No work due to holiday. Holiday granted.

Tuesday- No work due to holiday. Holiday granted.

Wednesday- No work due to holiday. Holiday granted.

Thursday- Cleaned construction area.

Friday- Retested man holes 1641 to 1645.


Saturday- No work performed. Contractor's option.

Sunday- No work performed. Contractor's option.


Engineer's remarks/Pending issues:

Percent Project Complete:	5%	Time Remaining (%):	84%
Invoiced to Date:	\$330,983.74	Weather days to date:	1
Original Contract Amount:	\$6,168,668.47	Holiday days granted:	15
Change Order Amount Approved:		Actual Days:	66
Remaining:	\$5,837,684.73	Days used with deduct:	47
Days to Substantial Completion:	300	Remaining to SC:	253
Days to Final Completion:	360	Remaining to FC:	313

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)



☉ 342°NW (T) • 30.779372, -85.155379 ±4m ▲ 16m

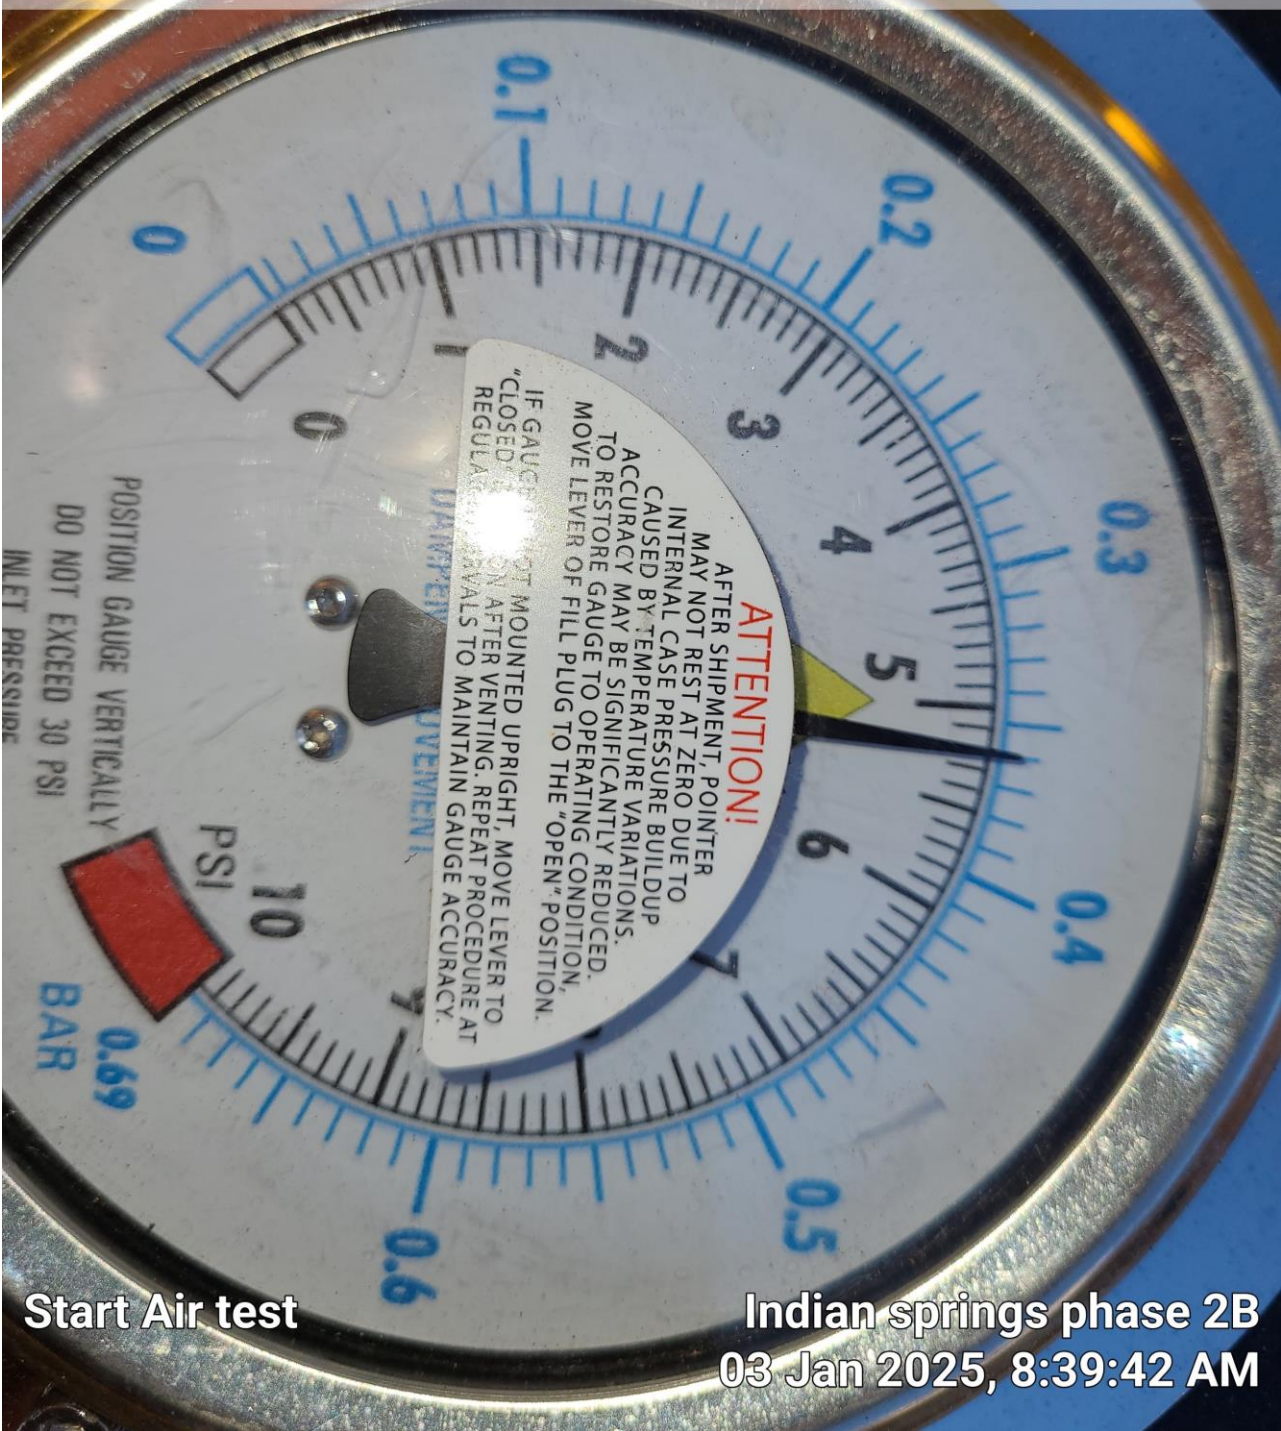

Start Air test

Indian springs phase 2B
03 Jan 2025, 8:39:42 AM



☉ 340°NW (T) ● 30.779373, -85.155388 ±9m ▲ 16m

