

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
 Prepared by: Alday-Howell Engineering, Inc.
 Prepared on: 1/12/2025
 For Project: **Indian Springs Sewer Phase 2C**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
 Contractor: Blankenship Contracting, Inc.
 Designer: Alday-Howell, Engineering Inspector: Dwayne Josey (850) 258-3386
 Notice to Proceed: 11/4/2024 Award Date: 12/13/2022



Substantial Completion: 9/17/2025 Final Completion: 11/16/2025

The report is for the week of: Monday, 1/6/2025 thru Sunday, 1/12/2025

The contractor performed the following operations this week. Sub work is noted in parenthesis:

- Monday-** No work due to rain. Rain day granted.
- Tuesday-** Performed air test at man hole 1637 to 1641 and installed 70 lf of 8" gravity.
- Wednesday-** Installed 63 lf of 8" gravity on Oak Dr.
- Thursday-** Installed 56 lf of 8" gravity on Oak Dr.
- Friday-** Cleaned construction area.
- Saturday-** No work performed. Contractor's option.
- Sunday-** No work performed. Contractor's option.


Engineer's remarks/Pending issues:

Percent Project Complete:	5%	Time Remaining (%):	82%
Invoiced to Date:	\$330,983.74	Weather days to date:	2
Original Contract Amount:	\$6,168,668.47	Holiday days granted:	15
Change Order Amount Approved:		Actual Days:	66
Remaining:	\$5,837,684.73	Days used with deduct:	53
Days to Substantial Completion:	300	Remaining to SC:	247
Days to Final Completion:	360	Remaining to FC:	307

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)

S 180 SW 240 W 270
www.cherne.com
2300 VIERL
SHAKOPEE
www.cherne.com

☉ 237°SW (T) • 30.779343, -85.15537 ±3m ▲ 19m

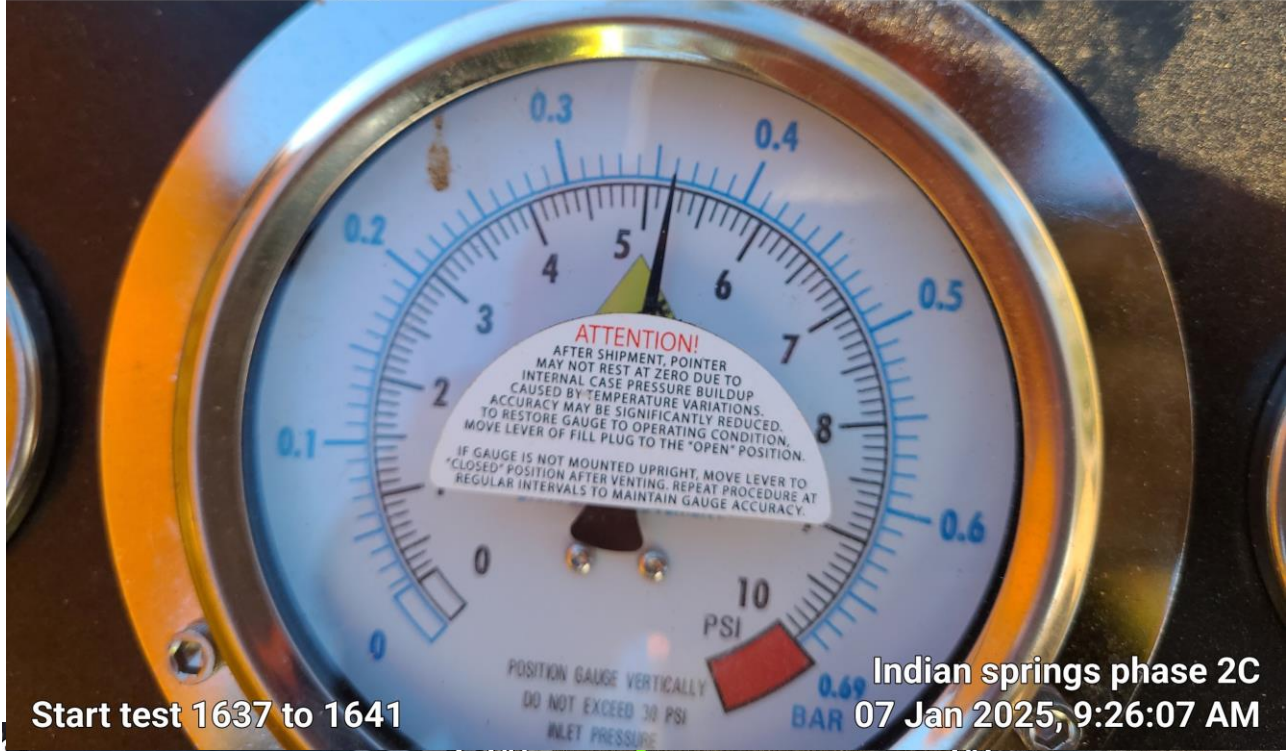


Start test 1637 to 1641

Indian springs phase 2C
07 Jan 2025, 9:26:07 AM

S 180 SW 240 VV 270
www.cherne.com
2300 VIERL
SHAKOPEE
www.cherne.com

☉ 239°SW (T) • 30.779353, -85.155394 ±3m ▲ 12m

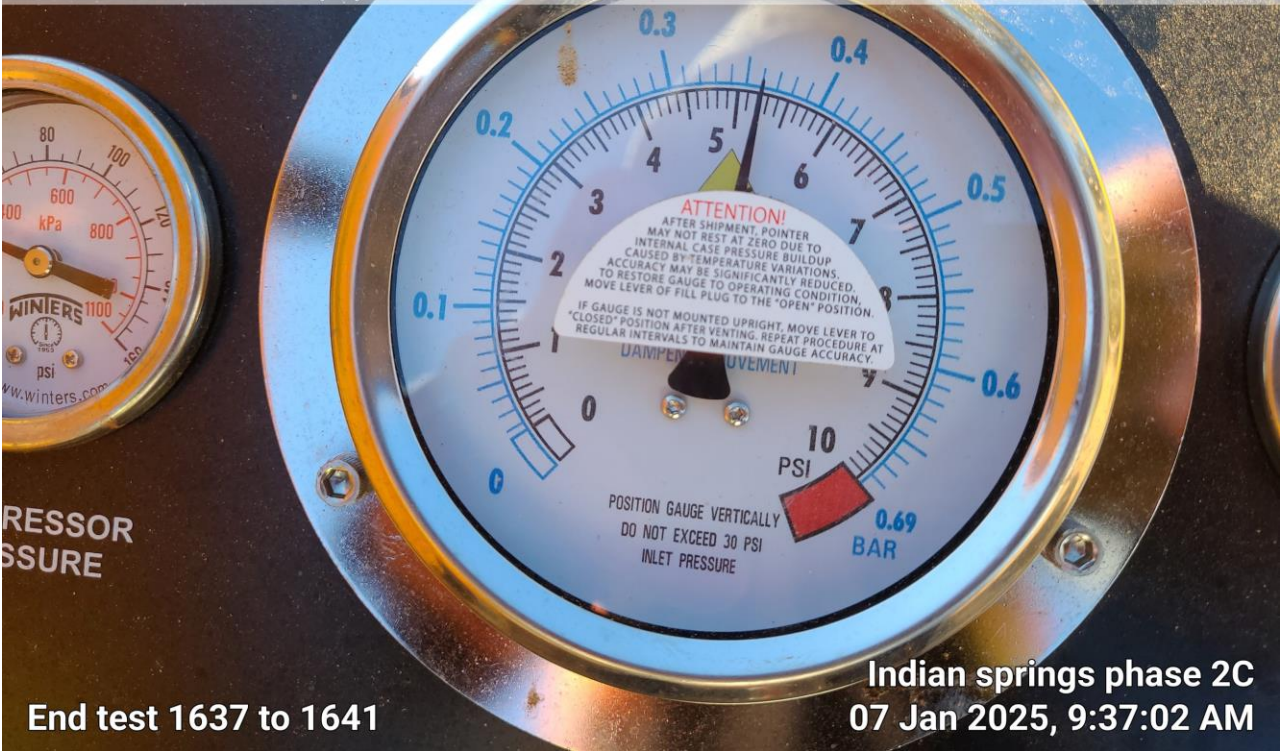

End test 1637 to 1641

Indian springs phase 2C
07 Jan 2025, 9:37:02 AM

