

# CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL  
 Prepared by: Alday-Howell Engineering, Inc.  
 Prepared on: 1/23/2025  
 For Project: **Indian Springs Phase 2 Water**  
**FDEP Grant/Loan Agreement DW320381** AHE # 20-034  
 Contractor: L & K Contracting, Inc.  
 Designer: Alday-Howell Engineering Inspector: Tyler Lawrence (850) 718-7233  
 Notice to Proceed: 10/15/2023 Award Date: 9/12/2023



Substantial Completion: 6/24/2025 Final Completion: 8/23/2025

The report is for the week of: Monday, 1/13/2025 thru Sunday, 1/19/2025

The contractor performed the following operations this week. Sub work is noted in parenthesis:

- Monday-** No work contractors option.
- Tuesday-** Set booster pump manifold.
- Wednesday-** Plumbed booster pump.
- Thursday-** Performed earthwork on Apalachee Trl.
- Friday-** Performed earthwork at the booster pump.
- Saturday-** No work contractors option.
- Sunday-** No work contractors option.


Engineer's remarks/Pending issues:

Percent Project Complete:	40%	Time Remaining (%):	28%
Invoiced to Date:	\$2,433,879.21	Weather days to date:	17
Original Contract Amount:	\$4,492,568.00	Holiday days granted:	41
Change Order Amount Approved:	-\$550,499.25	Actual Days:	463
Remaining:	\$1,508,189.54	Days used with deduct:	405
Days to Substantial Completion:	560	Remaining to SC:	155
Days to Final Completion:	620	Remaining to FC:	215

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)



☀ 332°NW (T) ☉ 30°44'49"N, 85°10'23"W ±574ft ▲ 125ft

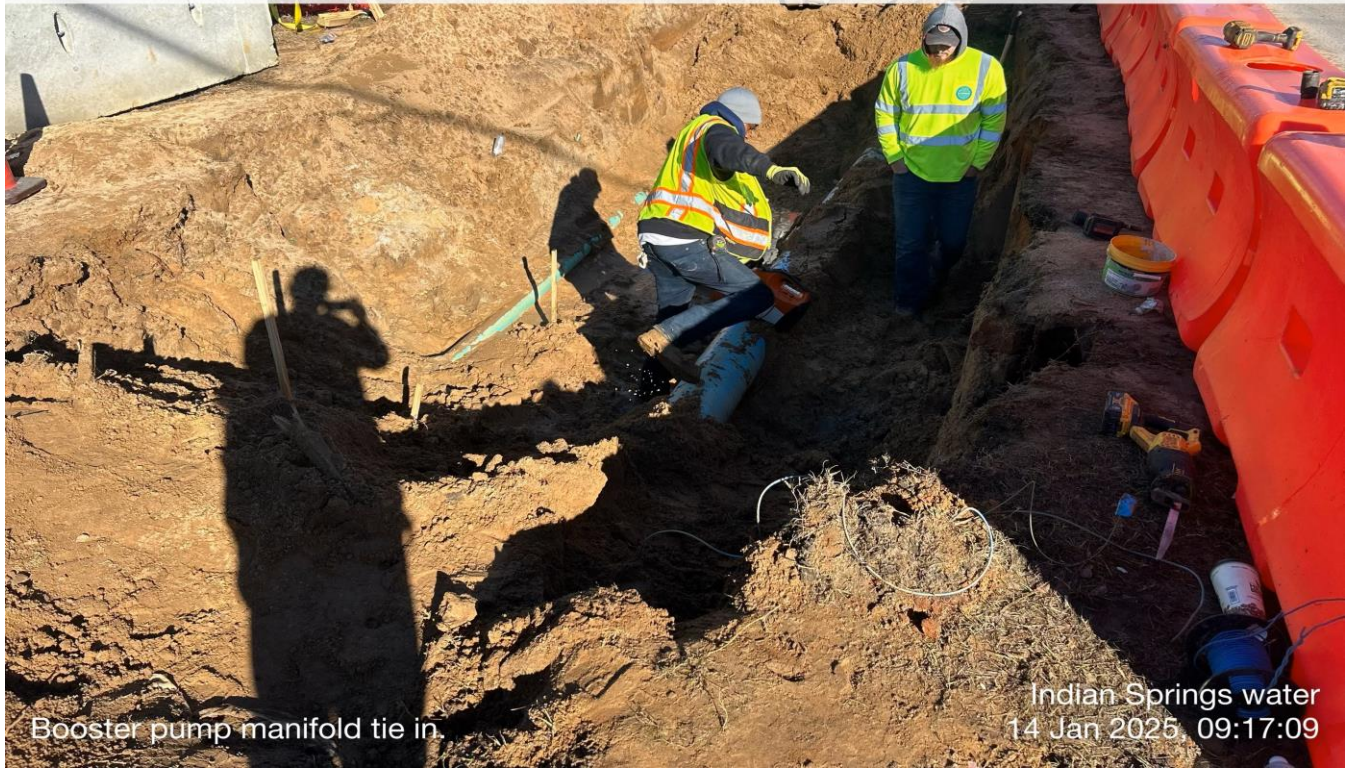

Booster pump manifold tie in.

Indian Springs water  
14 Jan 2025, 09:17:09



☀ 71°E (T) ☉ 30°44'47"N, 85°10'19"W ±19ft ▲ 136ft



Booster pump manifold tie in.

Indian Springs water  
14 Jan 2025, 12:11:18



☀ 45°NE (T) ☉ 30°44'47"N, 85°10'20"W ±39ft ▲ 124ft



Booster pump manifold tie in.

Indian Springs water  
14 Jan 2025, 13:32:22
