

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 2/2/2025
For Project: **Indian Springs Sewer Phase 2C**
NFWMD Const. Grant Agreement No. 20-036 AHE # 20-033
Contractor: Blankenship Contracting, Inc.
Designer: Alday-Howell, Engineering
Notice to Proceed: 11/4/2024



Inspector: Dwayne Josey (850) 258-3386

Award Date: 12/13/2022

Substantial Completion: 9/20/2025

Final Completion: 11/19/2025

The report is for the week of: Monday, 1/27/2025

thru Sunday, 2/2/2025

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- No work due to rain. Rain day granted.

Tuesday- Installed 2 laterals to right of way.

Wednesday- Installed manhole 1633 on Oak Dr.

Thursday- Installed 70 lf of 8" gravity on Oak Dr.

Friday- Installed one lateral to right of way on Oak Dr.


Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	7%	Time Remaining (%):	76%
Invoiced to Date:	\$411,213.40	Weather days to date:	5
Original Contract Amount:	\$6,168,668.47	Holiday days granted:	15
Change Order Amount Approved:		Actual Days:	91
Remaining:	\$5,757,455.07	Days used with deduct:	71
Days to Substantial Completion:	300	Remaining to SC:	229
Days to Final Completion:	360	Remaining to FC:	289

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)

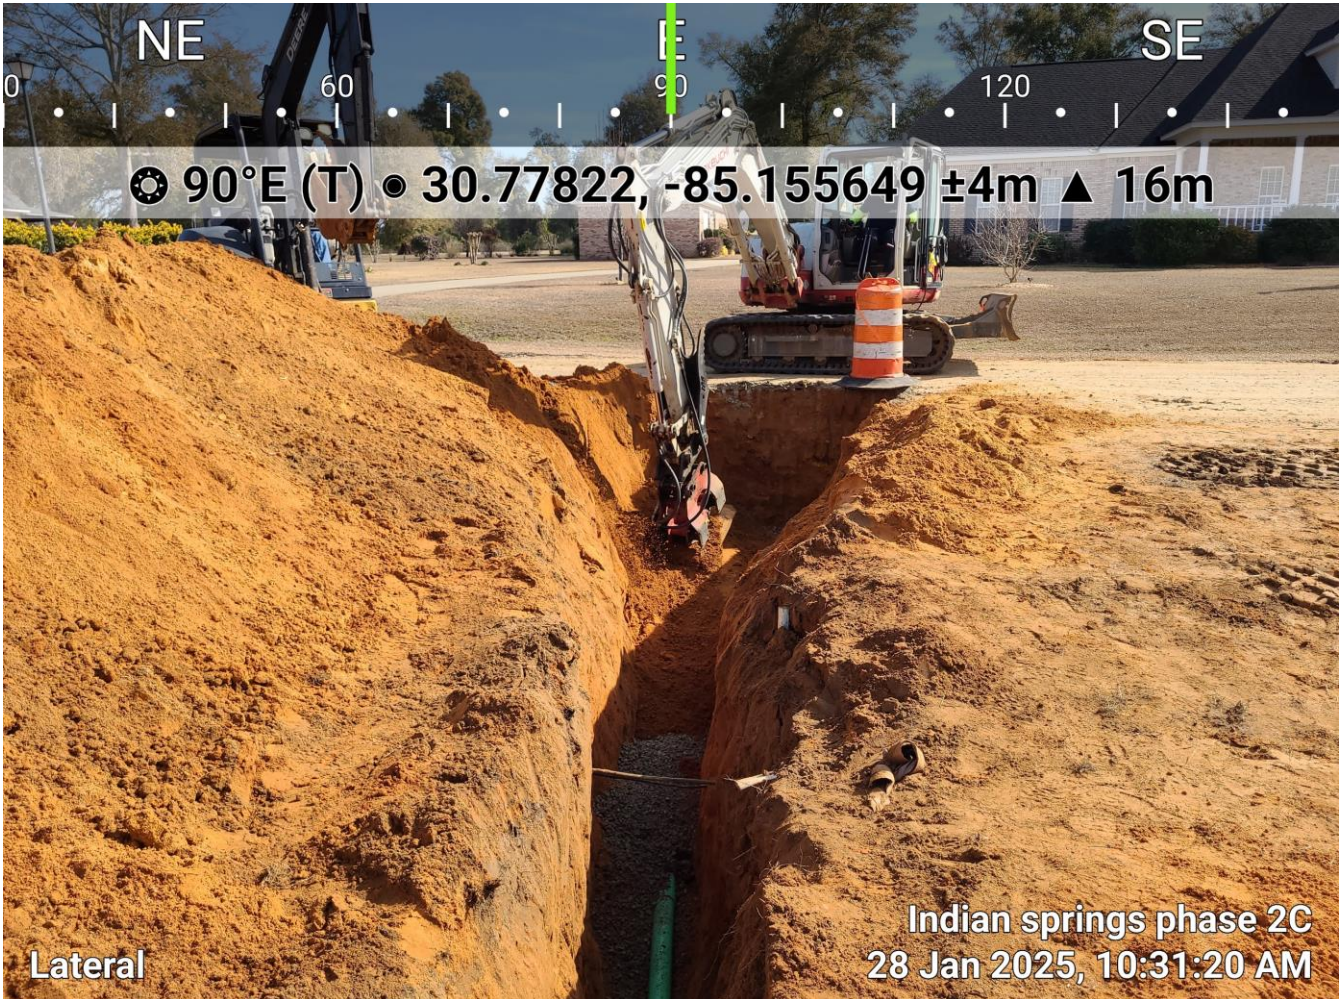



☉ 134°SE (T) ☉ 30.777225, -85.155785 ±4m ▲ 11m



MH 1633

Indian springs phase 2C
29 Jan 2025, 9:36:46 AM



☉ 150°SE (T) ☉ 30.777166, -85.155775 ±3m ▲ 15m



8in gravity

Indian springs phase 2C
30 Jan 2025, 11:21:22 AM

