

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
 Prepared by: Alday-Howell Engineering, Inc.
 Prepared on: 2/23/2025
 For Project: **Indian Springs Sewer Phase 2C**
NFWMD Const. Grant Agreement No. 20-036 AHE # 20-033
 Contractor: Blankenship Contracting, Inc.
 Designer: Alday-Howell, Engineering Inspector: Dwayne Josey (850) 258-3386
 Notice to Proceed: 11/4/2024 Award Date: 12/13/2022



Substantial Completion: 9/22/2025 Final Completion: 11/21/2025

The report is for the week of: Monday, 2/17/2025 thru Sunday, 2/23/2025

The contractor performed the following operations this week. Sub work is noted in parenthesis:

- Monday-** Installed 83 lf of 8" gravity main, And set man hole 2004, And installed 2 laterals to right of way on Robins Way.
- Tuesday-** Installed 3 laterals to right of way.
- Wednesday-** No work due to rain. Rain day granted.
- Thursday-** Installed 2 laterals to right of way.
- Friday-** Performed air test on Oak Dr. and Robins Way.
- Saturday-** No work at contractor's option.
- Sunday-** No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	7%	Time Remaining (%):	70%
Invoiced to Date:	\$411,213.40	Weather days to date:	7
Original Contract Amount:	\$6,168,668.47	Holiday days granted:	15
Change Order Amount Approved:		Actual Days:	112
Remaining:	\$5,757,455.07	Days used with deduct:	90
Days to Substantial Completion:	300	Remaining to SC:	210
Days to Final Completion:	360	Remaining to FC:	270

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)



☉ 148°SE (T) • 30.77596, -85.155179 ±3m ▲ 17m



8in Gravity

Indian Springs Phase 2C
17 Feb 2025, 8:22:16 AM




☉ 125°SE (T) • 30.776051, -85.155292 ±9m ▲ 17m



8in Gravity

Indian Springs Phase 2C
17 Feb 2025, 8:38:52 AM



☉ 289°W (T) • 30.777226, -85.155756 ±3m ▲ 16m




Start Air test 1633 to 1637

Indian Springs Phase 2C
21 Feb 2025, 9:06:46 AM



☉ 296°W (T) • 30.777207, -85.155741 ±3m ▲ 17m

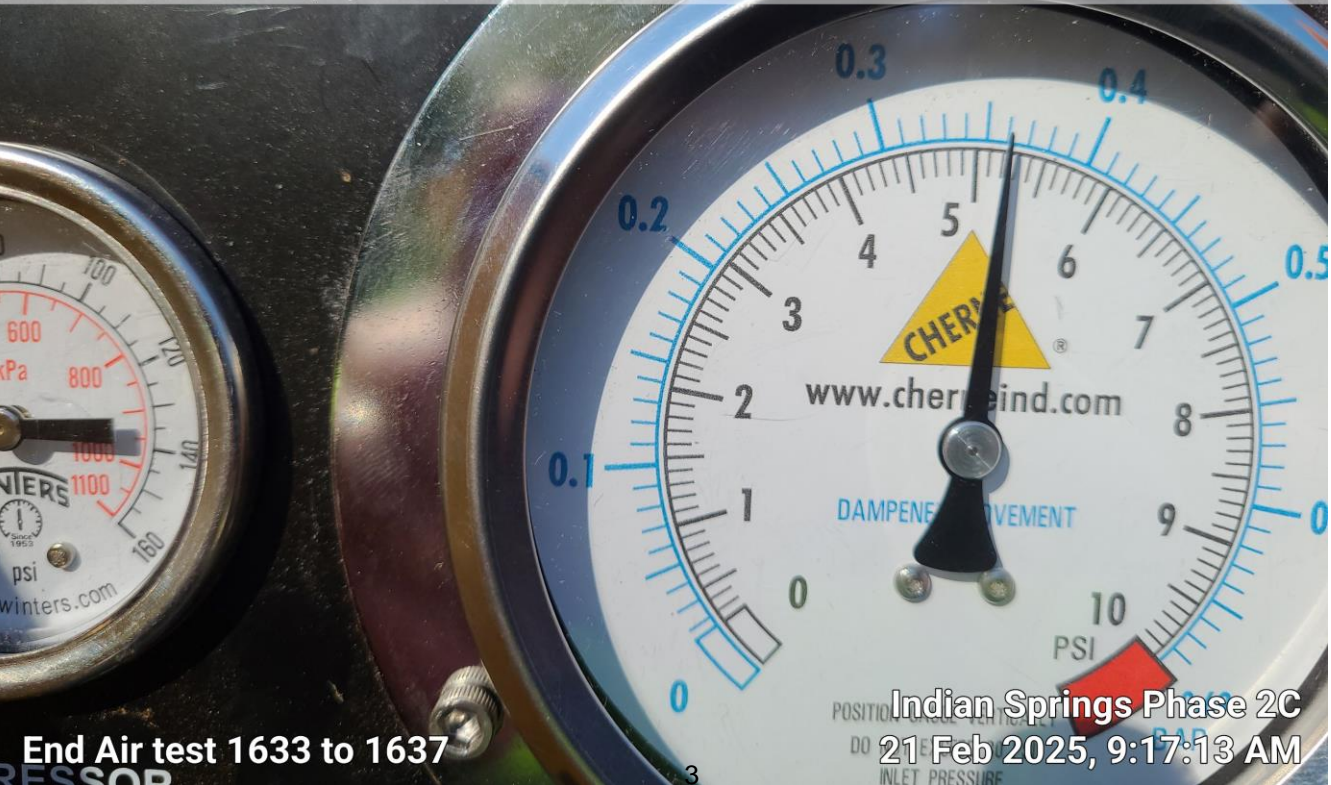

End Air test 1633 to 1637

Indian Springs Phase 2C
21 Feb 2025, 9:17:13 AM
