

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 4/9/2024



For Project: **Blue Springs Road Sewer Extensions Phase 1**
NFWMD Const. Grant Agreement No. 17-061 AHE # 17-062
Contractor: L & K Contracting, Inc.
Designer: Alday-Howell Engineering Inspector: Brett Lawrence (850) 557-7429
Notice to Proceed: 9/27/2022 Award Date: 6/29/2022

Substantial Completion: 4/4/2024

Final Completion: 5/4/2024

The report is for the week of: Monday, 3/31/2025 thru Sunday, 4/6/2025

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- No work at contractor's option.

Tuesday- Performed directional bore for lift station power.

Wednesday- Cleaned construction area.

Thursday- No work at contractor's option.

Friday- Placed seed and mulch.

Saturday- No work at contractor's option.


Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	65%	Time Remaining (%):	-83%
Invoiced to Date:	\$3,202,257.18	Weather days to date:	52
Original Contract Amount:	\$5,347,467.37		
Change Order Amount Approved:	\$83,361.30	Holiday days granted:	62
Contract Time Approved:	141	Actual Days:	923
Remaining:	\$2,228,571.49	Days used with deduct:	809
Days to Substantial Completion:	441	Original SC:	300
		Remaining to SC:	-368
Days to Final Completion:	471	Original FC:	330
		Remaining to FC:	-338

A handwritten signature in blue ink, appearing to read "Rob B", is positioned above the approval line.

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)

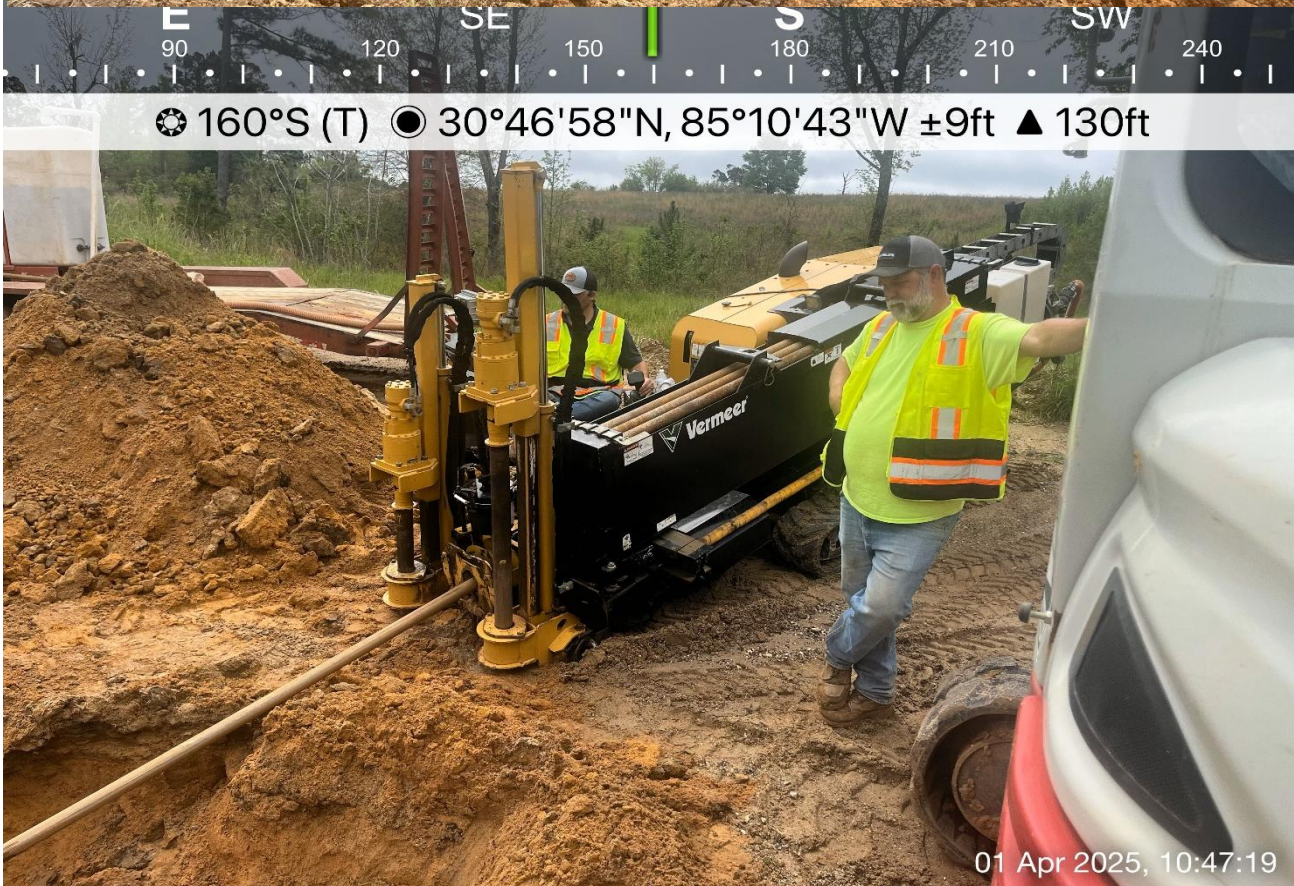



☀ 56°NE (T) ● 30°46'58"N, 85°10'43"W ±13ft ▲ 135ft



01 Apr 2025, 10:47:22



☀ 347°N (T) ● 30°46'52"N, 85°11'21"W ±9ft ▲ 178ft



04 Apr 2025, 09:19:25
