

# CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL  
Prepared by: Alday-Howell Engineering, Inc.  
Prepared on: 3/23/2025  
For Project: **Indian Springs Sewer Phase 2B**  
**NFWMD Const. Grant Agreement No. 20-036** AHE # 20-033  
Contractor: Blankenship Contracting, Inc.  
Designer: Alday-Howell Engineering  
Inspector: Dwayne Josey (850) 258-3386  
Notice to Proceed: 8/1/2023 Award Date: 12/13/2022



Substantial Completion: 7/25/2024 Final Completion: 9/23/2024

The report is for the week of: Monday, 3/17/2025 thru Sunday, 3/23/2025

The contractor performed the following operations this week. Sub work is noted in parenthesis:

**Monday-** Performed start up on wet well at lift station.

**Tuesday-** No work at contractor's option.

**Wednesday-** No work at contractor's option.

**Thursday-** No work at contractor's option.

**Friday-** No work at contractor's option.


**Saturday-** No work at contractor's option.

**Sunday-** No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	54%	Time Remaining (%):	-81%
Invoiced to Date:	\$3,113,992.08	Weather days to date:	19
Original Contract Amount:	\$6,377,639.99	Holiday days granted:	40
Change Order Amount Approved:		Actual Days:	601
Remaining:	\$3,263,647.91	Days used with deduct:	542
Days to Substantial Completion:	300	Remaining to SC:	-242
Days to Final Completion:	360	Remaining to FC:	-182

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)

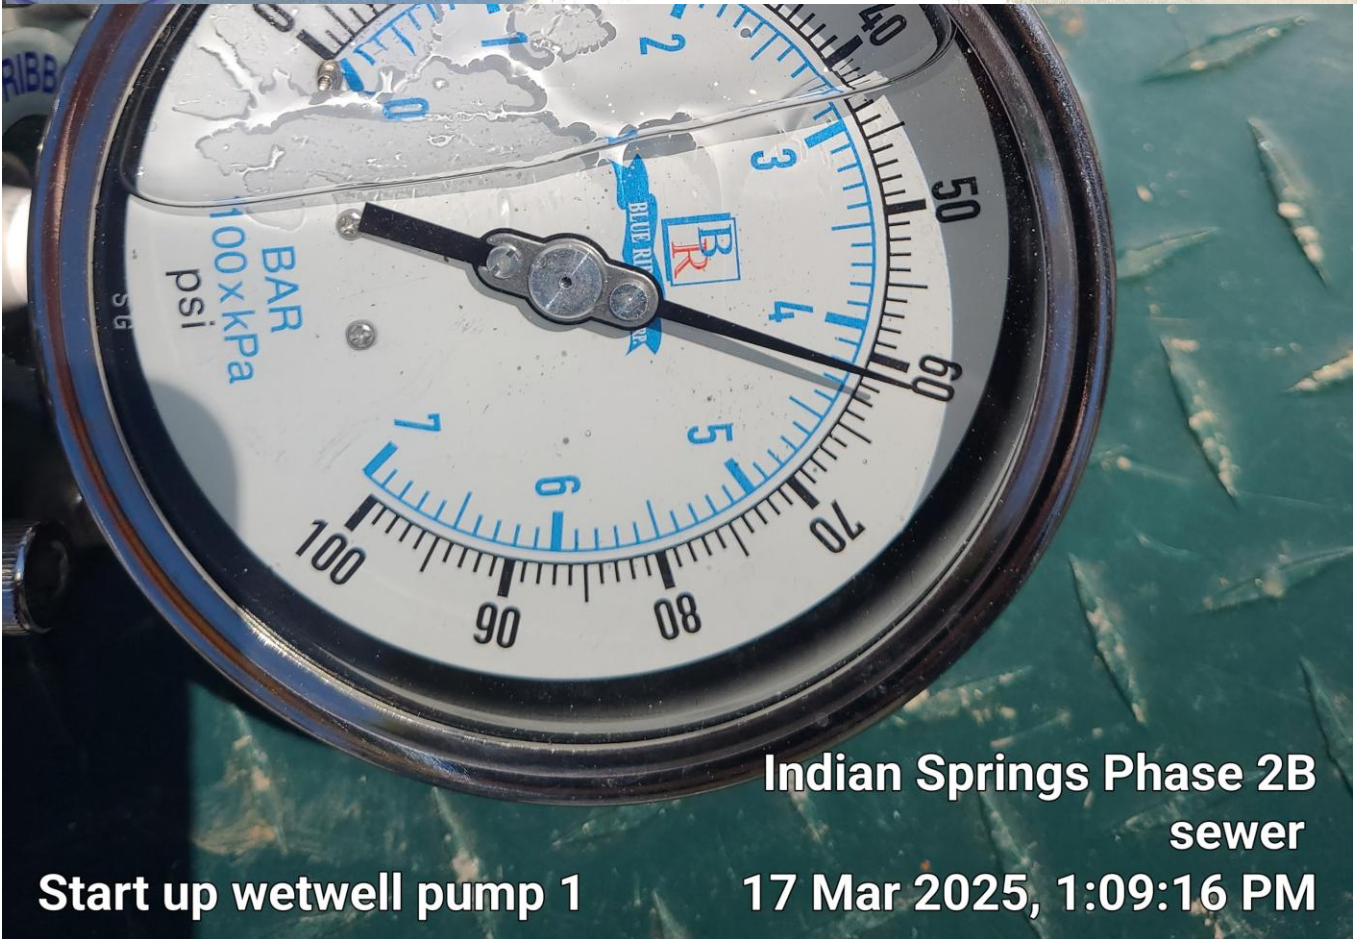



☉ 176°S (T) ● 30.778599, -85.159525 ±5m ▲ 24m



Start up wetwell

Indian Springs Phase 2B  
sewer  
17 Mar 2025, 1:16:53 PM
