

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
 Prepared by: Alday-Howell Engineering, Inc.
 Prepared on: 3/16/2025
 For Project: **Indian Springs Sewer Phase 2C**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
 Contractor: Blankenship Contracting, Inc.
 Designer: Alday-Howell, Engineering Inspector: Dwayne Josey (850) 258-3386
 Notice to Proceed: 11/4/2024 Award Date: 12/13/2022



Substantial Completion: 9/23/2025 Final Completion: 11/22/2025

The report is for the week of: Monday, 3/10/2025 thru Sunday, 3/16/2025


The contractor performed the following operations this week. Sub work is noted in parenthesis:

- Monday-** No work due to rain. Rain day granted.
- Tuesday-** Installed 64 lf of 8" gravity main on Oak Dr.
- Wednesday-** Installed 112 lf of 8" gravity main on Oak Dr.
- Thursday-** Installed 70 lf of 8" gravity main on Oak Dr.
- Friday-** Cleaned construction area on Oak Dr.
- Saturday-** No work at contractor's option.
- Sunday-** No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	7%	Time Remaining (%):	63%
Invoiced to Date:	\$411,213.40	Weather days to date:	8
Original Contract Amount:	\$6,168,668.47		
Change Order Amount Approved:		Holiday days granted:	15
		Actual Days:	133
Remaining:	\$5,757,455.07	Days used with deduct:	110
Days to Substantial Completion:	300	Remaining to SC:	190
Days to Final Completion:	360	Remaining to FC:	250

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)

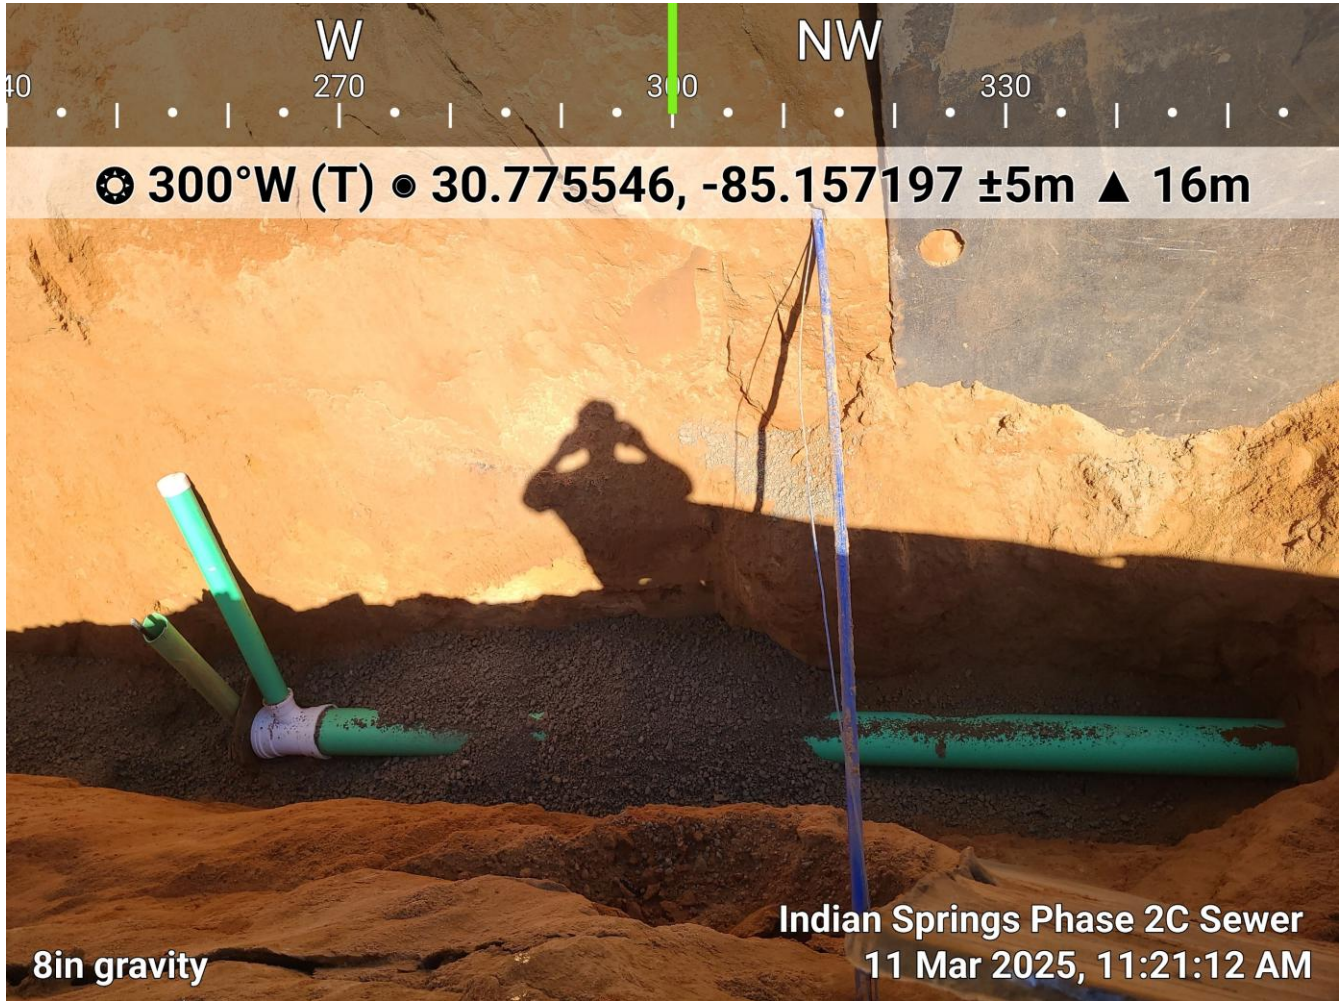



☉ 228°SW (T) ● 30.775387, -85.157877 ±5m ▲ 16m



8in gravity

Indian Springs Phase 2C sewer
13 Mar 2025, 12:57:28 PM
