

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 7/20/2025



For Project: **Indian Springs Sewer Phase 2C**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
Contractor: Blankenship Contracting, Inc.
Designer: Alday-Howell, Engineering Inspector: Dwayne Josey (850) 258-3386
Notice to Proceed: 11/4/2024 Award Date: 12/13/2022

Substantial Completion: 7/27/2026

Final Completion: 9/25/2026

The report is for the week of: Monday, 7/14/2025 thru Sunday, 7/20/2025

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Installed 380 lf of 4" force main on Club House Dr.

Tuesday- Installed 100 lf of 4" force main, 27 lf of trenchless and 73 lf of trench, on Clubhouse Dr.

Wednesday- Installed 200 lf of 4" force main on Clubhouse Dr. and Magnolia Dr.

Thursday- Installed 200 lf of 4" force main on Magnolia Dr.


Friday- Locate utilities on Magnolia Dr.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.


Engineer's remarks/Pending issues:

Percent Project Complete:	19%	Time Remaining (%):	62%		
Invoiced to Date:	\$1,085,658.93	Weather days to date:	13		
Original Contract Amount:	\$6,168,668.47				
Change Order Amount Approved:	\$2,820,626.04	Holiday days granted:	17		
Contract Time Approved:	300	Actual Days:	259		
Remaining:	\$7,903,635.58	Days used with deduct:	229		
Days to Substantial Completion:	600	Original SC:	300	Remaining to SC:	371
Days to Final Completion:	660	Original FC:	360	Remaining to FC:	431

Approved:  Robin G. Besczeynski, Utility Project Manager (850-526-2040)

North East

☉ 74°NE (T) ☉ 30.768724, -85.16433 ±6m ▲ 33m

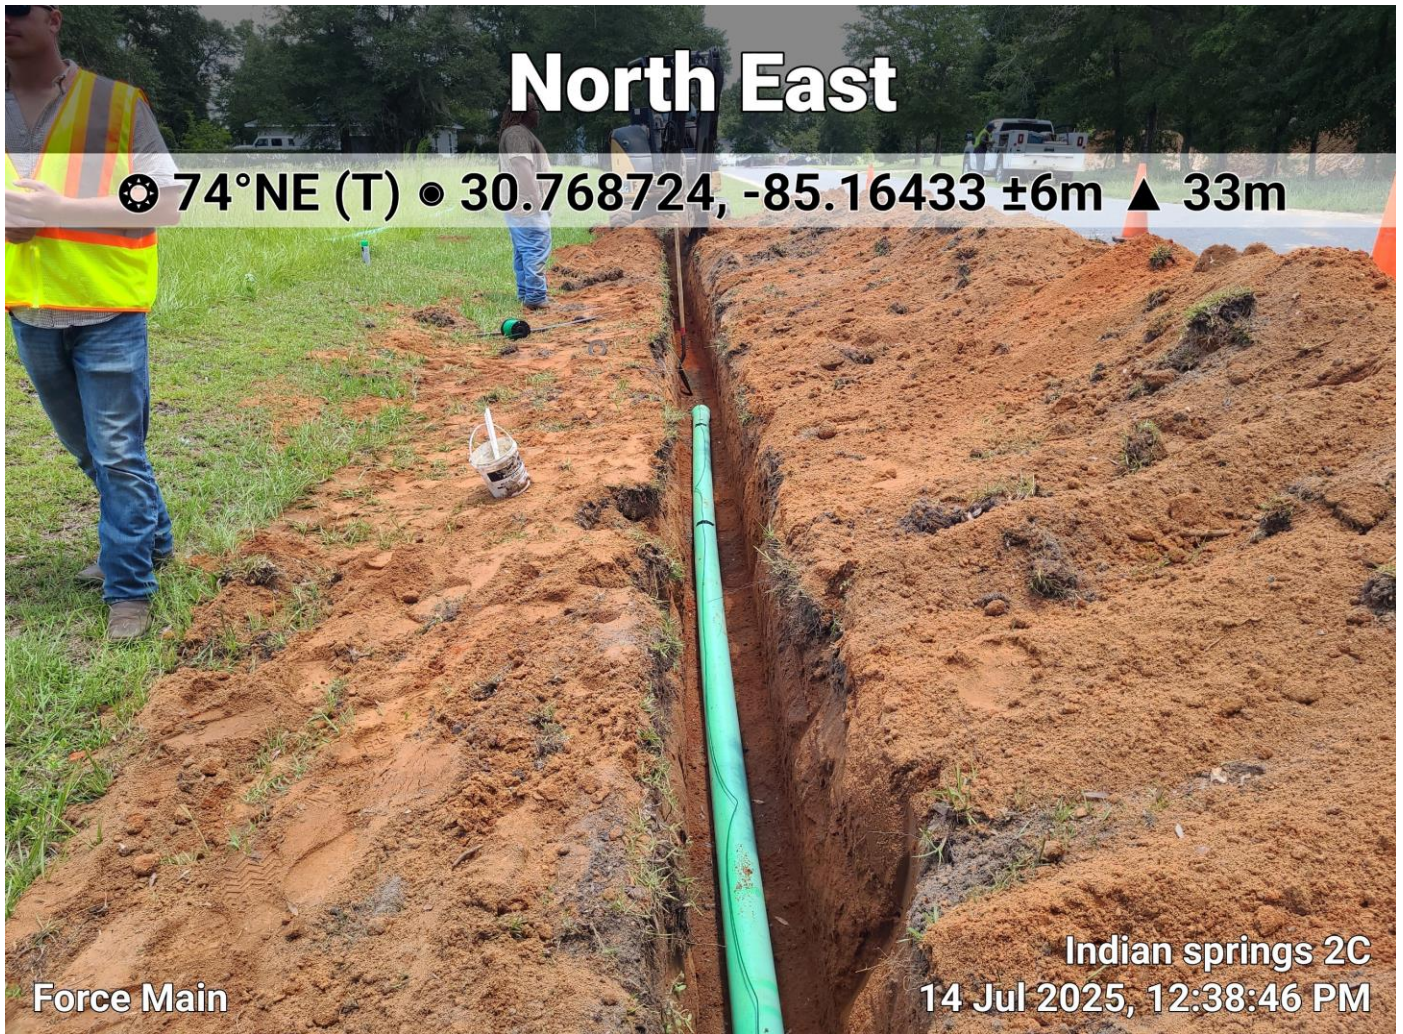

Force Main

Indian springs 2C
14 Jul 2025, 12:38:46 PM

☉ 74°NE (T) ☉ 30.768724, -85.16433 ±6m ▲ 33m



Force Main

Indian springs 2C
16 Jul 2025, 8:02:03 AM

South West

☉ 257°SW (T) ☉ 30.769497, -85.163037 ±3m ▲ 24m



Force Main

Indian springs 2C
17 Jul 2025, 12:48:26 PM

