

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 7/27/2025



For Project: **Indian Springs Sewer Phase 2C**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
Contractor: Blankenship Contracting, Inc.
Designer: Alday-Howell, Engineering Inspector: Dwayne Josey (850) 258-3386
Notice to Proceed: 11/4/2024 Award Date: 12/13/2022

Substantial Completion: 7/27/2026

Final Completion: 9/25/2026

The report is for the week of: Monday, 7/21/2025 thru Sunday, 7/27/2025

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Installed 165 lf of 4" force main on Magnolia Blossom Ln., 46 lf of trenchless and 119 lf of trench.

Tuesday- Installed 150 lf of 4" force main on Magnolia Blossom Ln., 28 lf of trenchless and 122 lf of trench.

Wednesday- Locate utilities on Magnolia Blossom Ln.

Thursday- Performed CCTV test.


Friday- Performed CCTV test.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	19%	Time Remaining (%):	61%		
Invoiced to Date:	\$1,085,658.93	Weather days to date:	13		
Original Contract Amount:	\$6,168,668.47				
Change Order Amount Approved:	\$2,820,626.04	Holiday days granted:	17		
Contract Time Approved:	300	Actual Days:	266		
Remaining:	\$7,903,635.58	Days used with deduct:	236		
Days to Substantial Completion:	600	Original SC:	300	Remaining to SC:	364
Days to Final Completion:	660	Original FC:	360	Remaining to FC:	424

Approved:  Robin G. Besczeynski, Utility Project Manager (850-526-2040)




South

☉ 191°S (T) ● 30.775059, -85.159421 ±6m ▲ 18m



Indian springs 2C
24 Jul 2025, 9:17:52 AM

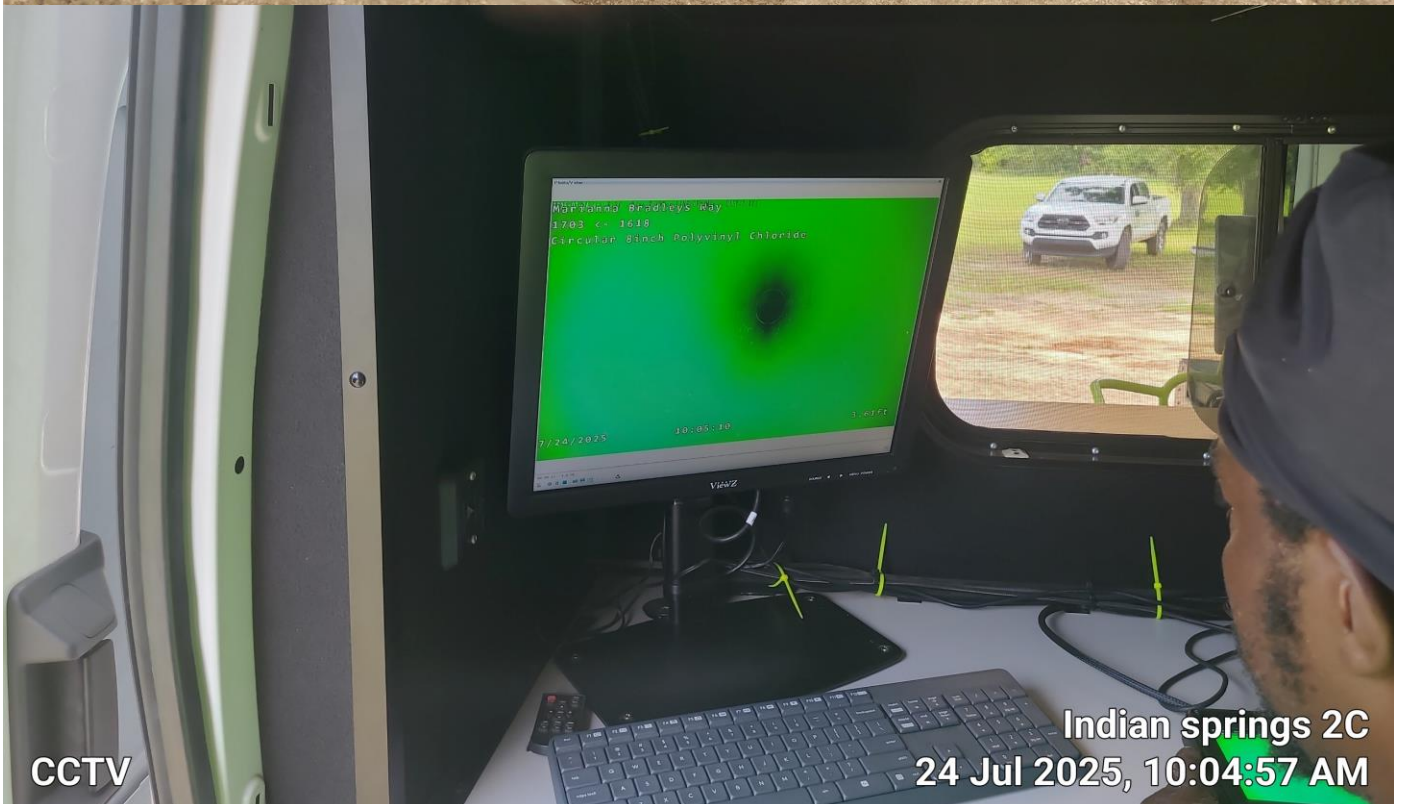

Indian springs 2C
24 Jul 2025, 10:04:57 AM

