

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL

Prepared by: Alday-Howell Engineering, Inc.

Prepared on: 8/31/2025

For Project: Indian Springs Sewer Phase 2B

NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033

Contractor: Blankenship Contracting, Inc.

Designer: Alday-Howell Engineering

Inspector: Dwayne Josey (850) 258-3386

Notice to Proceed: 8/1/2023

Award Date: 1/24/2023



Substantial Completion: 8/20/2025

Final Completion: 10/19/2025

The report is for the week of: Monday, 8/25/2025

thru Sunday, 8/31/2025

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Prepared to perform hydrastatic test at Wayside lift station.

Tuesday- Performed hydrastitic test on force main at Wayside lift station.

Wednesday- Prepared to raise man hole 90-19 at Wayside lift station.

Thursday- Prepared to raise manhole 90-19 at Wayside lift station.

Friday- No work due to Holiday. Holiday day granted

Saturday- No work due to Holiday. Holiday day granted

Sunday- No work due to Holiday. Holiday day granted

Engineer's remarks/Pending issues:

Percent Project Complete: 74%

Time Remaining (%): -2%

Invoiced to Date: \$4,283,389.98

Weather days to date: 21

Original Contract Amount: \$6,377,639.99

Change Order Amount Approved:

Holiday days granted: 45

Contract Time Approved: 384

Actual Days: 762

Remaining: \$2,094,250.01

Days used with deduct: 696

Days to Substantial Completion: 684 Original SC: 300

Remaining to SC: -12

Days to Final Completion: 744 Original FC: 360

Remaining to FC: 48

A handwritten signature in blue ink, appearing to read 'Rob B', is positioned above the approved line.

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)

West


☉ 289°W (T) • 30.755903, -85.195957 ±6m ▲ 0m



Bell restraint

Indian Springs Phase 2B
26 Aug 2025, 8:35:48 AM

☉ 326°NW (T) • 30.755773, -85.195892 ±3m ▲ 0m

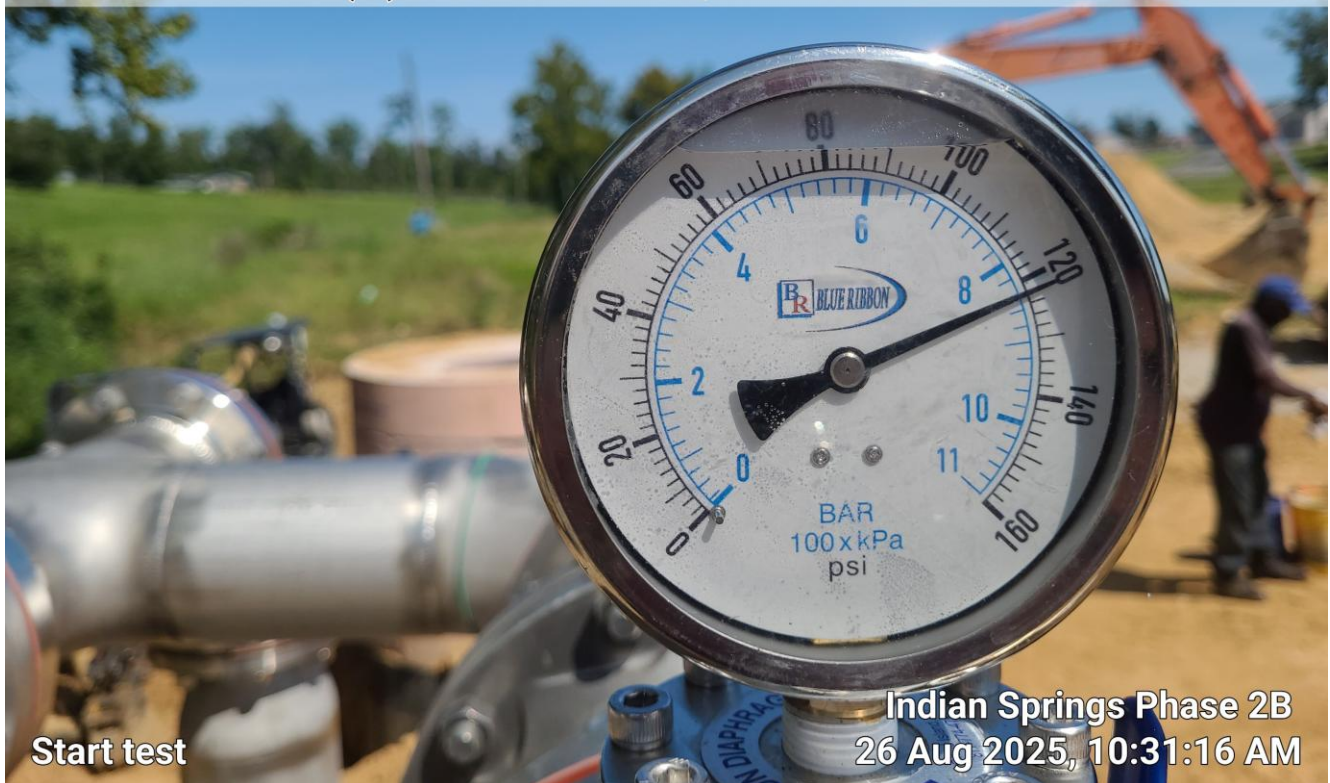


Start test

Indian Springs Phase 2B
26 Aug 2025, 10:31:16 AM

North West

☉ 346°NW (T) • 30.755785, -85.195911 ±3m ▲ 0m

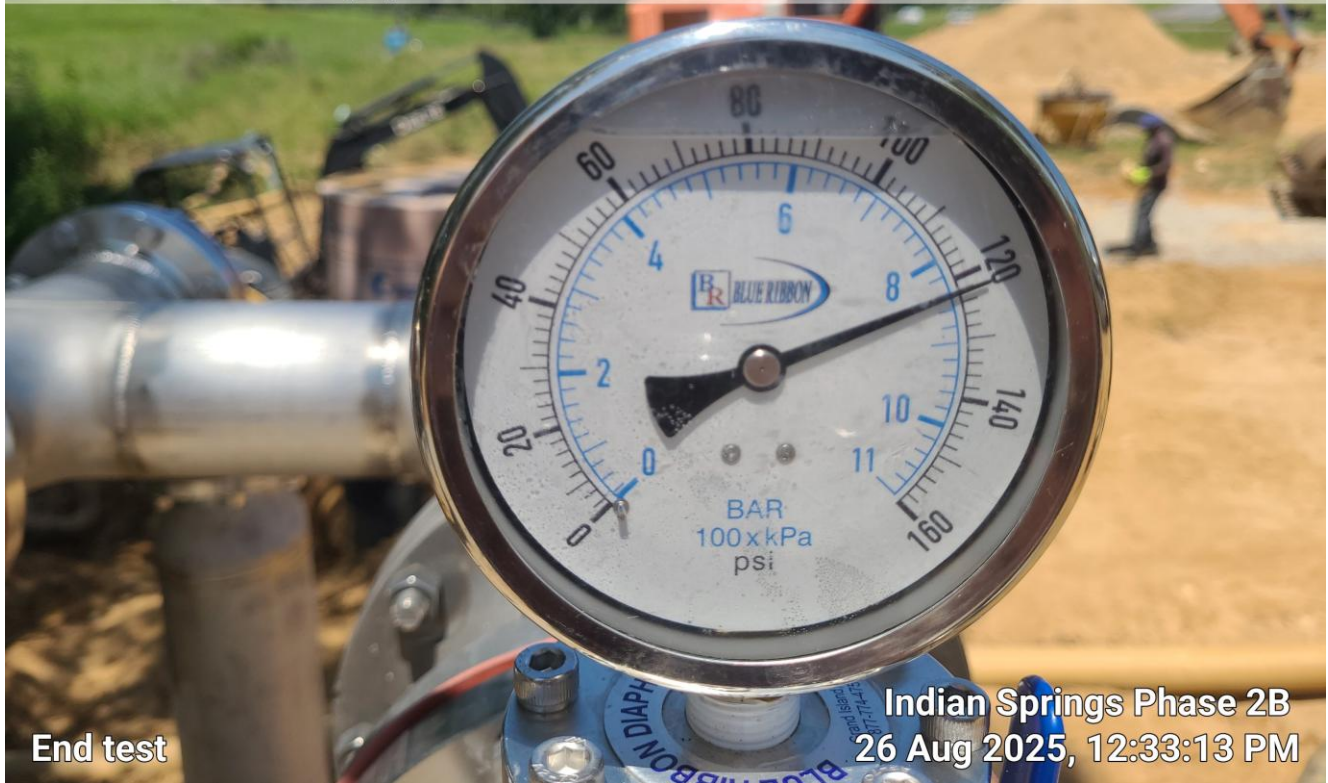

End test

Indian Springs Phase 2B
26 Aug 2025, 12:33:13 PM

☉ 167°SE (T) • 30.755892, -85.195705 ±3m ▲ 0m



Raise MH 90-19

Indian Springs Phase 2B
27 Aug 2025, 8:46:59 AM

South

☉ 172°S (T) • 30.755784, -85.19601 ±3m ▲ 1m



Raise MH 90-19 Wayside

Indian Springs Phase 2B
28 Aug 2025, 9:19:19 AM
