

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 11/11/2025



For Project: **Indian Springs Sewer Phase 2C**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
Contractor: Blankenship Contracting, Inc.
Designer: Alday-Howell, Engineering Inspector: Dwayne Josey (850) 258-3386
Notice to Proceed: 11/4/2024 Award Date: 7/9/2024

Substantial Completion: 8/5/2026

Final Completion: 10/4/2026

The report is for the week of: Monday, 11/3/2025

thru Sunday, 11/9/2025

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- No work at contractor's option.

Tuesday- No work at contractor's option.

Wednesday- No work at contractor's option.

Thursday- Poured concrete around bottom of wetwell. Set man hole 1641.

Friday- Set man hole 1641 at lift station on Oak Dr.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	27%	Time Remaining (%):	45%
Invoiced to Date:	\$1,546,146.65	Weather days to date:	18
Original Contract Amount:	\$6,168,668.47		
Change Order Amount Approved:	\$2,820,626.04	Holiday days granted:	21
Contract Time Approved:	300	Actual Days:	371
Remaining:	\$7,443,147.86	Days used with deduct:	332
Days to Substantial Completion:	600	Original SC:	300
		Remaining to SC:	268
Days to Final Completion:	660	Original FC:	360
		Remaining to FC:	328

Approved:  Robin G. Besczeynski, Utility Project Manager (850-526-2040)


North East Elevation

☉ 232°SW (T) ☉ 30°46'45"N, 85°9'19"W ±68ft ▲ 142ft



07 Nov 2025, 08:06:05

☉ 331°NW (T) ☉ 30°46'45"N, 85°9'19"W ±131ft ▲ 1231ft

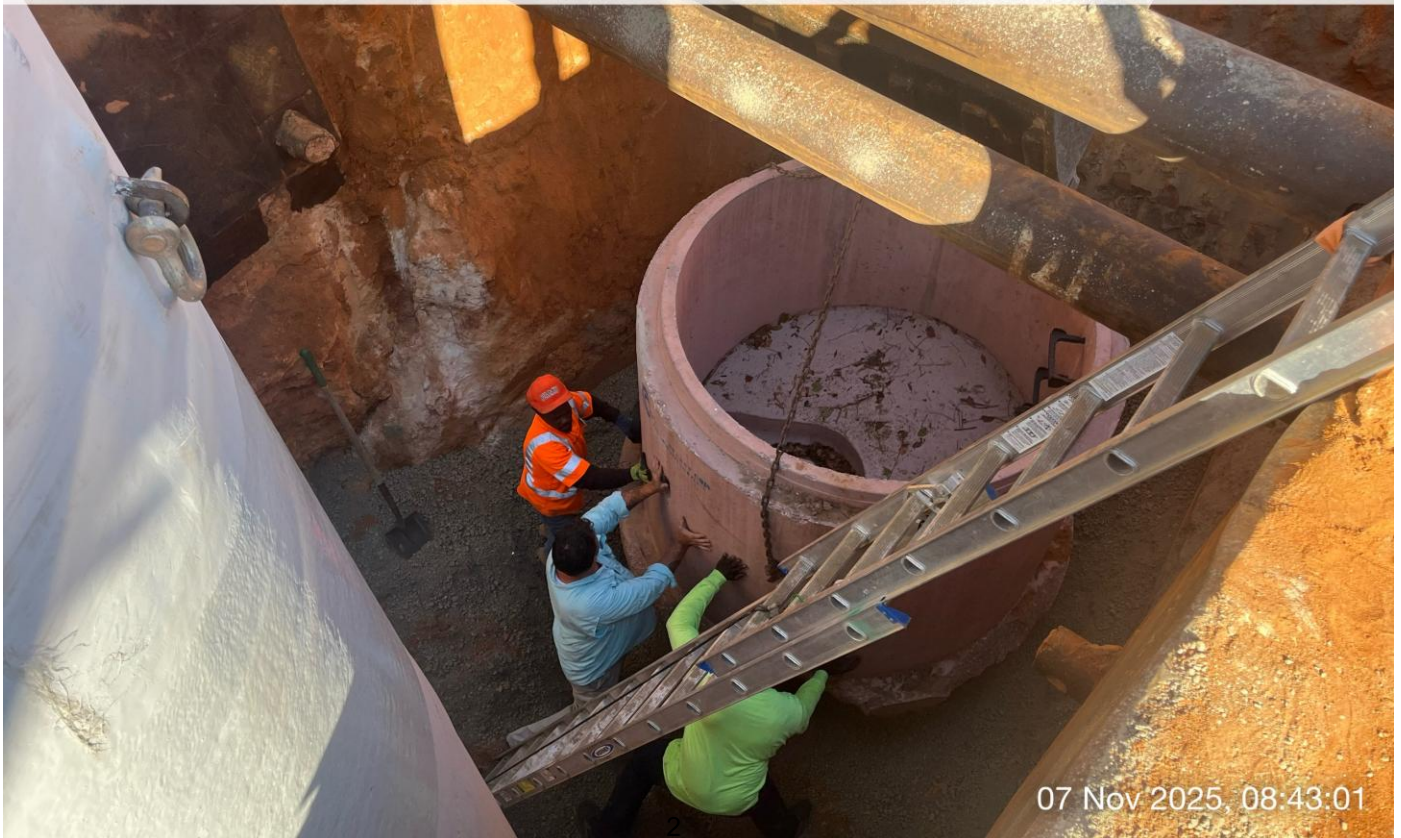

07 Nov 2025, 08:43:01

East Elevation

☉ 273°W (T) ☉ 30°46'45"N, 85°9'19"W ±9ft ▲ 144ft



☉ 151 SE (T) ☉ 30 46 44 N, 85 9 18 W ±83ft ▲ 158ft

