

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 1/12/2026
For Project: Blue Springs Road Sewer Extensions Phase 1
NWFWMD Const. Grant Agreement No. 17-061
Contractor: L & K Contracting, Inc.
Designer: Alday-Howell Engineering
Notice to Proceed: 9/27/2022
Award Date: 6/29/2022



Substantial Completion: 6/18/2025 Final Completion: 7/18/2025

The report is for the week of: Monday, 1/5/2026 thru Sunday, 1/11/2026

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- No work at contractor's option.

Tuesday- Performed low pressure test.

Wednesday- Performed low pressure test.

Thursday- Performed low pressure test.

Friday- Performed low pressure test.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues: Added 60 weather days and 10 holidays to correct time.

Percent Project Complete:	77%	Time Remaining (%):	-26%	
Invoiced to Date:	\$3,786,915.31	Weather days to date:	114	
Original Contract Amount:	\$5,347,467.37	Holiday days granted:	86	
Change Order Amount Approved:	\$85,681.90	Actual Days:	1203	
Contract Time Approved:	495	Days used with deduct:	1003	
Remaining:	\$1,646,233.96	Remaining to SC:	-208	
Days to Substantial Completion:	795 Original SC:	300	Remaining to FC:	-178
Days to Final Completion:	825 Original FC:	330		

A handwritten signature in blue ink that reads 'Robin G. Besczezynski'.

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)


East Elevation

⌚ 292°W (T) ● 30°47'2"N, 85°10'25"W ±13ft ▲ 150ft



South East Elevation

⌚ 293°NW (T) ● 30°47'2"N, 85°10'25"W ±13ft ▲ 160ft

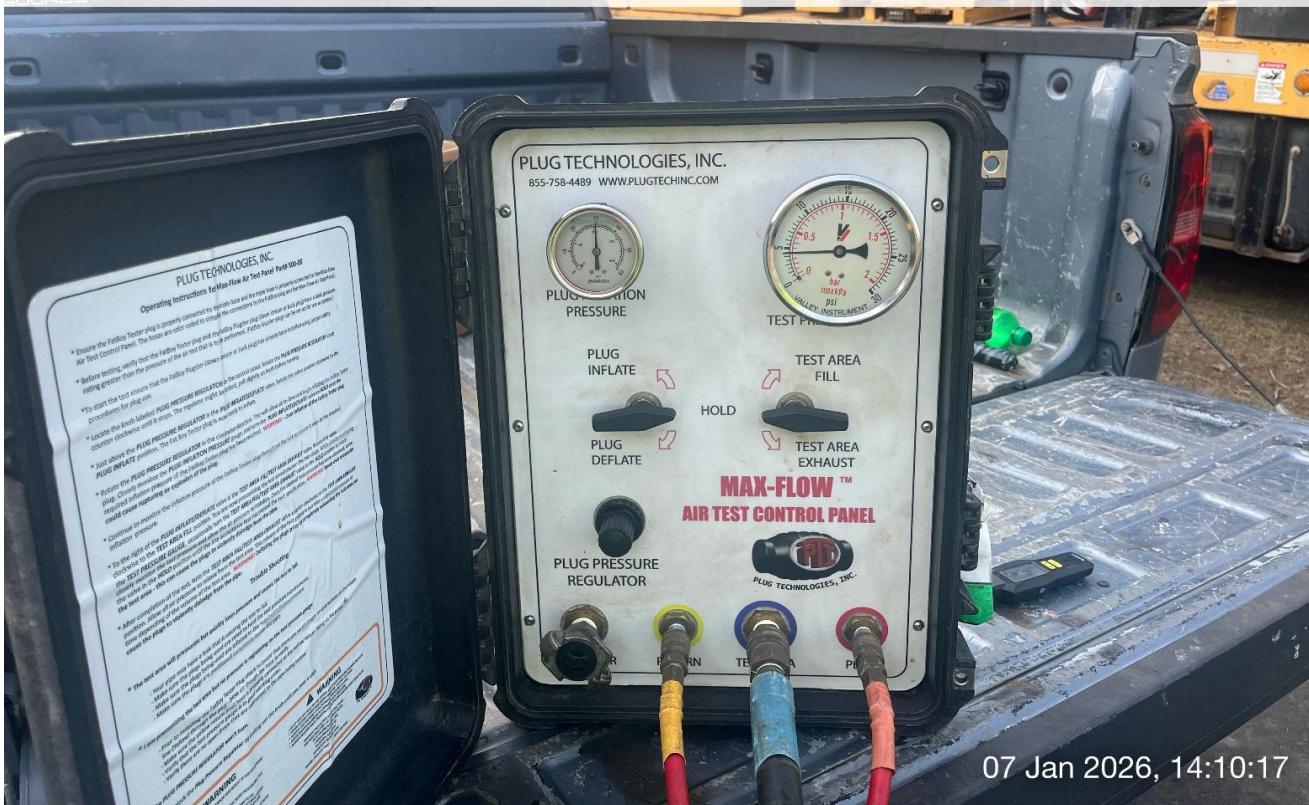

07 Jan 2026, 14:10:17

South West Elevation

⌚ 56°NE (T) ● 30°47'2"N, 85°10'25"W ±13ft ▲ 157ft



East Elevation

⌚ 265°W (T) ● 30°47'0"N, 85°10'33"W ±875ft ▲ 147ft

