

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
 Prepared by: Alday-Howell Engineering, Inc.
 Prepared on: 2/1/2026
 For Project: **Indian Springs Sewer Phase 2B**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
 Contractor: Blankenship Contracting, Inc.
 Designer: Alday-Howell Engineering Inspector: Dwayne Josey (850) 258-3386
 Notice to Proceed: 8/1/2023 Award Date: 1/24/2023



Substantial Completion: 12/10/2025 Final Completion: 2/8/2026

The report is for the week of: Monday, 1/26/2026 thru Sunday, 2/1/2026

The contractor performed the following operations this week. Sub work is noted in parenthesis:

- Monday-** Performed hydrostatic test on 913 lf of new force main at Wayside lift station.
- Tuesday-** Put new force main in service at Wayside lift station.
- Wednesday-** Repaired broken sewer line at 5091 Lake Bluff. Repaired sidewalk on north side of hwy. 90 over new force main for Wayside lift station.
- Thursday-** Removed bypass hoses and cleaned construction area at Wayside lift station.
- Friday-** Clean construction area at Wayside lift station.
- Saturday-** No work at contractor's option.
- Sunday-** No work at contractor's option.


Engineer's remarks/Pending issues:

Percent Project Complete:	81%	Time Remaining (%):	-7%	
Invoiced to Date:	\$4,822,733.50	Weather days to date:	30	
Original Contract Amount:	\$6,377,639.99	Holiday days granted:	58	
Change Order Amount Approved:	\$262,722.00	Actual Days:	916	
Contract Time Approved:	474	Days used with deduct:	828	
Remaining:	\$1,817,628.49			
Days to Substantial Completion:	774 Original SC:	300	Remaining to SC:	-54
Days to Final Completion:	834 Original FC:	360	Remaining to FC:	6

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)

East Elevation

☉ 148°SE (T) ● 30.755893, -85.195989 ±3m ▲ 0m

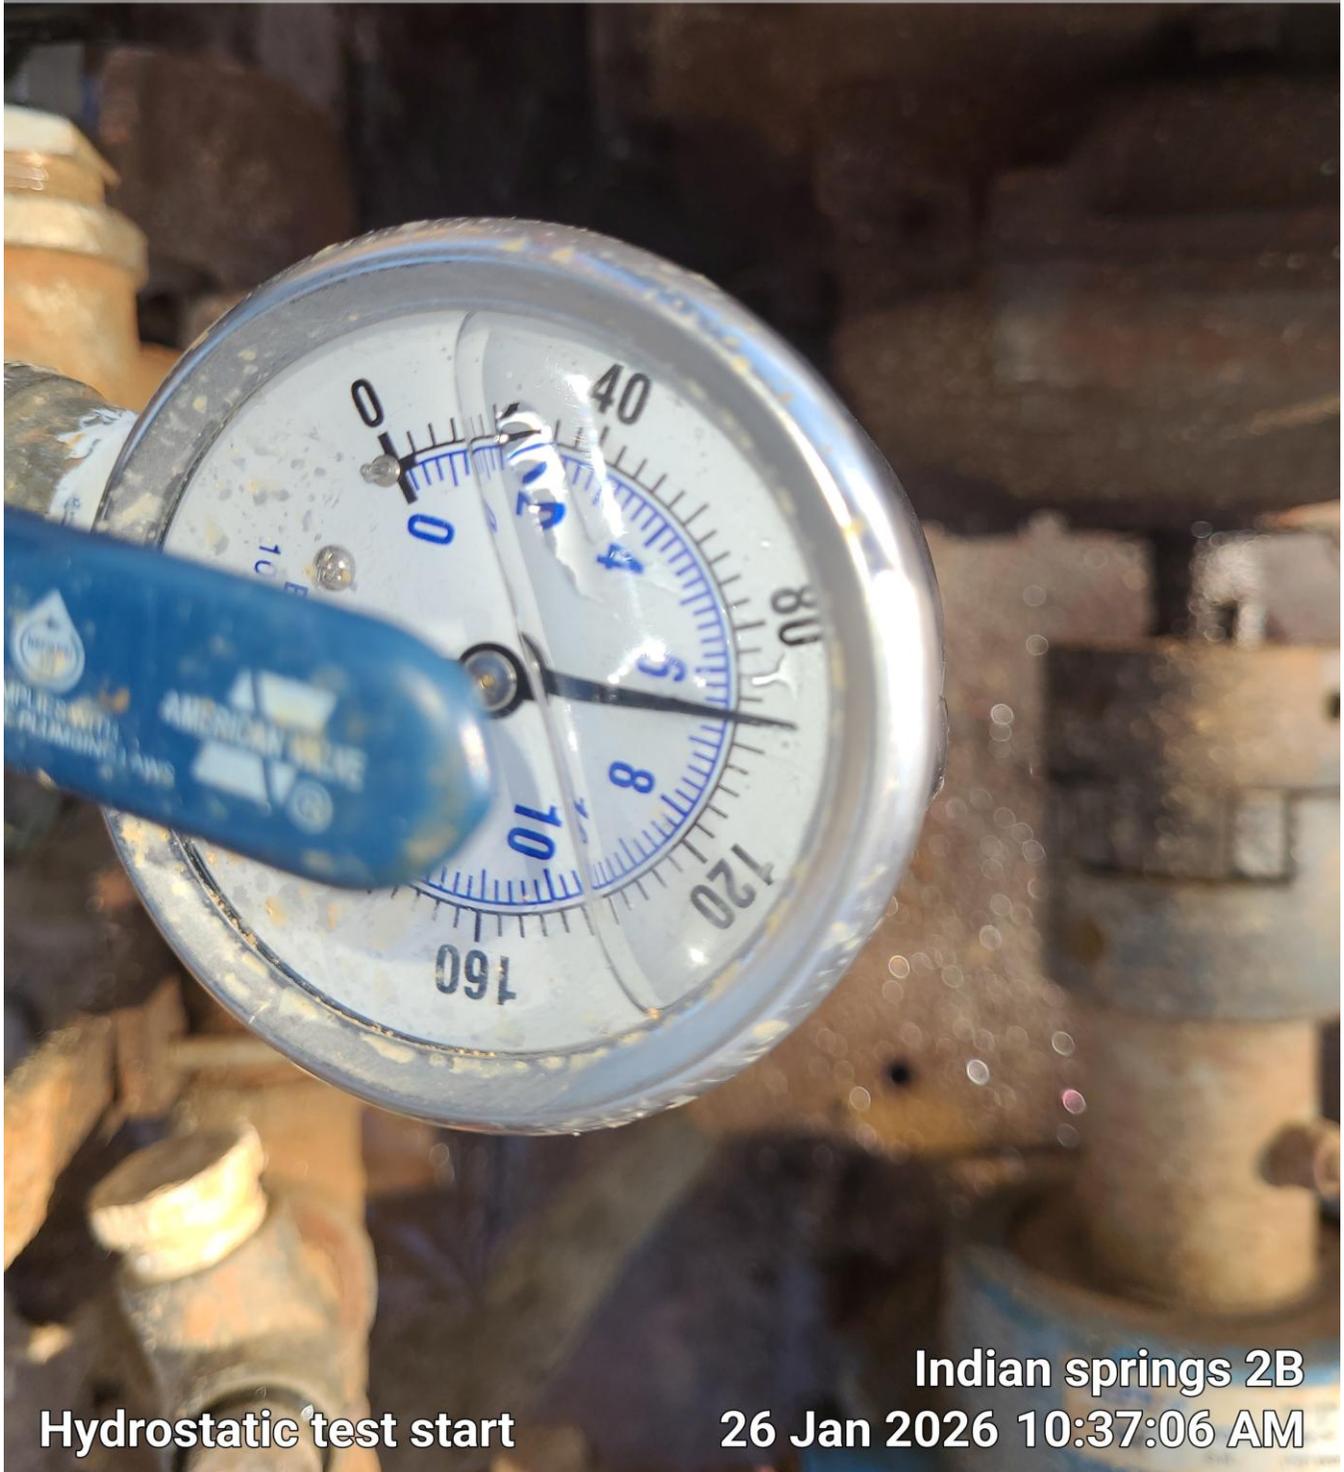

Hydrostatic test start

Indian springs 2B
26 Jan 2026 10:37:06 AM

East Elevation

☉ 235°SW (T) • 30.755861, -85.196019 ±3m ▲ 0m



Hydrostatic test end

Indian springs 2B
26 Jan 2026 12:37:09 PM

South Elevation

☉ 344°NW (T) • 30.773846, -85.169456 ±5m ▲ 18m



Sewer line cut

Indian springs 2B
28 Jan 2026 10:08:04 AM

North Elevation

☉ 268°W (T) ● 30.758298, -85.196389 ±3m ▲ 7m



Repair sidewalk

Indian springs 2B
29 Jan 2026 2:02:47 PM
