

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
 Prepared by: Alday-Howell Engineering, Inc.
 Prepared on: 2/15/2026
 For Project: **Indian Springs Sewer Phase 2B**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
 Contractor: Blankenship Contracting, Inc.
 Designer: Alday-Howell Engineering Inspector: Dwayne Josey (850) 258-3386
 Notice to Proceed: 8/1/2023 Award Date: 1/24/2023



Substantial Completion: 12/12/2025 Final Completion: 2/10/2026

The report is for the week of: Monday, 2/9/2026 thru Sunday, 2/15/2026

The contractor performed the following operations this week. Sub work is noted in parenthesis:

- Monday-** Performed exfiltration test on manholes 1025, 1029, and 1031 on Appalachee Trl.
- Tuesday-** Performed exfiltration test on manholes on Appalachee Trl. Put in service 2 residence and abandon 2 tankes. Begin forming for concrete pad at Wayside lift station.
- Wednesday-** Performed exfiltration test on manholes. Performed walk through on right of way on Appalachee Trl.
- Thursday-** Performed exfiltration test on 1 man hole. Performed on lot walk through on Appalachee Trl.
- Friday-** Performed walk through at Wayside lift station. Forming for concrete pad at Wayside lift station.
- Saturday-** No work at contractor's option.
- Sunday-** No work due to rain. Rain day granted.


Engineer's remarks/Pending issues:

Percent Project Complete:	81%	Time Remaining (%):	-9%
Invoiced to Date:	\$4,822,733.50	Weather days to date:	32
Original Contract Amount:	\$6,377,639.99	Holiday days granted:	58
Change Order Amount Approved:	\$262,722.00	Actual Days:	930
Contract Time Approved:	474	Days used with deduct:	840
Remaining:	\$1,817,628.49	Days to Substantial Completion:	774 Original SC: 300 Remaining to SC: -66
Days to Substantial Completion:	774 Original SC: 300	Days to Final Completion:	834 Original FC: 360 Remaining to FC: -6


 Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)

East Elevation

☉ 127°SE (T) • 30.769826, -85.165645 ±3m ▲ 21m

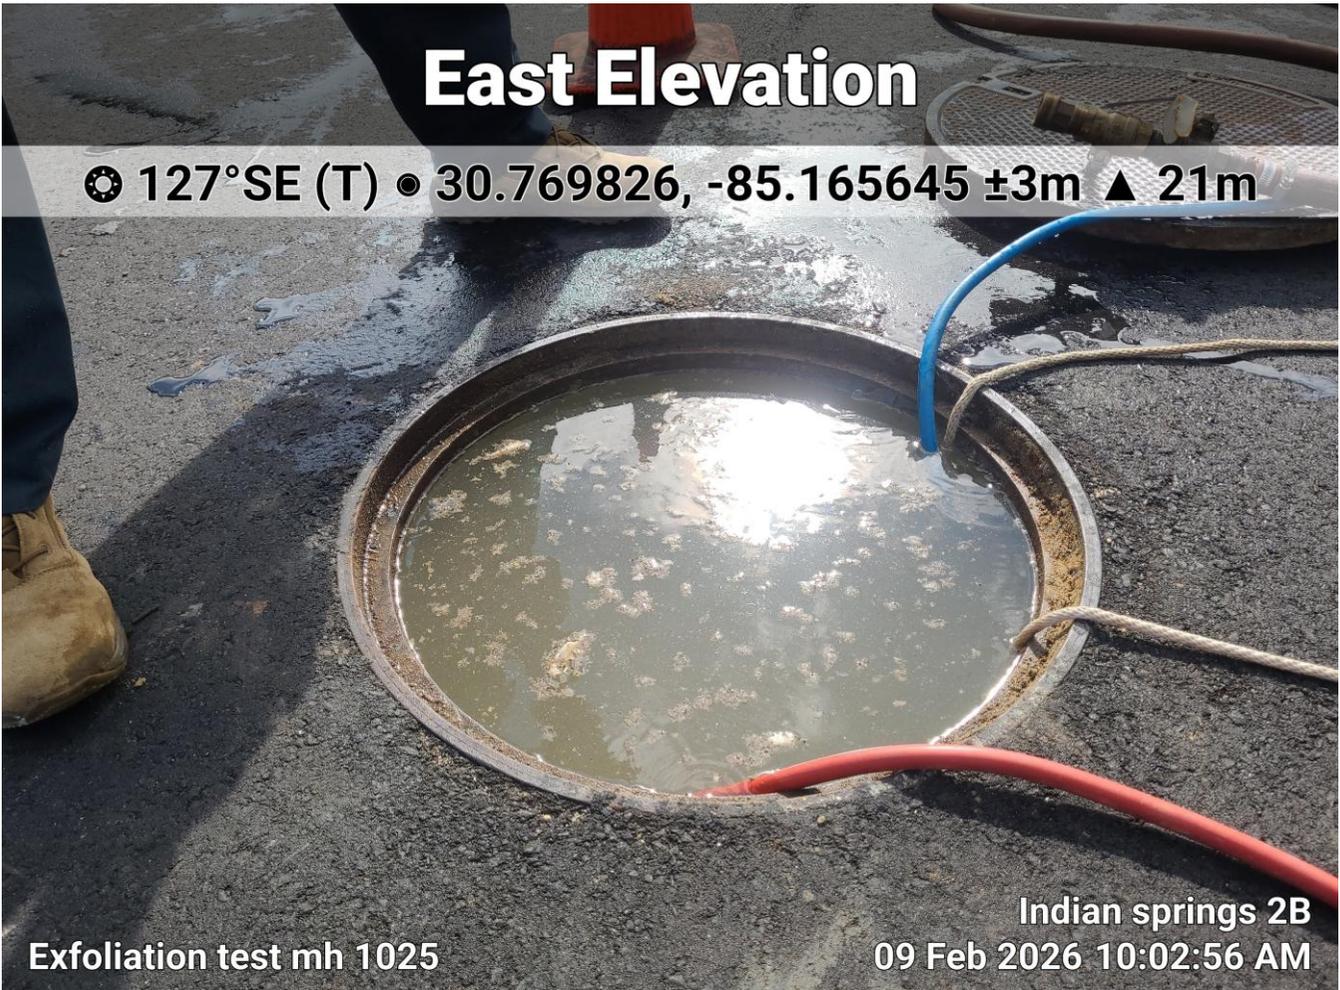

Exfoliation test mh 1025

Indian springs 2B
09 Feb 2026 10:02:56 AM

East Elevation

☉ 239°SW (T) • 30.755742, -85.195809 ±3m ▲ 0m



Concrete pad. Wayside

Indian springs phase 2B
11 Feb 2026 6:46:06 AM

South West

☉ 238°SW (T) ☉ 30°46'24"N, 85°10'4"W ±114ft ▲ 141ft



