

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
 Prepared by: Alday-Howell Engineering, Inc.
 Prepared on: 4/12/2026
 For Project: **Indian Springs Sewer Phase 2B**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
 Contractor: Blankenship Contracting, Inc.
 Designer: Alday-Howell Engineering Inspector: Dwayne Josey (850) 258-3386
 Notice to Proceed: 8/1/2023 Award Date: 1/24/2023



Substantial Completion: 1/16/2026

Final Completion: 3/17/2026

The report is for the week of: Monday, 4/6/2026

thru Sunday, 4/12/2026

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Worked on completing punch list.

Tuesday- Worked on completing punch list.

Wednesday- Worked on completing punch list.

Thursday- Worked on completing punch list.

Friday- Worked on completing punch list.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.


Engineer's remarks/Pending issues:

Percent Project Complete:	84%	Time Remaining (%):	-11%	
Invoiced to Date:	\$5,001,931.28	Weather days to date:	34	
Original Contract Amount:	\$6,377,639.99	Holiday days granted:	61	
Change Order Amount Approved:	\$262,722.00	Actual Days:	986	
Contract Time Approved:	504	Days used with deduct:	891	
Remaining:	\$1,638,430.71			
Days to Substantial Completion:	804 Original SC:	300	Remaining to SC:	-87
Days to Final Completion:	864 Original FC:	360	Remaining to FC:	-27

Approved: Robin G. Besczezynski, Utility Project Manager (850-526-2040)

South Elevation

☉ 352°N (T) ● 30°45'20"N, 85°11'45"W ±3m ▲ 28m (MSL)

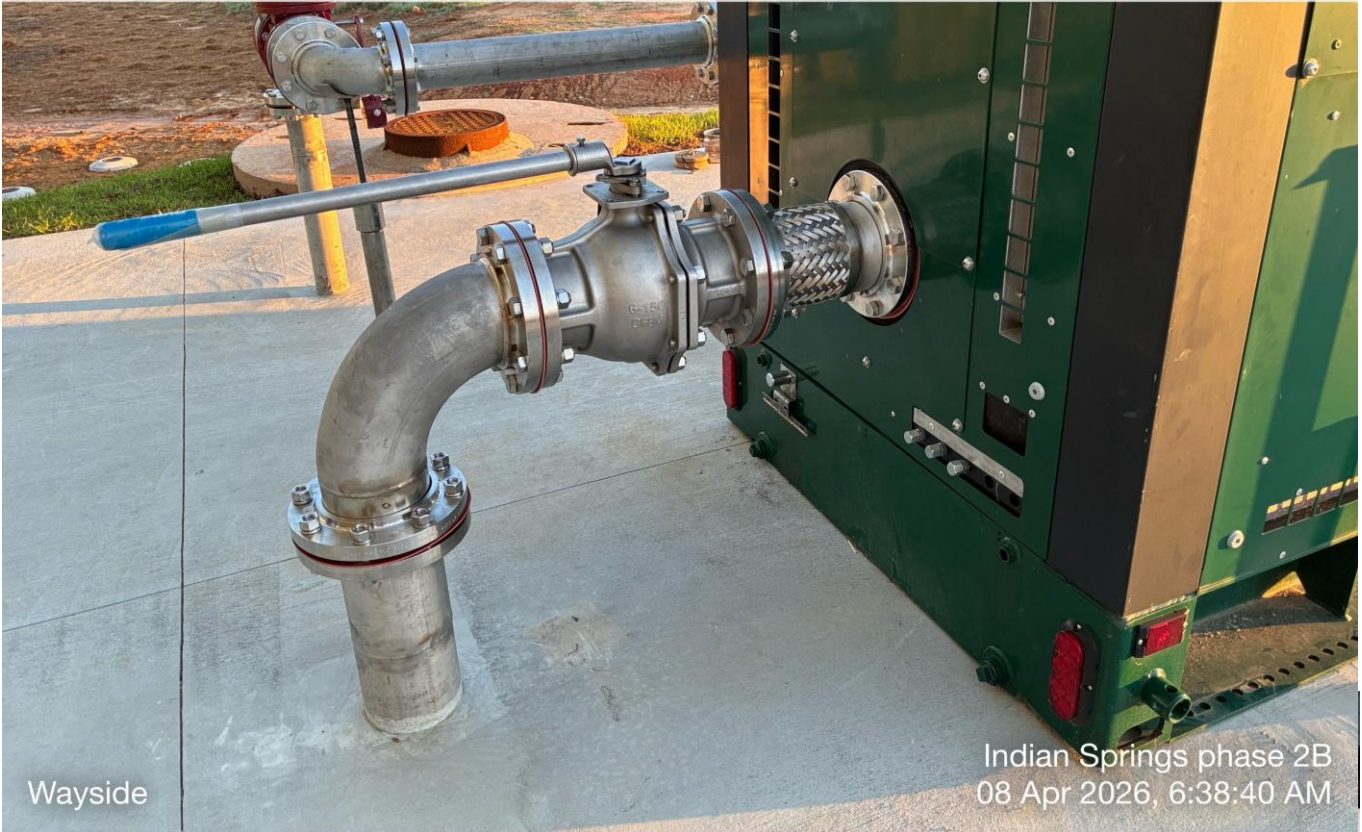

Wayside

Indian Springs phase 2B
08 Apr 2026, 6:38:40 AM

☉ 328°NW (T) ● 30°46'14"N, 85°10'00"W ±4m ▲ 52m (MSL)



Sod 2821 Appalachian Trl

Indian Springs phase 2B
08 Apr 2026, 10:22:13 AM

East Elevation

☉ 275°W (T) ● 30°45'30"N, 85°11'47"W ±2m ▲ 25m (MSL)



Wayside

Indian Springs phase 2B
10 Apr 2026, 10:23:11 AM
