

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
 Prepared by: Alday-Howell Engineering, Inc.
 Prepared on: 4/19/2026
 For Project: **Indian Springs Sewer Phase 2B**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
 Contractor: Blankenship Contracting, Inc.
 Designer: Alday-Howell Engineering Inspector: Dwayne Josey (850) 258-3386
 Notice to Proceed: 8/1/2023 Award Date: 1/24/2023



Substantial Completion: 1/16/2026 Final Completion: 3/17/2026

The report is for the week of: Monday, 4/13/2026 thru Sunday, 4/19/2026

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Worked on completing punch list.

Tuesday- No work at contractor's option.

Wednesday- No work at contractor's option.

Thursday- No work at contractor's option.

Friday- Worked on completing punch list.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues:

Percent Project Complete:	84%	Time Remaining (%):	-12%
Invoiced to Date:	\$5,001,931.28	Weather days to date:	34
Original Contract Amount:	\$6,377,639.99	Holiday days granted:	61
Change Order Amount Approved:	\$262,722.00	Actual Days:	993
Contract Time Approved:	504	Days used with deduct:	898
Remaining:	\$1,638,430.71	Days to Substantial Completion:	804 Original SC: 300 Remaining to SC: -94
Days to Substantial Completion:	804 Original SC: 300	Days to Final Completion:	864 Original FC: 360 Remaining to FC: -34

Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)



North Elevation

☉ 169°S (T) ☉ 30°45'21"N, 85°11'45"W ±6m ▲ 28m (MSL)




Wayside

Indian Springs phase 2B
13 Apr 2026, 8:37:15 AM

East Elevation

☉ 283°W (T) ☉ 30°45'21"N, 85°11'45"W ±8m ▲ 24m (MSL)

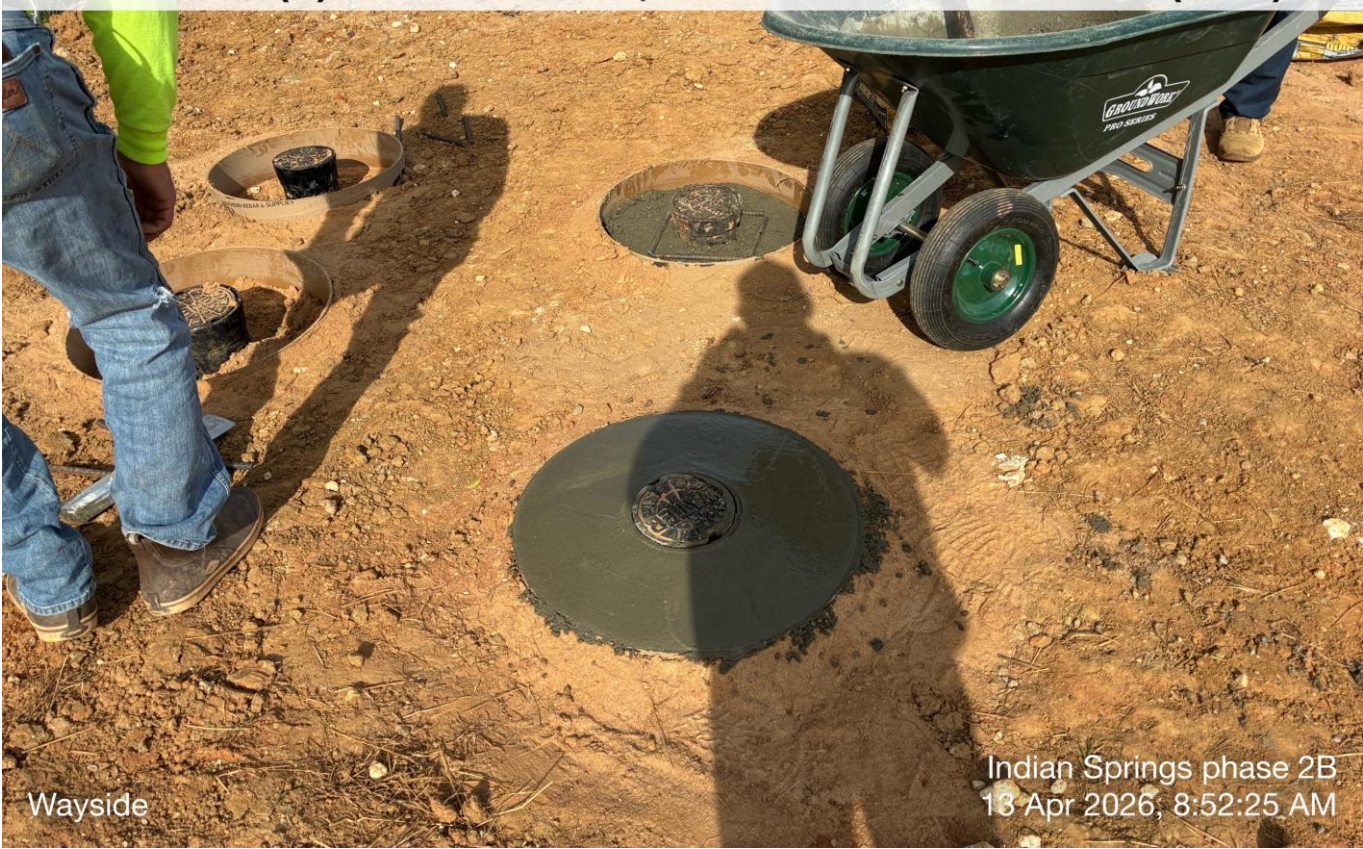

Wayside

Indian Springs phase 2B
13 Apr 2026, 8:52:25 AM

South East Elevation

☀ 314°NW (T) ☉ 30°45'21"N, 85°11'45"W ±4m ▲ 26m (MSL)



Wayside

Indian Springs phase 2B
13 Apr 2026, 9:40:45 AM
