

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
 Prepared by: Alday-Howell Engineering, Inc.
 Prepared on: 6/7/2026
 For Project: **Indian Springs Sewer Phase 2D**
NFWMD Const. Grant Agreement No. 20-036 AHE # 23-012
 Contractor: Blankenship Contracting, Inc.
 Designer: Alday-Howell, Engineering Inspector: Dwayne Josey 850-258-3386
 Notice to Proceed: 11/4/2024 Award Date: 12/13/2022



Substantial Completion: 9/14/2026 Final Completion: 11/13/2026

The report is for the week of: Monday, 6/1/2026 thru Sunday, 6/7/2026

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Installed 14 lf of 8" gravity on Oak Dr.

Tuesday- Installed 37 lf of 8" gravity and set manhole 1608 on Oak Dr.

Wednesday- Installed 28 lf of 8" gravity on Oak Dr.

Thursday- Removed asphalt from Oak Dr.

Friday- No work at contractor's option.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues: Percent complete is phase specific, invoiced is per project.

Percent Project Complete:	13%	Time Remaining (%):	16%
Invoiced to Date:	\$3,891,523.46	Weather days to date:	35
Original Contract Amount:	\$6,168,668.47	Holiday days granted:	44
Change Order Amount Approved:	\$2,820,626.04	Actual Days:	581
Contract Time Approved:	300	Days used with deduct:	502
Remaining:	\$5,097,771.05	Days to Substantial Completion:	600
Days to Substantial Completion:	600	Original SC:	300
Days to Final Completion:	660	Original FC:	360
		Remaining to SC:	98
		Remaining to FC:	158

Completed on lot connection: 0
Completed septic tank abandoned: 0


 Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)

East Elevation

☉ 281°W (T) ☉ 30°46'22"N, 85°9'39"W ±5m ▲ 48m (MSL)



☉ 281°W (T) ☉ 30°46'22"N, 85°9'39"W ±4m ▲ 57m (MSL)



North East Elevation

☀ 234°SW (T) ● 30°46'22"N, 85°9'39"W ±5m ▲ 51m (MSL)




M H 1608

Indian Springs phase2D
02 Jun 2026, 1:06:56 PM

South East Elevation

☉ 318°NW (T) ☉ 30°46'22"N, 85°9'39"W ±4m ▲ 49m (MSL)

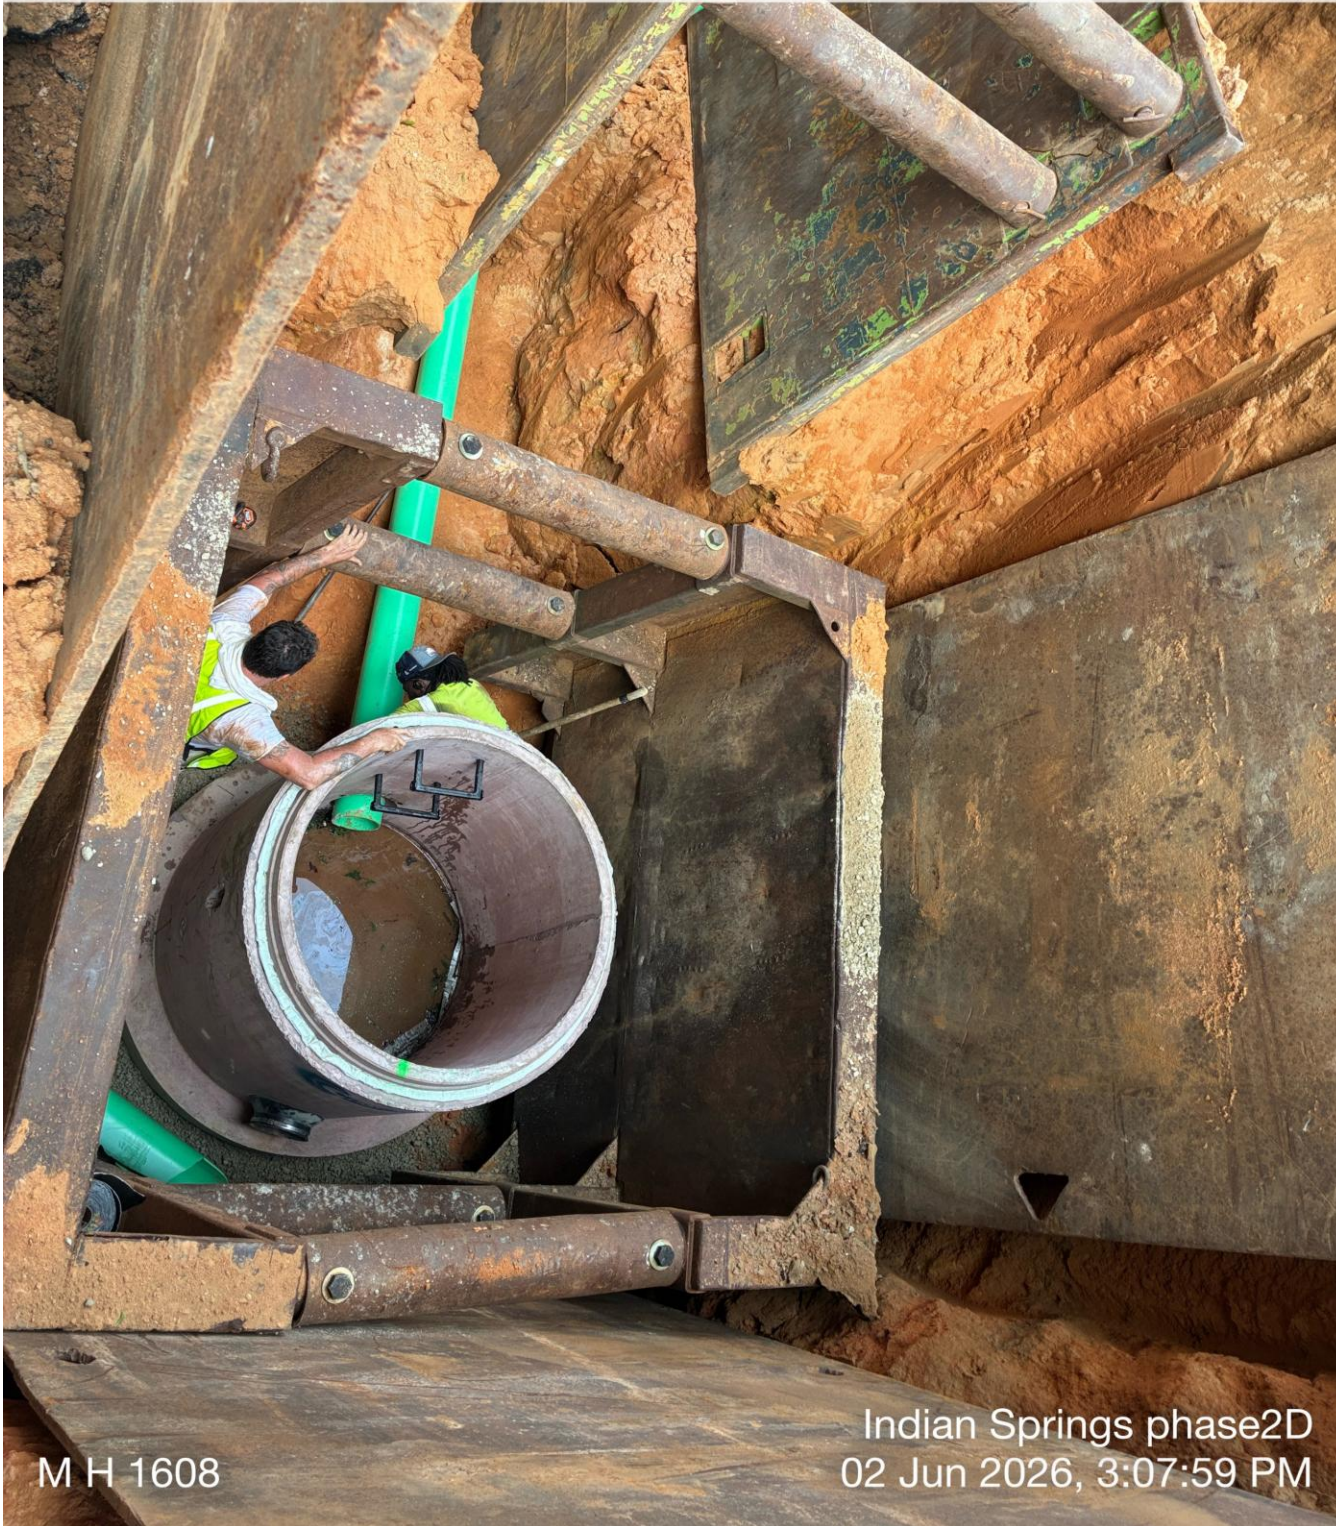

M H 1608

Indian Springs phase2D
02 Jun 2026, 3:07:59 PM
